


New Henry Clay High School

➤ Completed/Work in Progress:

- Geothermal well field drilling at the south end of the site is complete.
- KAWC installation of main waterline is complete.
- ICF and CIP concrete formwork placing and pouring, and the installation of IFAs at ICF walls is in progress.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are in progress.
- Steel erection is underway in areas A, B and C.
- Area D hollowcore and joist erection is complete.
- Above ceiling MEP installation is in progress at areas A,B and C.
- Installation of Stairs A, B and C is complete.
- West driveway retaining wall construction is in progress.
- Interior metal stud wall framing in progress at Area A Level 1.

➤ Upcoming Look Ahead:

- Continue hauling in fill materials and continue site grading.
- Continue sanitary piping and manholes.
- Continue with ICF and CIP concrete walls.
- Continue laying CMU walls.
- Continue with under-slab plumbing and electrical.
- Continue pouring concrete slabs on grade.
- Continue installing IFAs and hollow metal frames.
- Continue with steel erection.
- Continue with above ceiling MEP installation.
- Continue retaining wall construction.

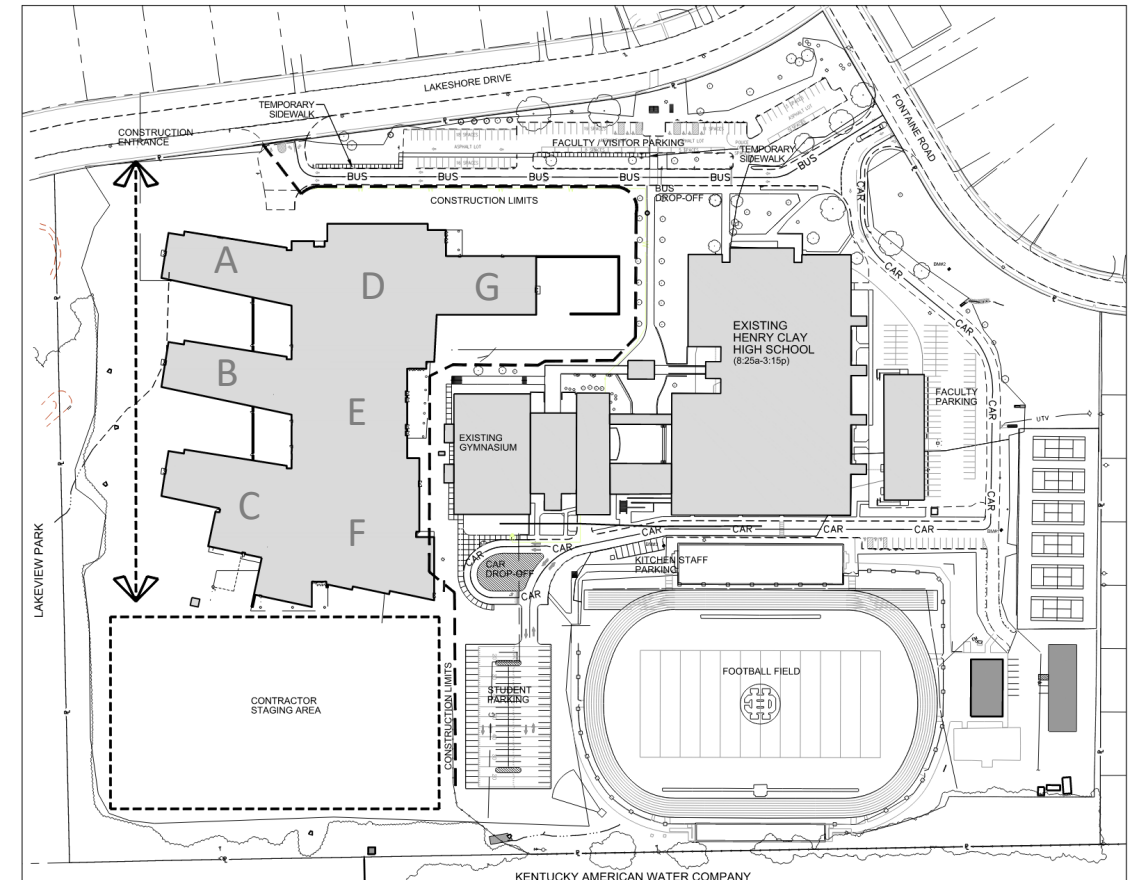

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.


New Henry Clay High School

Area A (Classroom Wing) Levels 1 & 2: Metal Stud Wall Framing and Installation of Hollow Metal Frames in Progress



New Henry Clay High School

Area A (Classroom Wing): Level 3 Steel Erection & Above Ceiling MEP in Progress

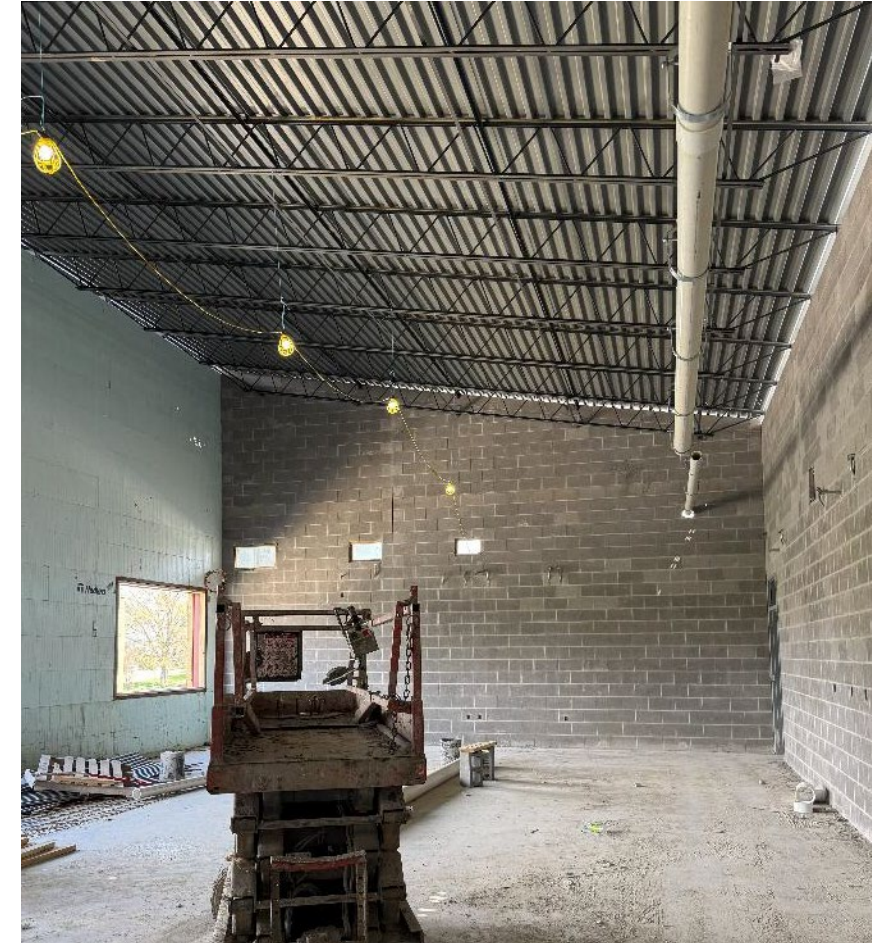

Week Ending April 03, 2026

New Henry Clay High School

Level 2 North-South Corridor: Steel Erection for Level 3 Floor Slab, ICF, CMU, and Hollow Metal Frame Installation Underway



New Henry Clay High School

Level 2 North-South Corridor: ICF, CMU, and Hollow Metal Frame Installation Underway



Week Ending April 03, 2026


New Henry Clay High School

Left: Area B (Classroom Wing): Level 3 CMU and Hollow Metal Frame Installation is Underway
Right: Area C (Classroom Wing): Level 2 CMU and Hollow Metal Frame Installation is Underway



New Henry Clay High School


Area D (Multi-Purpose Room): Storm Shelter ICF is Complete and Storm Shelter is Enclosed

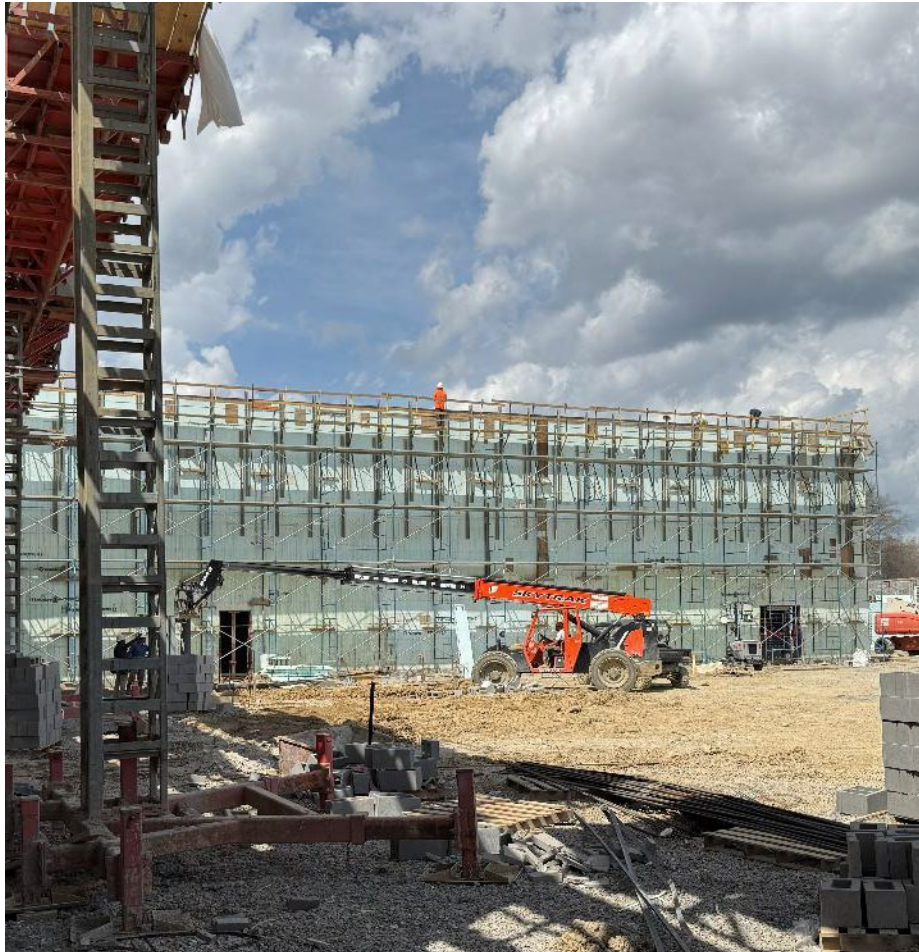

Week Ending April 03, 2026

New Henry Clay High School

Area C (Cafeteria & Classroom Wing): Stair C Installation is Complete

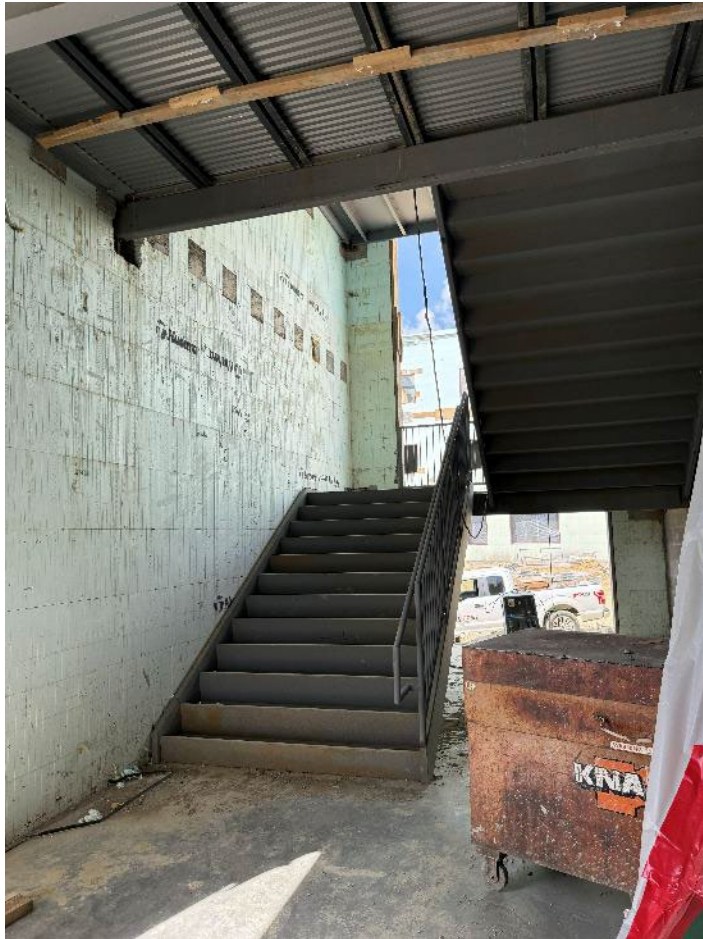

Week Ending April 03, 2026
