

Measure BB Bond

21st Century Classroom Improvements
December 2025




CUMMING
GROUP

//////////////////// BUILDING VALUE THROUGH EXPERTISE



HLPUSD MEASURE BB - SUMMARY

SCHOOLS IN PROGRESS

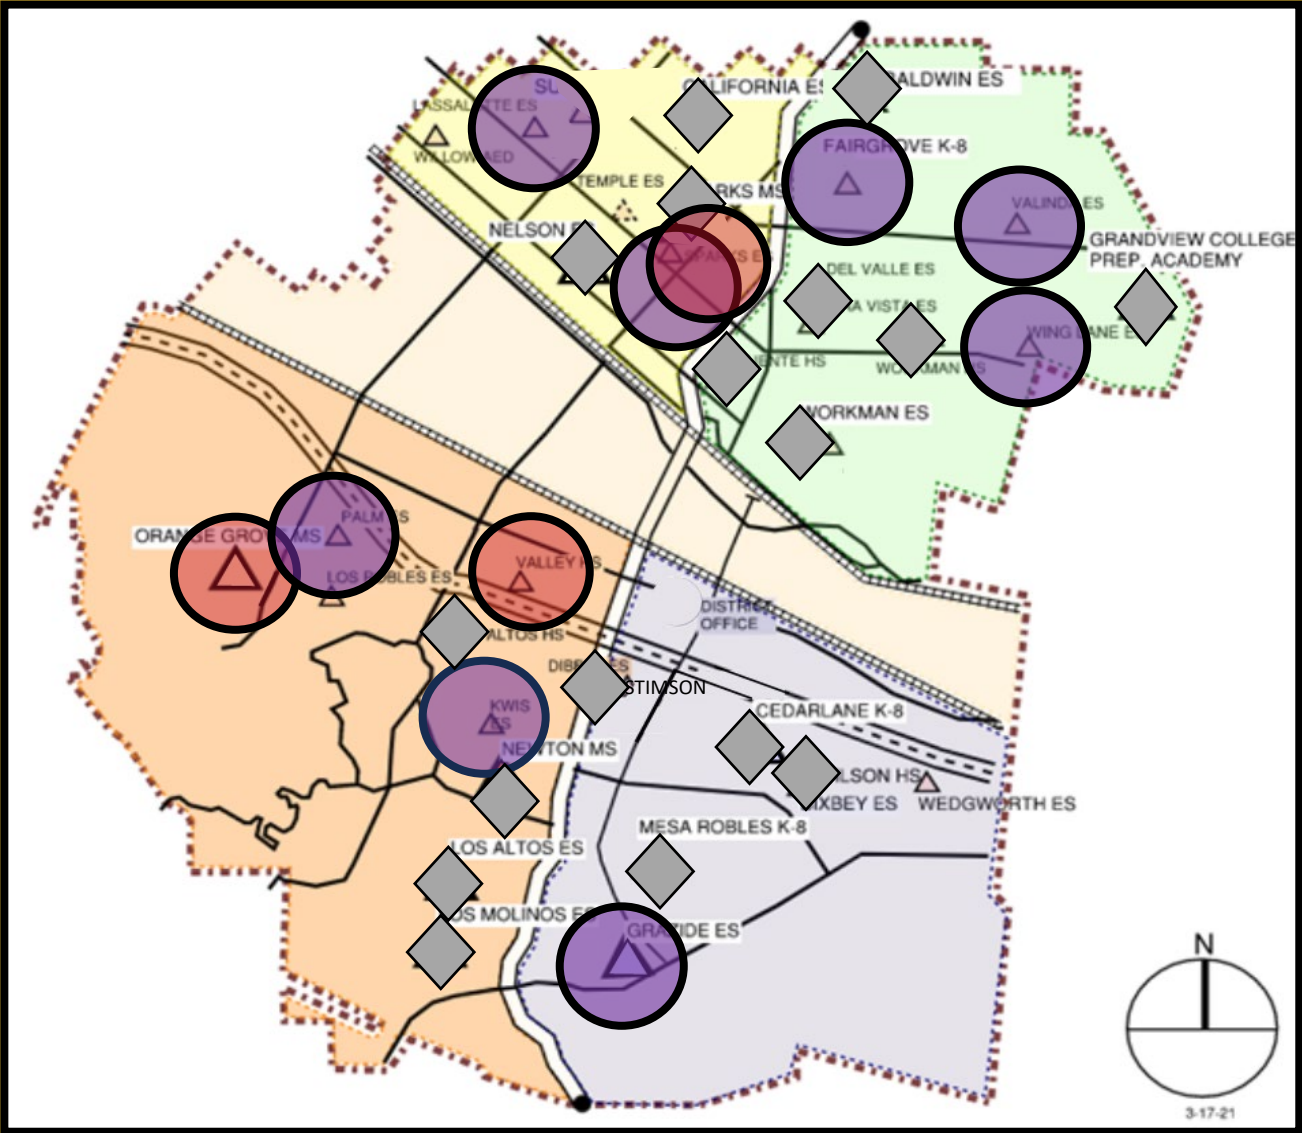

IN PROGRESS CONSTRUCTION

- Fairgrove K-8
- Grazide ES
- Kwis ES
- Lassalette ES
- Sparks ES
- Valinda ES
- Wing Lane ES
- PENDING START DATE
- Palm ES

IN DESIGN

- Orange Grove MS
- Sparks MS II
- Valley Alternative School

COMPLETED

- Baldwin ES
- California ES
- Cedarlane K-8
- Grandview MS
- La Puente HS
- Los Altos ES
- Los Altos HS
- Los Molinos ES
- Mesa Robles K-8
- Nelson ES
- Newton MS
- Sierra Vista MS
- Sparks MS
- Stimson EC
- Wilson HS
- Workman ES
- Workman HS

PROJECT STATUS

School	Design Phase and Pre Bid	Ready to start construction	Under Construction	Close Out Phase	Completed	Original Competition Date	Anticipated phase completion date
Sparks MS II Expansion	X				0%		15-Apr-27
Valley Alternative School	X				0%	NA	12-Jun-26
Orange Grove	X				0%	NA	10-Jul-26
Palm ES		X			0%	2-Mar-26	30-Jun-26
Valinda K-8			X		70%	31-Dec-25	2-Mar-26
Sparks ES			X		75%	6-Feb-26	6-Feb-26
Wing Lane ES			X		60%	6-Feb-26	2-Mar-26
Sierra Vista MS				X	98%	3-Oct-26	1-Nov-25
Kwis ES			X		95%	10-Oct-26	31-Jan-26
Lassalette			X		90%	3-Oct-25	1-Jan-26
Fairgrove Academy			X		57%	5-Dec-26	1-Mar-26
Baldwin ES				X	98%	7-Jul-25	1-Aug-25
California ES				X	98%	15-Sep-25	1-Aug-25
Grazide ES			X		90%	31-Jan-26	31-Jan-26
Los Molinos ES				X	98%	31-Jul-25	7-Aug-25
Nelson ES					X		Completed
Los Altos ES					X		Completed
Workman ES					X		Completed
Cedarlane K8					X		Completed
Newton MS					X		Completed
Sparks MS					X		Completed
Grandview K8					X		Completed
La Puente High					X		Completed
Workman High					X		Completed
Los Altos High					X		Completed
Wilson High					X		Completed

Fairgrove K-8

Phase 1 Completed

Phase 2 Under Construction



Grazide Elementary

Substantially Complete



Kwis Elementary

Substantially Complete



Lassalette Elementary

Substantially Complete



Valinda Elementary

Phase 1 Complete

Construction Progress Phase 2



Wing Lane Elementary

Phase 1 Complete

Construction Progress Phase 2





QUESTIONS & ANSWERS
