



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

PROGRESS THIS WEEK:

- Grout Precast Plank – Area C
- Mobilize Masons To Start Level 1 CMU Area B
- Additional Site Grading Playfield Sports Courts

GOALS NEXT 2 WEEKS:

- Continue Main Structure Steel Erection- Area B
- Complete Area A2 Stair Shaft & Elevator Shaft.
- Continue Load Bearing Masonry Area B & C Following Precast Erection







PROJECT HIGHLIGHT THIS WEEK:

- Significant Project Progress & Coordination Through Inclement Weather Events.
- Site Storm & Playfield Work Continues To Progress.

DATE: April 24, 2026

MRCC PROJECT PROGRESS:



MILESTONE CHECKLIST:

- Construction Start – 9/18/25
- Foundations Complete 3/25/26
- Steel Complete
- Enclosed
- MRCC Substantial Completion
- Playfield Completion

Photos or Visual Assets:



Site Grading – Playfield Sports Courts



Storm Structure Installation– South Parking Area



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

DATE: April 24, 2026


MORE PROGRESS PHOTOS:




Precast Grouting Level 1 - Area C



Aerial View of Structural Steel & Precast- Area C

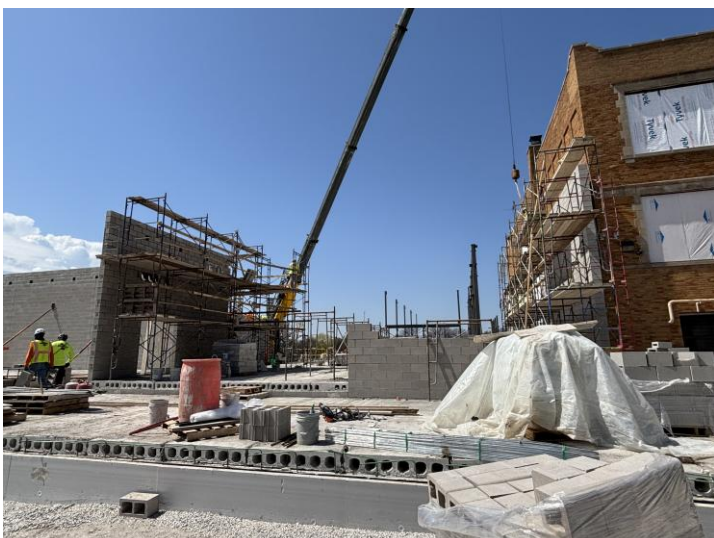

Scaffolding For Masonry On Precast Level 1 – Area B

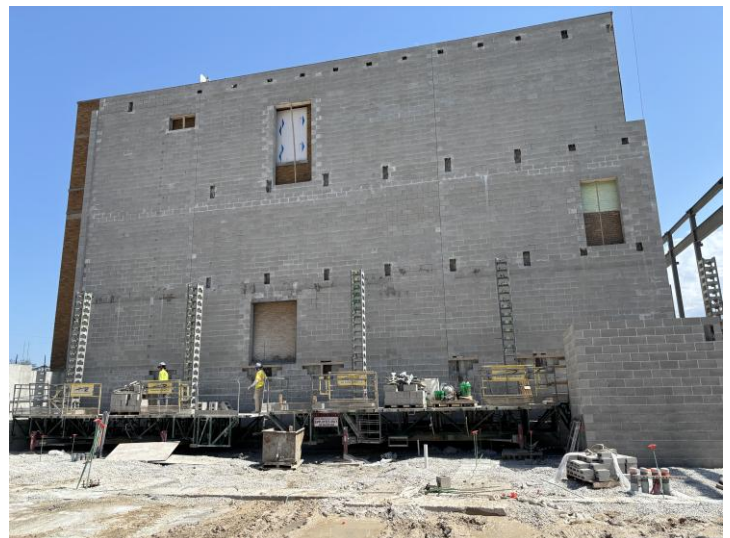

East One-Side Wall Top Out– Area A2
