


Lake Mills High School **EXECUTIVE SUMMARY**

PROVIDED BY FINDORFF

615 Catlin Dr., Lake Mills, WI 53551 04/10/2026

What's New?

Great progress continues on the locker room renovation, and the team is thrilled with how smoothly the project is moving along. All MEPF piping has been successfully cut, capped, and made safe, creating a clean and secure space for upcoming work. The interior locker room walls have been fully demolished, opening things up and allowing the transformation to truly begin. The existing tile flooring has also been removed, clearing the way for the next construction phases. In addition, the layout for the new locker room walls has been completed, providing a clear roadmap for the refreshed space and keeping the momentum strong. The next steps promise even more exciting progress as the space continues to take shape. The locker room slab will be scanned and saw cut to prepare for new installations, followed by the installation of underground plumbing piping to support long-term functionality. Construction will then move forward with the installation of new interior locker room masonry walls, bringing the new design to life. To wrap things up for this phase, slab-on-grade infills will be poured, creating a solid foundation for what's to come. Each milestone brings the project closer to completion, and the team is energized by the steady progress and positive results.

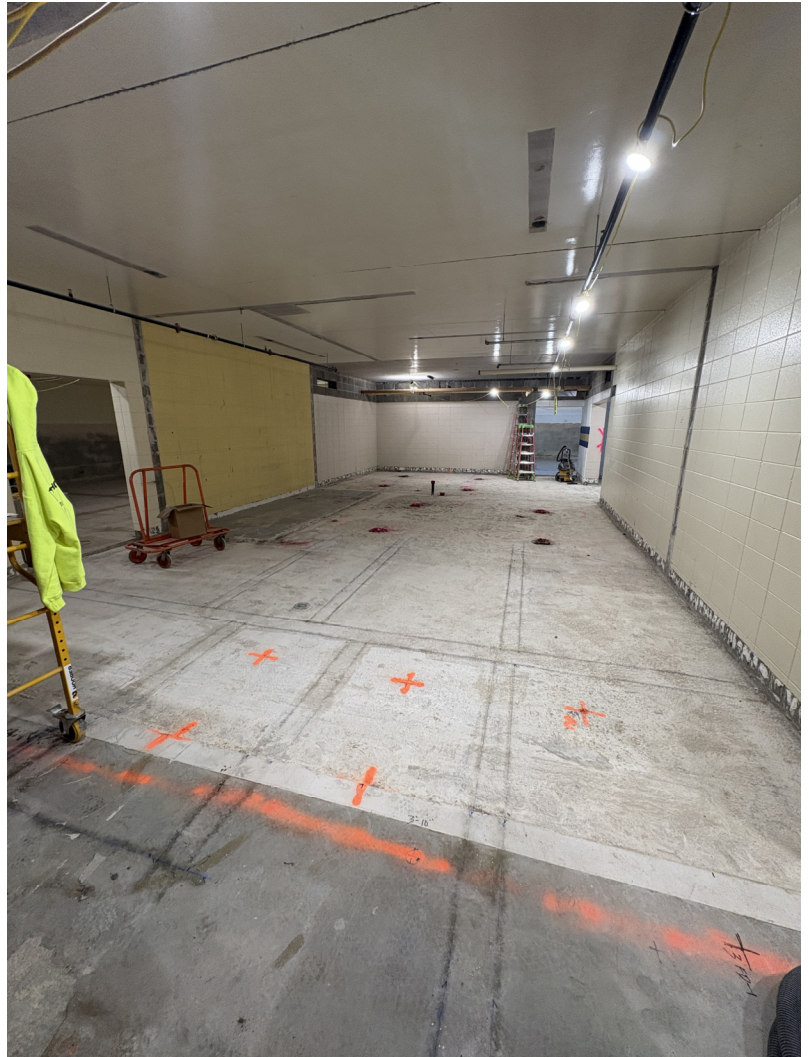

Layout for new walls in the locker room space!

DID YOU KNOW?

Contrary to the belief that demolition is just about destruction, the truth is, that nearly everything that comes down during the process can find a new life. Steel, concrete, wood, and even hardware can be sorted, processed, and repurposed (3) into new construction materials. Not only does this significantly reduce waste, but it also contributes to a more sustainable building cycle. In fact, a study in Canada found that with the waste from construction and demolition, about 75% of the solid waste has value, meaning it can still be reused.

Questions?

Sr Project Manager: Menno Huizer / mhuizer@findorff.com

Project Engineer: Ben Neumann / bneumann@findorff.com

Superintendent: Dave Ritter / dritter@findorff.com

Lake Mills High School **EXECUTIVE SUMMARY**

PROVIDED BY FINDORFF

615 Catlin Dr., Lake Mills, WI 53551 PAGE 2

Completed Work!

- Cut, cap, and make safe all MEPF piping
- Demo of all interior locker room walls
- Demo of existing tile flooring
- Layout of new locker room walls

Work Coming Up

- Scanning and Saw Cutting of the locker room slab
- Underground plumbing piping
- Installation of new interior locker room masonry walls
- Pour locker room slab on grade infills



Top and Bottom: During Demo Work



Post Demo Work



Questions?

Sr Project Manager: Menno Huizer / mhuizer@findorff.com

Project Engineer: Ben Neumann / bneumann@findorff.com

Superintendent: Dave Ritter / dritter@findorff.com
