



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

PROGRESS THIS WEEK:

- Completed Concrete Pour for the Generator Pad – North Side of Area A
- Continued Structural Steel Install – Area B1
- Site Storm Installation Continued – South Side Play Field

GOALS NEXT 2 WEEKS:

- Repour Concrete Slab & Install Shoring for Structural Renovations - Area A1
- Start Fine Grading the Pump Track – South Side of Play Area
- Start 3-Hour CMU Wall Between Area A2 & C2

PROJECT HIGHLIGHT THIS WEEK:

- Received Soil Profile For Haul Off
- Long Span Joist Delivered – Area C2

Photos or Visual Assets:



Site Storm Excavated – South View



Structural Steel Installed – Area A2

DATE: May 22nd, 2026

MRCC PROJECT PROGRESS:



MILESTONE CHECKLIST:

- Construction Start – 9/18/25
- Foundations Complete 3/25/26
- Steel Complete
- Enclosed
- MRCC Substantial Completion
- Playfield Completion



Milwaukee Recreation Community Center & Browning Playfield


CONSTRUCTION UPDATE

DATE: May 22nd, 2026

MORE PROGRESS PHOTOS:



3-Hour CMU Wall – Main Entry

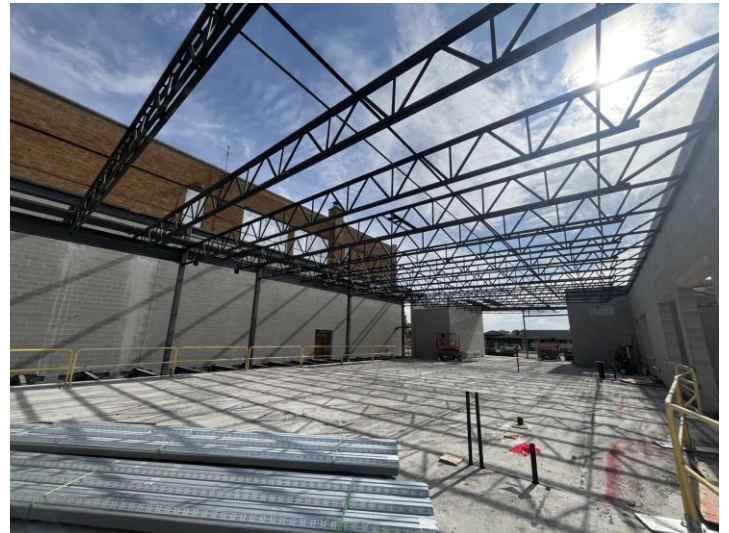

Structural Steel – Area B1



Long Span Joist Delivery – Area C2



Generator Pad – North Side Area A
