


New Henry Clay High School

➤ Completed/Work in Progress:

- Geothermal well field drilling at the south end of the site is complete.
- KAWC installation of main waterline is complete.
- ICF and CIP concrete formwork placing and pouring, and the installation of IFAs at ICF walls is in progress.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are in progress.
- Steel erection is underway in areas A, B and C.
- Area D concrete roof structure is complete.
- Above ceiling MEP installation is in progress at areas A,B and C.
- Installation of Stairs A, B, C, D & E is complete.
- West driveway retaining wall construction is complete.
- Interior metal stud wall & soffit framing in progress at Areas A, B & C.

➤ Upcoming Look Ahead:

- Continue site grading.
- Continue with ICF and CIP concrete walls.
- Continue laying CMU walls.
- Continue with under-slab plumbing and electrical.
- Continue pouring concrete slabs on grade.
- Continue installing IFAs and hollow metal frames.
- Continue with steel erection.
- Continue with above ceiling MEP installation.
- Area A roofing to begin soon.
- Mechanical penthouse construction to begin soon.

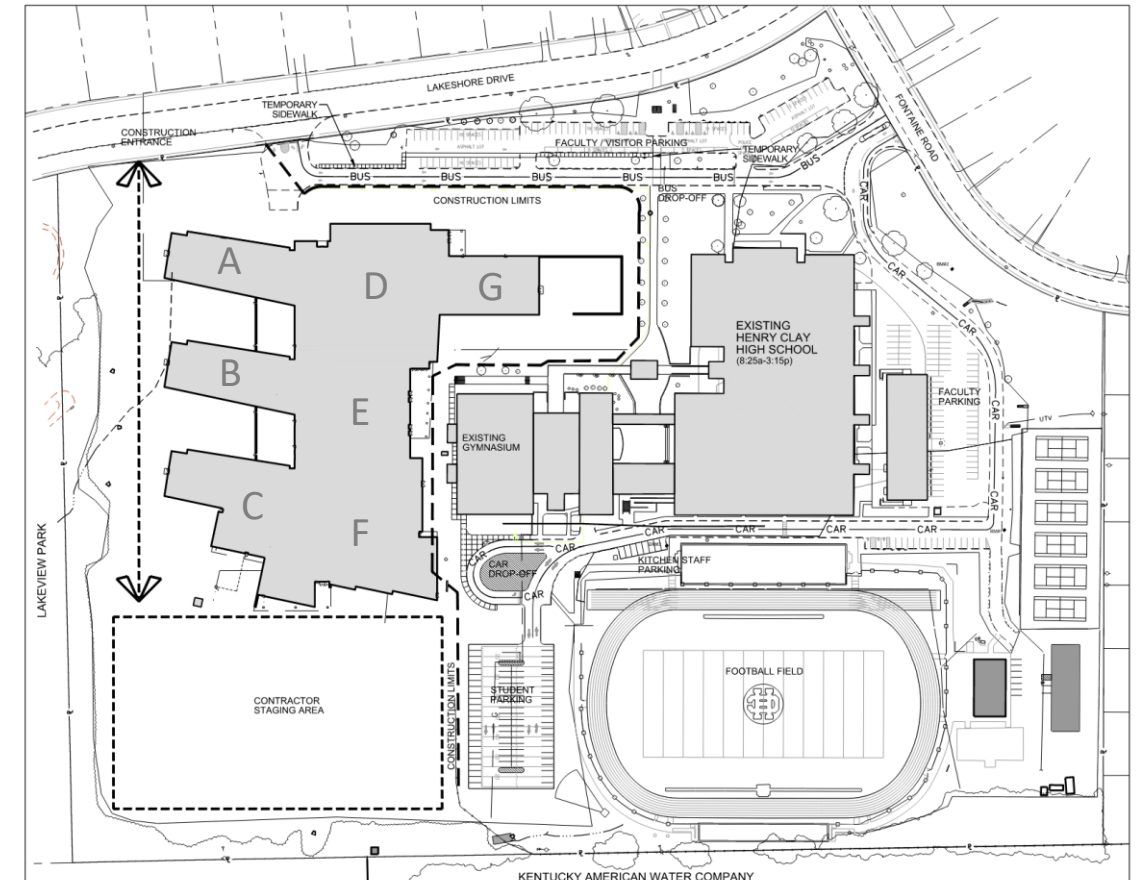

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Area A (Classroom Wing): Stone & Brick Veneer Masonry In Progress




Week Ending May 29, 2026

New Henry Clay High School



Area C (Classroom Wing): Stair F Concrete Stairs & Plinth is in Progress

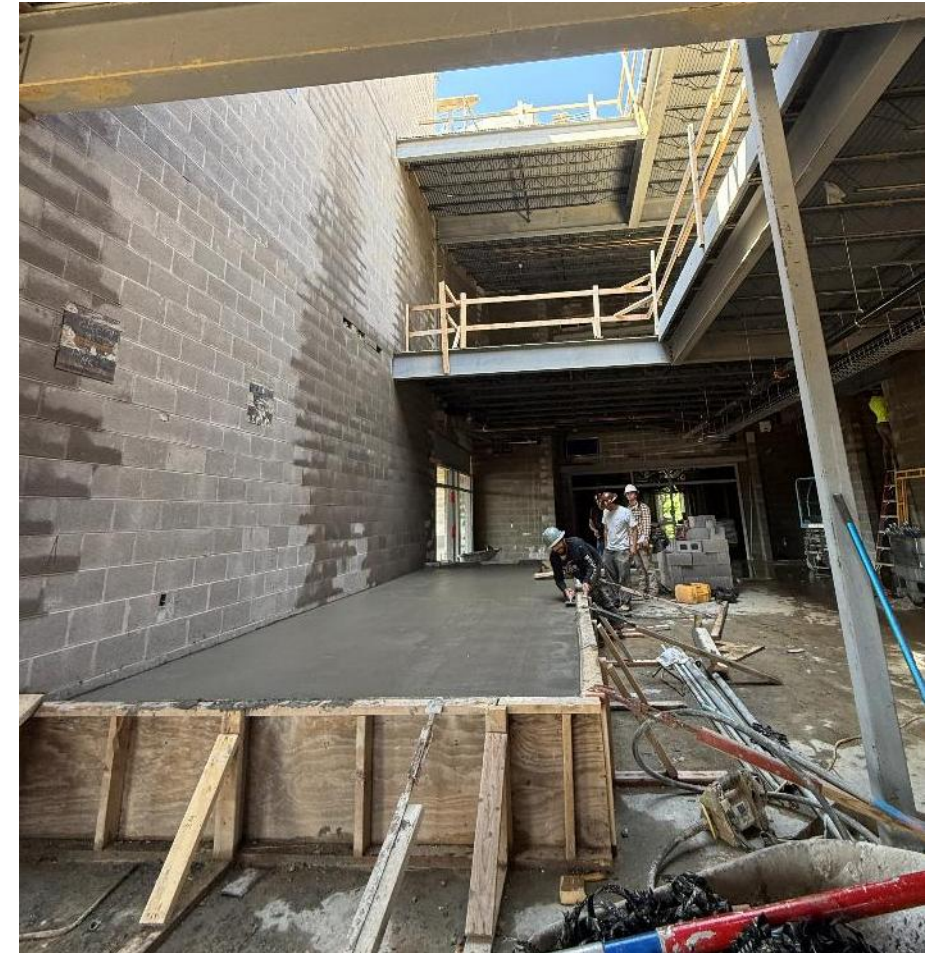

Week Ending May 29, 2026

New Henry Clay High School



Level 2 Area E (Gym): Hollowcore Concrete Plank Installation is Complete at Plan North End of Gym



Week Ending May 29, 2026

New Henry Clay High School

Area G Level 1 (Athletics Office, Weight Room, ROTC, Classrooms): CMU Walls, Hollow Metal Frames/Storefront Installation and Steel Erection for Level 2 in Progress



New Henry Clay High School

Level 2 Area G (Media Center): ICF Construction & IFA Installation in Progress




Week Ending May 29, 2026

New Henry Clay High School



Steel Erection for Roof at North-South Corridor Continues

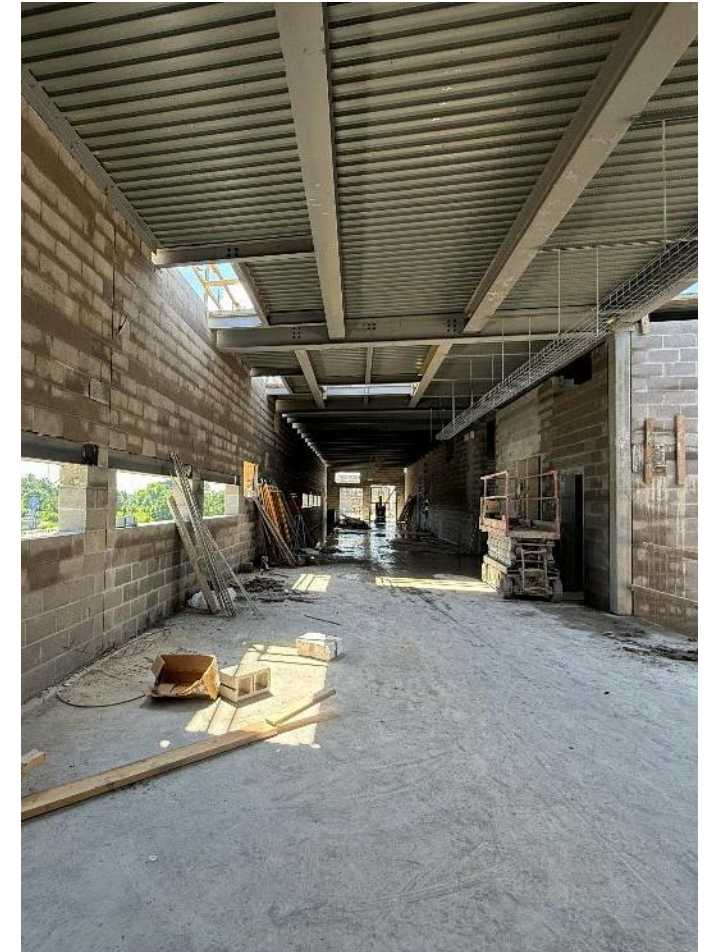

Week Ending May 29, 2026

New Henry Clay High School

Level 3 Area C (Classroom Wing): CMU Wall Construction is in Progress & Steel Erection for Roof is Underway



Week Ending May 29, 2026
