



# Milwaukee Recreation Community Center & Browning Playfield

## CONSTRUCTION UPDATE

### PROGRESS THIS WEEK:

- Continued Roof Decking Installation – Area B
- CMU Wall Completion Stair 3 – Area A2
- Installed New Under Slab Plumbing – Area A1

### GOALS NEXT 2 WEEKS:

- Underground Plumbing – East Side Of Area C
- Start Long Span Joist Installation – Area C2
- Shoring Installation For Lintel Replacement – Area A

### PROJECT HIGHLIGHT THIS WEEK:






- Site Light Pole Bases Installed In Playfield
- Under Slab Plumbing Inspection Passed – Area A1

### Photos or Visual Assets:

**DATE:** May 29th, 2026

### MRCC PROJECT PROGRESS:



### MILESTONE CHECKLIST:

- Construction Start – 9/18/25
- Foundations Complete 3/25/26
- Steel Complete
- Enclosed
- MRCC Substantial Completion
- Playfield Completion



Site Light Pole Bases Installed – Playfield



CMU Wall – Southwest Corner Of Area C1



# Milwaukee Recreation Community Center & Browning Playfield

## CONSTRUCTION UPDATE

**DATE: May 29th, 2026**

### MORE PROGRESS PHOTOS:




CMU Wall Stair 3 – North Side Of Area A2



Installed Roof Decking – Area B1



Site Tour With MKE Rec Team!

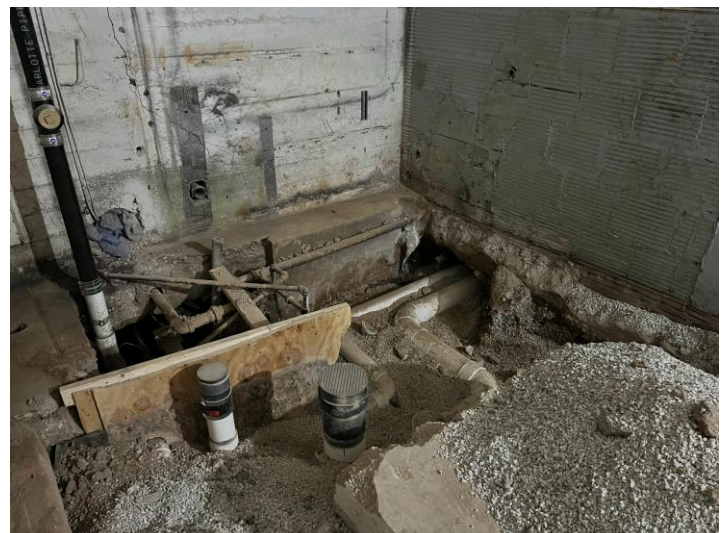

New Under Slab Plumbing – Area A1
