

BOND UPDATES

tomballisd.net/bond



We're excited to keep our community informed as bond projects move forward. Some updates may seem small, others more noticeable, but each one is an important step in providing the best opportunities for our students.

Thank you for your continued support in making these improvements possible!

Tomball West High School

Bond 2021

Facility - Ongoing Construction

- Construction of Tomball West High School continues to progress as planned and remains on schedule for the start of the 2026–2027 school year.
- An official ribbon-cutting ceremony is planned for July 27 at 9 AM, giving the community an opportunity to celebrate the opening of Tomball ISD's newest high school before students arrive in August.



Agricultural Project Barn & Competitive Soccer Field

- The Agricultural Project Barn is 85% complete with the canopy due to be installed next week and louvers the following week. The project is aggressively targeting completion by the end of this month.



- As of June 3, the TWHS Soccer Stadium is 90% complete with the scoreboard scheduled to be installed next week.




Traffic Light at Mueschke Road - West Complex Site Development



- The traffic light at the intersection of Mueschke Road and Destination Drive has been completed but is not yet active as construction on Tomball West High School continues.
- The traffic light will be activated prior to the start of the 2026-27 school year.

Creekside Park 5th Grade Addition

Bond 2021



- Construction on the 5th grade addition continues to progress as planned.
- All exterior brick and stone work has been completed, with interior finish work continuing.
- The cafeteria expansion will continue through the majority of the summer, with flooring replacement as a major component still to be completed.

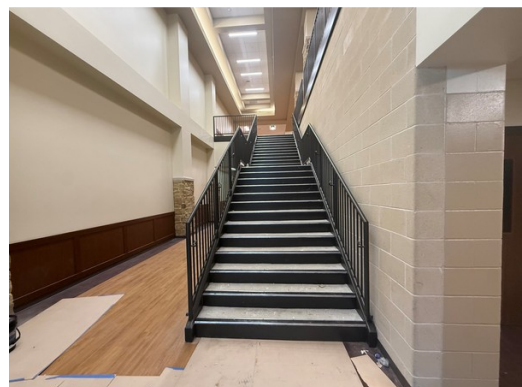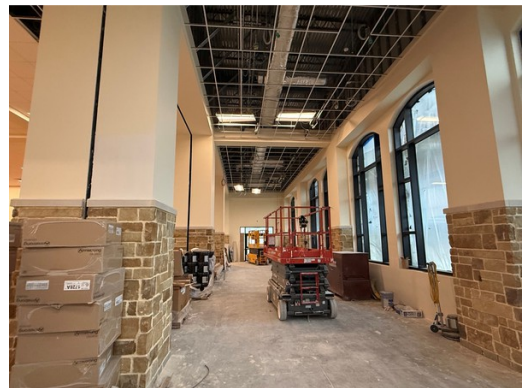



Multi-Program Activity Centers (MPACs)

Bond 2025

- During the June 2026 Board meeting, PBK Architects presented the schematic design of the Multi-Program Activity Centers (MPACs). The plans align with the exact size and dimensions shared with voters during the 2025 Bond Election, ensuring the project is being delivered as presented to the community.
- The 80-yard field design was intentionally developed to accommodate site constraints across all three comprehensive high school campuses while ensuring equitable facilities and opportunities for students districtwide. An MPAC will be constructed at each comprehensive high school, featuring an 80-yard turf field plus a 10-yard end zone.
- MPACs will also include a drop-down netting to accommodate multiple student groups, ample storage, two golf simulators, and a fully air-conditioned space.

MPAC Schematic Design Plan

[Click to view in full detail](#)



Transportation Center

Bond 2025

- At the June 2026 Board meeting, the Board of Trustees approved the selection of Gamma Construction to complete the expansion of the Transportation parking lot.
- The expansion project will increase parking space to accommodate a total of 365 buses and 304 staff vehicles.
- Also included in the scope of work will be the realignment of the main entrances, new security gate, updated lighting, security fencing and security cameras.

Athletic Updates

Bond 2025

- At the June 2026 Board meeting, the Board of Trustees re-approved the purchase of replacement bleachers at Tomball High School after moving on from the previously awarded vendor.
 - Due to the delays with the original vendor, product availability, and impact to campus activities, the bleacher replacement project will be completed during the Summer of 2027.
-

Facility Infrastructure Replacements

Bond 2025

- At the May 2026 Board meeting, the Board of Trustees approved the selection of Air Conditioning Innovative Solutions (ACIS) to complete the replacement of HVAC equipment at the Tomball ISD Staff Development Center.
 - This project will include the replacement of existing chillers, water pumps, and infrastructure to ensure proper system performance and reliability.
-

Safety & Security

Bond 2025

- At the May 2026 Board meeting, the Board of Trustees approved the purchase of a district-wide radio communication system intended to strengthen both daily communication and emergency response efforts.
-


Turf Installation

Bond 2025

- Work has begun at Tomball High School to replace the existing artificial turf and track surfaces. The project is scheduled to be completed this summer and ready for use this August.



- Below is a rendering of the field.

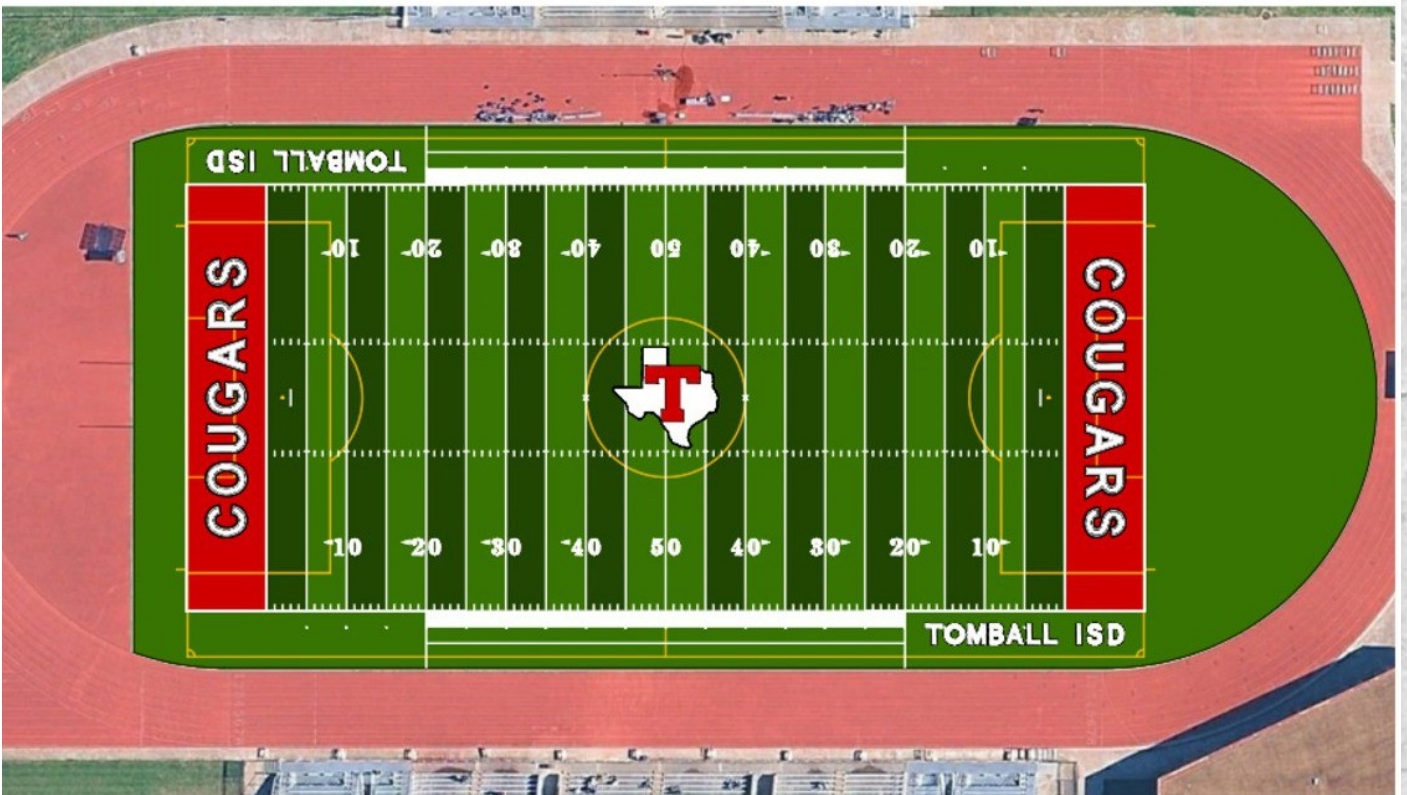

Student & Staff Device Refresh Bond 2025

- At the May 2026 Board meeting, the Board of Trustees approved Phase 2 of the technology device refresh for staff at the following campuses:
 - Creekside Park
 - Northpointe Intermediate School
 - Canyon Pointe Elementary School

- Wildwood Elementary School
 - Willow Wood Junior High
 - Oakcrest Intermediate School
 - Lakewood Elementary School
 - Willow Creek Elementary School
-



Tomball ISD

Tomball is using Smore to create beautiful newsletters
