



# Milwaukee Recreation Community Center & Browning Playfield

## CONSTRUCTION UPDATE

### PROGRESS THIS WEEK:

- Floor Decking Installed – Area B1
- Stripped Asphalt – Southeast Corner Of Site
- Demolition to Replace Lintels – Area A1

### GOALS NEXT 2 WEEKS:

- Install Roof Decking – Area A2
- Start Pump Track
- Start Shade Structure Foundations – Site

### PROJECT HIGHLIGHT THIS WEEK:

- Installing Long Span Joists
- Soil Haul off Plan Started

### Photos or Visual Assets:

**DATE: June 12<sup>th</sup> , 2026**

### MRCC PROJECT PROGRESS:




### MILESTONE CHECKLIST:

- Construction Start – 9/18/25
- Foundations Complete 3/25/26
- Steel Complete
- Enclosed
- MRCC Substantial Completion
- Playfield Completion



Asphalt Stripping – Southeast Of Site

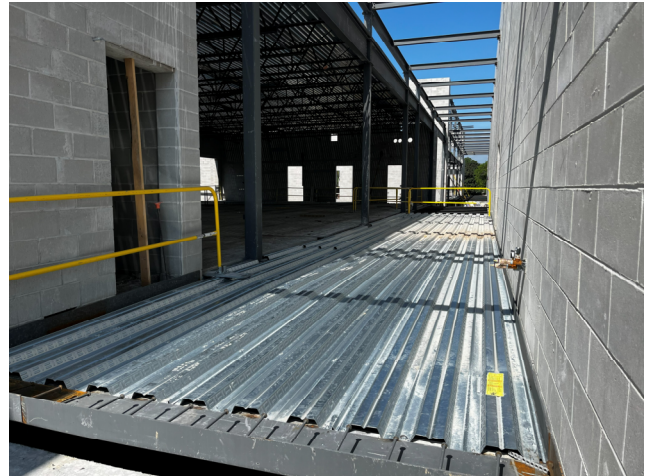

Floor Decking Installed – Area B1



# Milwaukee Recreation Community Center & Browning Playfield

## CONSTRUCTION UPDATE

**DATE: June 12<sup>th</sup>, 2026**

### MORE PROGRESS PHOTOS:



First Long Span Joist Installed – Area C2



Structural Steel Joist Installed – Area C1



Plumbing Installed – Area C1



Concrete Slab Pour – Area A1
