


New Henry Clay High School

➤ Completed/Work in Progress:

- ICF placing and pouring, and the installation of IFAs at ICF walls is in progress.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are in progress.
- Steel erection is underway in all areas.
- Area D concrete roof structure is complete.
- Above ceiling MEP installation is in progress at areas A,B and C.
- Installation of Stairs A, B, C, D, E & F is complete.
- West driveway retaining wall construction is complete.
- Interior metal stud wall & soffit framing in progress at Areas A, B & C.
- Area A & Area B roofing is in progress.
- Mechanical penthouse construction is in progress.
- CMU finishing & painting, and hanging drywall is in progress at areas A & B.

➤ Upcoming Look Ahead:

- Continue site grading.
- Continue with ICF walls, IFA frames, laying CMU walls and installing hollow metal frames.
- Continue with under-slab plumbing and electrical at Areas E & C.
- Continue pouring concrete slabs on grade at Areas E & C.
- Continue with steel erection at Areas A, C, E and G.
- Continue with above ceiling MEP installation at all areas.

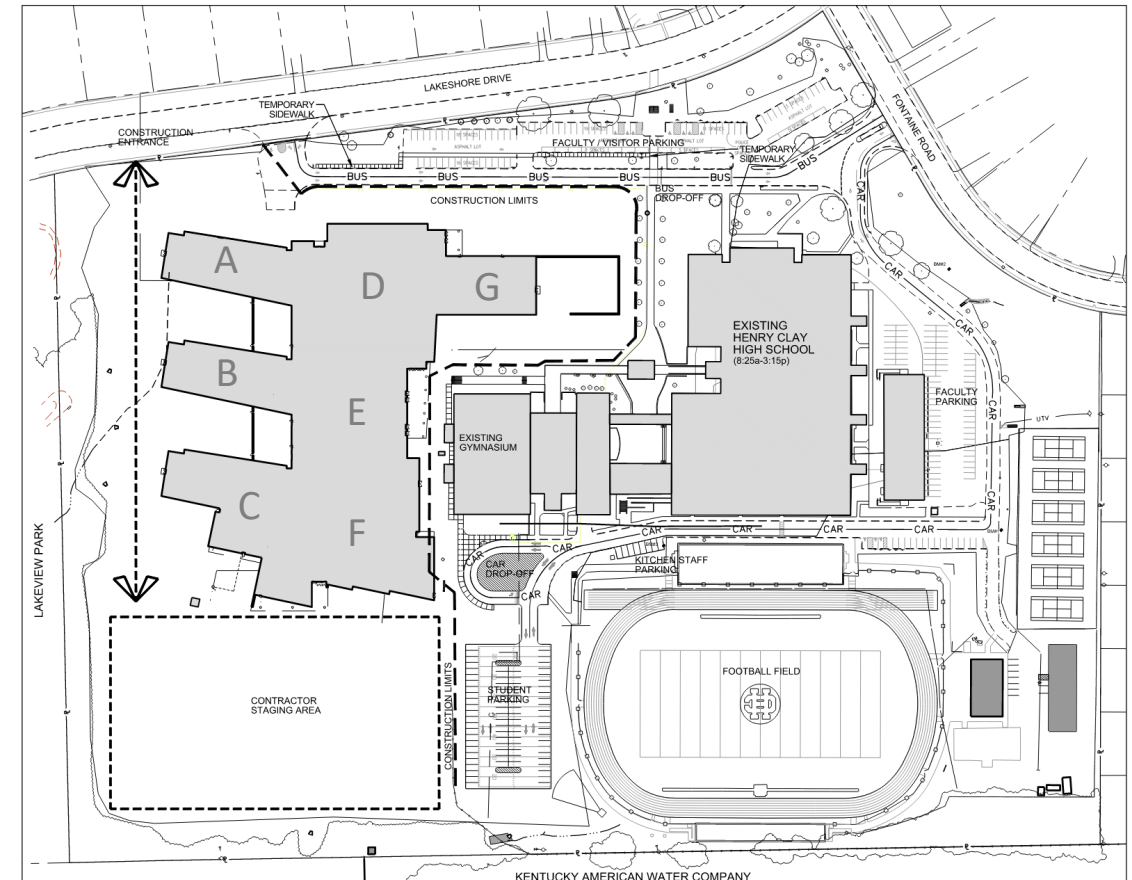

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Areas A & B (Classroom Wings): Stone & Brick Veneer Masonry is in Progress



Week Ending June 19, 2026

New Henry Clay High School

Areas A & B (Classroom Wings): CMU Finishing & Painting, and Hanging Drywall is in Progress



Week Ending June 19, 2026

New Henry Clay High School

Level 1 Area C (Cafeteria): ICF Construction at Cafeteria Perimeter Continues



Week Ending June 19, 2026

New Henry Clay High School



Level 1 & 2: North-South Corridor: Light Gauge Soffit Framing Continues



Week Ending June 19, 2026

New Henry Clay High School

Area E Level 2 (Gym): Concrete Topper / Slab at Level 2 North Bleachers is Complete w/ CMU Walls in Progress



New Henry Clay High School

Level 2 Area G (Media Center): ICF Construction & IFA Installation, Steel Erection & Partial Floor Slab in Progress




Week Ending June 19, 2026

New Henry Clay High School



Level 3 North-South Corridor: Hollow Metal Frame & Storefront Installation is in Progress

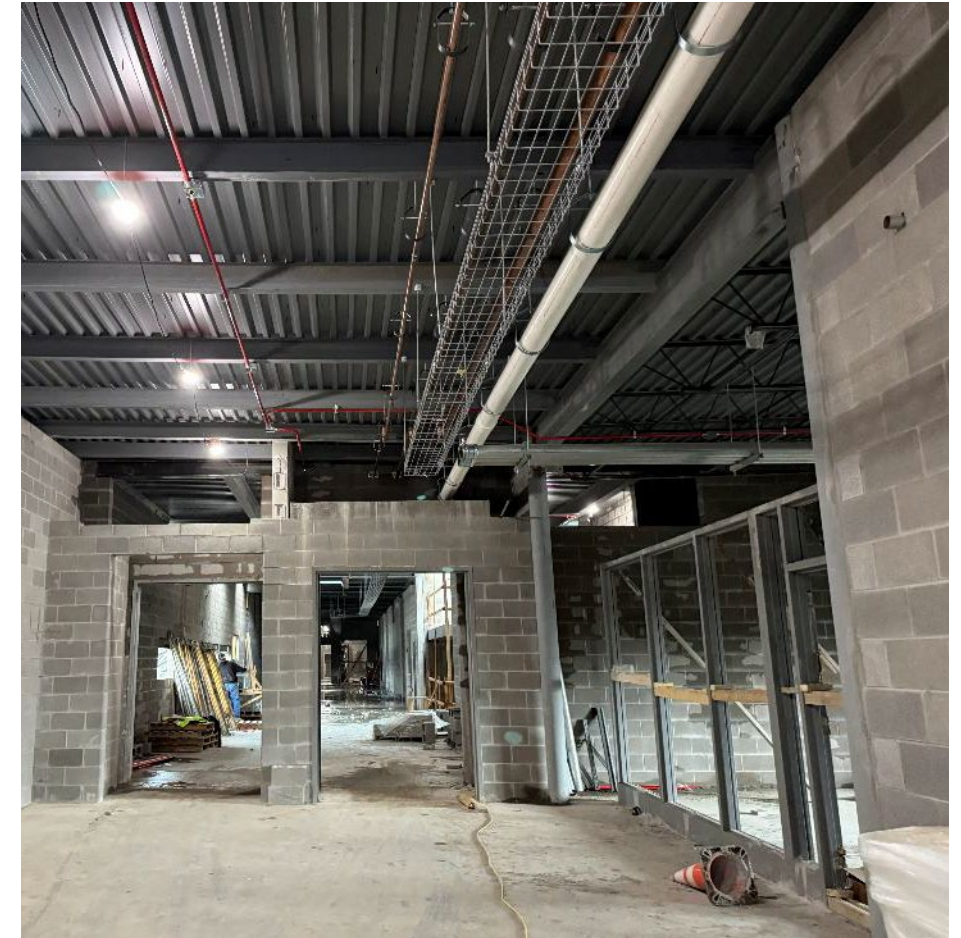

Week Ending June 19, 2026
