

BOND CONSTRUCTION UPDATE - May 2026

#ThankYouVoters

2022 BOND - PRIORITY 1 PROJECTS



Districtwide Improvements

- **Fire Alarm Upgrades**
 - FSE, TES, RRE, & SJH - substantially complete and punch list work in progress
- **Intrusion/Access Control Upgrades** remains in progress at all campuses
- **Graphics Design Packages** - all campuses complete
- **LED Lighting Upgrades** - approx 95% complete throughout
- **Mechanical Upgrades** - work is complete with punch lists items being corrected
- **Punch Lists** - identification and corrections are ongoing

Priority 1 Improvements




RRE Cafeteria Graphic

Priority 1 Improvements



RRE/FSE Monuments

Priority 1 Improvements

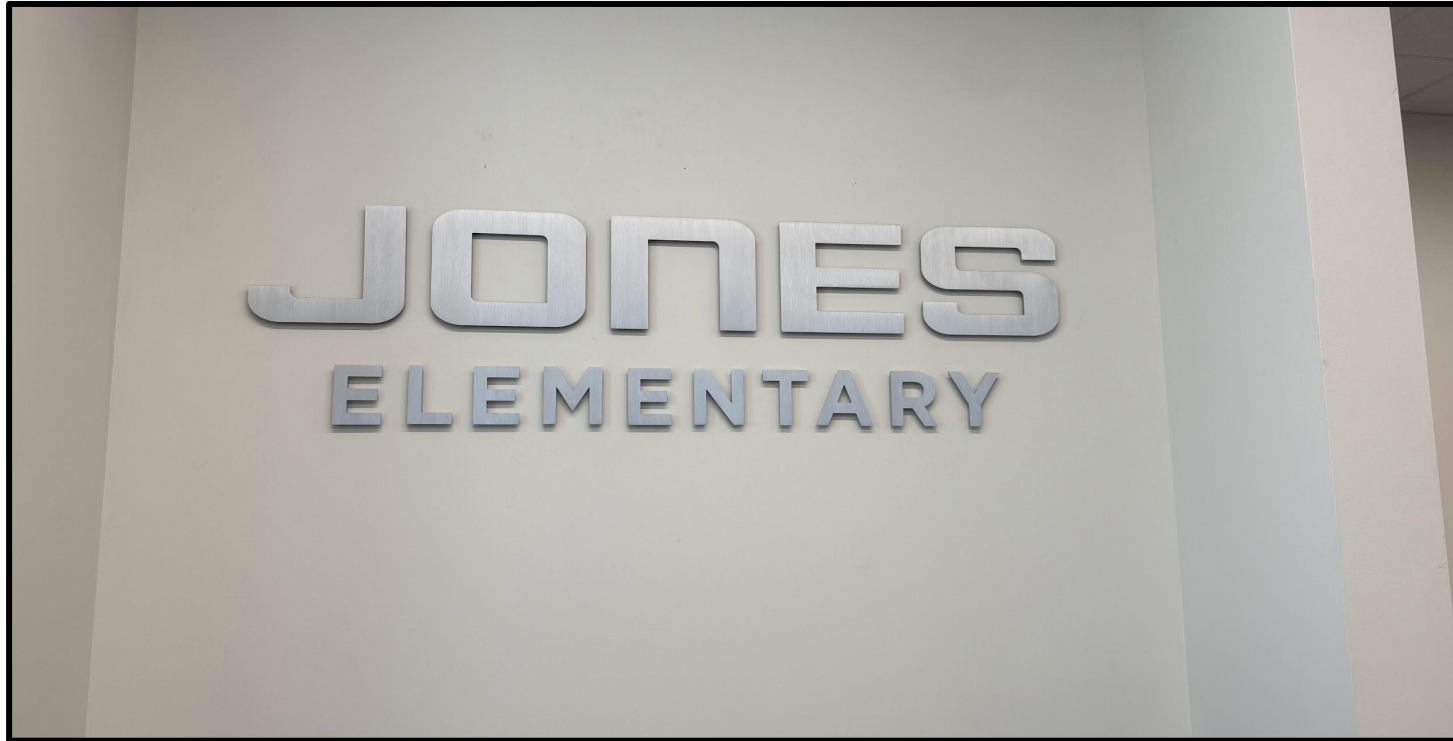

JES Waiting Room

Priority 1 Improvements



JES Corridor Graphic

Priority 1 Improvements



JES Mural Graphic

Priority 1 Improvements



HES Reception & Hallway Graphic

Priority 1 Improvements



HES Main Corridor & Cafeteria Graphic

Priority 1 Improvements




TES Front Office & Gym Graphic

Priority 1 Improvements



TES Main Corridor Graphic

Priority 1 Improvements

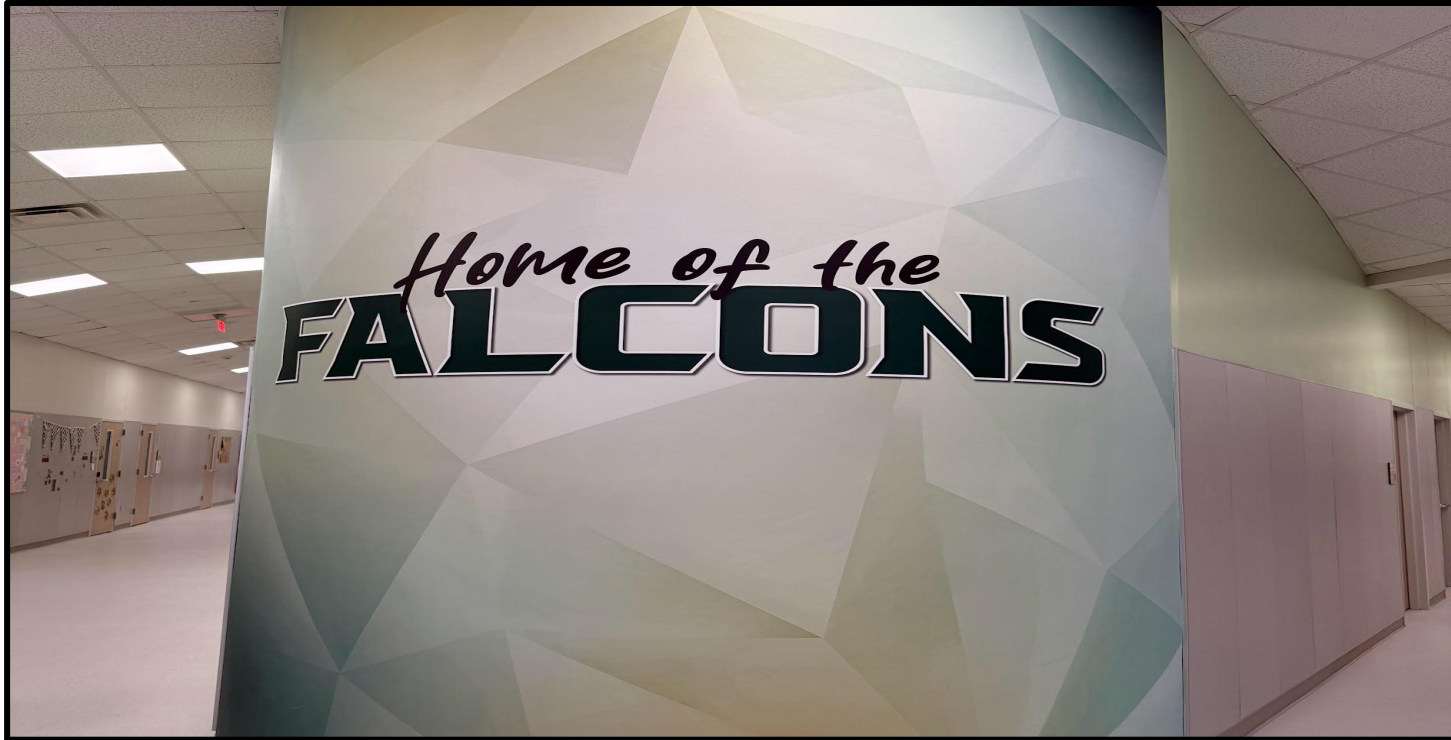

FSE Curved Wall Vinyl Covering

2024 - \$702 M BOND



- **Warren Ranch High School** - construction started and opening in 2028
- **Johnson Junior High** - construction start and opening TBD
- **Elementary #9** - construction started and opening in 2027
- **Elementary #10** - construction start and opening TBD
- **Land & Buses** - ongoing; 15 buses ordered and delivered
- Demographic Update scheduled for Summer 2026.

- Storm and sanitary lines are around 95% complete
- Underground plumbing and electrical are complete at building pad
- Building slab on grade is 50% complete
- Building pads at stadium and ag barn are nearly complete
- Paving is in progress - student lot and some drives have been placed
- CMU walls are in progress at the central plant
- Structural steel deliveries scheduled to start in May
- Opening scheduled in summer 2028



Front
Elevation
Rendering

WALLER ISD
BOND

24

WARREN RANCH HIGH SCHOOL



Site
Overview

WALLER ISD
CONSTRUCTION



Building Slab



Building pads at Stadium and Ag Barn

WALLER ISD **BOND** 24 WARREN RANCH HIGH SCHOOL



Central Plant CMU

WALLER ISD
CONSTRUCTION

- Campus is in the Cypress Green development east of Hopfe Road
- All building piers are complete
- Underground piping in the building has been completed
- Currently working on grade beams in Areas A and B
- Placed first concrete pavement in the front parking lot
- Structural steel delivery and erection scheduled in June
- Opening scheduled in August 2027



Rendering

ELEMENTARY #9



Site Plan



Aerial View - Looking North



North Parking Lot (first concrete pour)



Underground Work

A photograph of a classroom filled with children of various ages, from young children to teenagers. They are all expressing excitement, with many having their arms raised in the air. They are seated at small, light-colored tables with blue chairs. The room has white walls, a tiled ceiling, and educational posters on the wall. The entire image is overlaid with a semi-transparent red filter.

#ThankYouVoters

Waller
Independent School District
