

REFERENDUM PROJECT UPDATES

DATE: June 11, 2026

MEMORIAL ART ROOM FLOORS

The new epoxy floors have been installed; base trim will be completed by the end of next week.



MEMORIAL ROOF REPLACEMENT

The rain has caused some delays, but the project is still on schedule. They have completed above the pool and are moving to front part of Memorials commons and working back towards the kitchen.

MEMORIAL PARKINGLOT LIGHT REPLACEMENT

The lighting on the building is 50% complete. The old parking lot lights have been removed; new poles and light fixtures will be installed next week. The remaining wall pack lights should be completed in the next 2 weeks.



MEMORIAL POOL EQUIPMENT REPLACEMENT

Demolition and installation have been moved to the week of June 29th.

MEMORIAL GYM FLOOR REFINISHING

The project starts the last week in June and should be completed by the second week in July.

NORTH WATER HEATER REPLACEMENT

The area has been prepped for the new water heaters, they have begun moving into the basement for final hookup. The final installation will take a couple of weeks.



NORTH GENERATOR REPLACEMENT

The new generator installation will begin the week of June 22. The new generator is scheduled to ship and be onsite on June 25th.




NORTH GYM AHU REPLACEMENT

Demolition is complete. Trades are preparing for the new AHUs, the ship dates have been moved to July 17th. Installation and operation should be completed by August 15th.



NORTH PHOTO LAB REMODEL

The existing flooring will be removed this week; rough electrical ins will be done the last week in June. The cabinets for the project are scheduled to be installed later this week and into the last week in June.

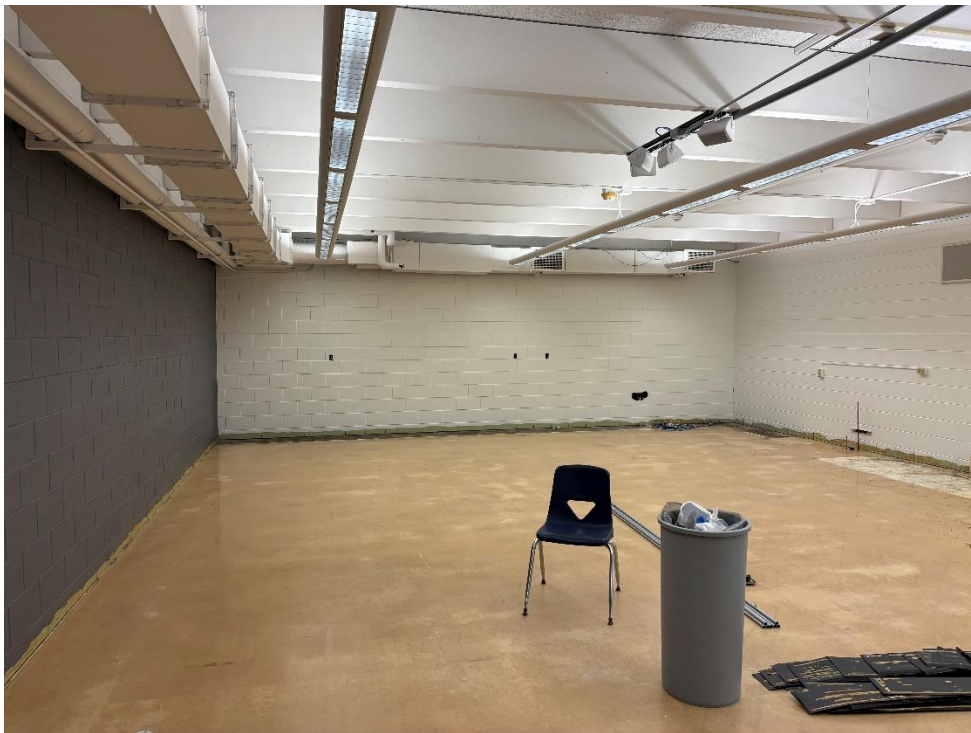

NORTHSTAR TRACK RELINING

The track repair and relining will begin this week. They had a break in their schedule and will be on site on Tuesday the 23rd.

NORTHSTAR GYM FLOOR RELINING

The contractor was able to start earlier than expected, he began sanding the gym floor. It is anticipated that the final sanding will be completed this week and lines will begin to be painted on the floor.



NORTHSTAR BATHROOM DIVIDERS

Work is scheduled for July 20th.

LOCUST LANE ADA PLAYGROUND SURFACING

The prep for the new ADA surface is completed, the new surface is scheduled to be installed the week of June 22nd



MANZ PARKING LOT REPLACEMENT

The parking lot paving was completed ahead of schedule last week. Lining the parking lot will be done in the next 2 weeks depending on weather.



MANZ EXTERIOR LIGHT REPLACEMENT

The exterior light replacement to LED downlighting began earlier this week. The lights being replaced on the building should be completed the week of June 15th, the parking lot lights will be removed the week of June 22.



SAM DAVEY PARKING LOT REPLACEMENT

The parking lot demolition is complete; area is being prepped to receive blacktop. The new blacktop surface and concrete replacement are scheduled to be completed in the next 2 weeks depending on weather.



