

New London Spicer: MS/HS Phase 2

2026 Renovations

Weekly Update: Ending 06/26/26

Ongoing/ Completed:

- **Willmar Electric:** Light adjustments as needed by Acoustic Associates (Classrooms, Cafeteria, Hallways Main Level).
- **Willmar Electric:** Dropping lights & other electric related items in completed areas such as Main Area D.
- **Acoustic Associates:** Completed Area C pad out, working through Main Area D.
- **Acoustic Associates:** Completed grid of Main Area D, Area F, 50% complete with Main Area E.
- **RJ Mechanical:** Glycol drain of existing systems 100% complete, system filled with water and cleaning solution. Two 10" holes made within Media Center for new piping.
- **KMS:** 100% complete with NLS ductwork cleaning 6/25/2026.
- **Prime Mechanical:** 90% complete with insulation of new roof mains.
- **Prime Mechanical:** 90% complete with Main Level insulation, areas remaining are Kitchen, Technology 2020.
- **Chappel Central:** Dropping diffusers within completed areas such as Main Area D.
- **Boulder Creek:** Onsite 6/23/2026 started demolition of Technology 2020 chase.
- **Yale/BCI:** Final existing condensing unit has been removed from roof, this section of roof was replaced with new roofing material

2-Week Look Ahead:

- **RJ Mechanical:** Clean existing glycol lines and refill with new product.
- **RJ Mechanical:** Complete piping within Media Center chase.
- **Acoustic Associates:** Complete grid in Main Level Area E.
- **Acoustic Associates:** Complete Main Area D & Area F pad out.
- **Boulder Creek:** Reinstall chase within Technology 2020 when insulation is complete.
- **Prime:** Complete insulation within lower-level areas.

Issues/Concerns/Other:

- **Chappel/Prime:** Clearance within Technology 2020 Chase is very minimal. Chappel/Prime to issue a change order to complete insulation within the Chase rather than exteriorly lined.
- **SitealogIQ:** Multiple 2x4 light screens, and a few desks/chairs within the building have been damaged. SitealogIQ to document affected rooms.




Grid Completion Area F



Existing Condenser Removal



State Inspector Visit 6/23/2026

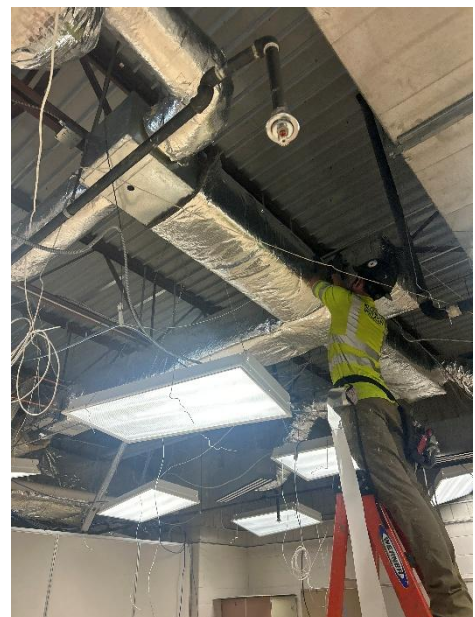

Insulation Install of Classrooms
