


New Henry Clay High School

➤ Completed/Work in Progress:

- ICF placing and pouring, and the installation of IFAs at ICF walls is in progress.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are in progress.
- Steel erection is underway in all areas.
- Area D concrete roof structure is complete.
- Above ceiling MEP installation is in progress at areas A,B and C.
- Installation of stairs in all areas but the Gym is complete.
- Exterior stone & brick veneer is in progress at Areas A, B & C.
- Interior metal stud wall & soffit framing in progress at Areas A, B & C.
- Area A & Area B are dried-in with roofing systems in progress.
- Mechanical penthouse construction is in progress.
- CMU finishing & painting, and hanging drywall is in progress at areas A & B.

➤ Upcoming Look Ahead:

- Continue site grading.
- Continue with ICF walls, IFA frames, laying CMU walls and installing hollow metal frames.
- Continue with under-slab plumbing and electrical at Areas F & C.
- Continue pouring concrete slabs on grade at Areas F & C.
- Continue with steel erection A, C, E, F and G.
- Continue with above ceiling MEP installation at all areas.

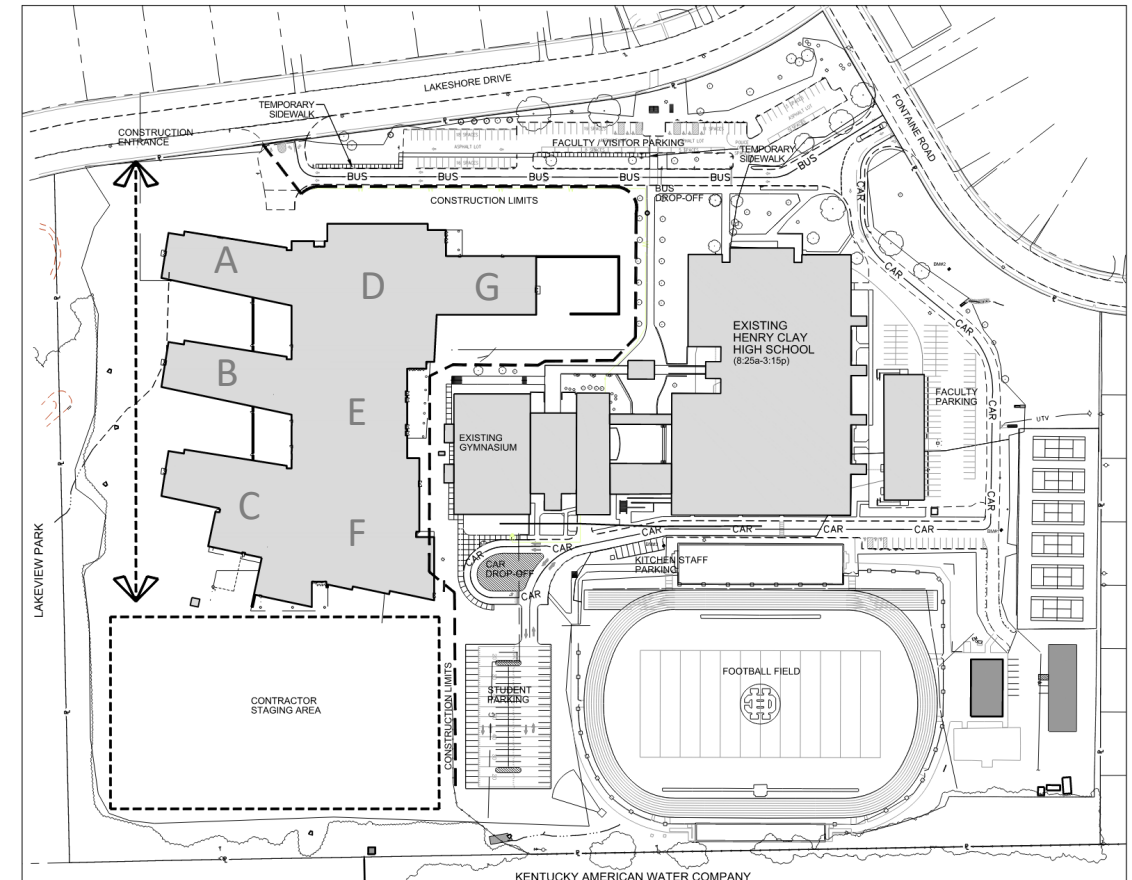

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.


New Henry Clay High School

Areas A, B & C (Classroom Wings): Stone & Brick Veneer Masonry is in Progress



New Henry Clay High School

Level 1 Area G (East Lobby, Weight Room, ROTC & Health Classrooms): Stair G Installation is Complete w/ Formwork in Progress for the Concrete Plinth at the Base of the Stair

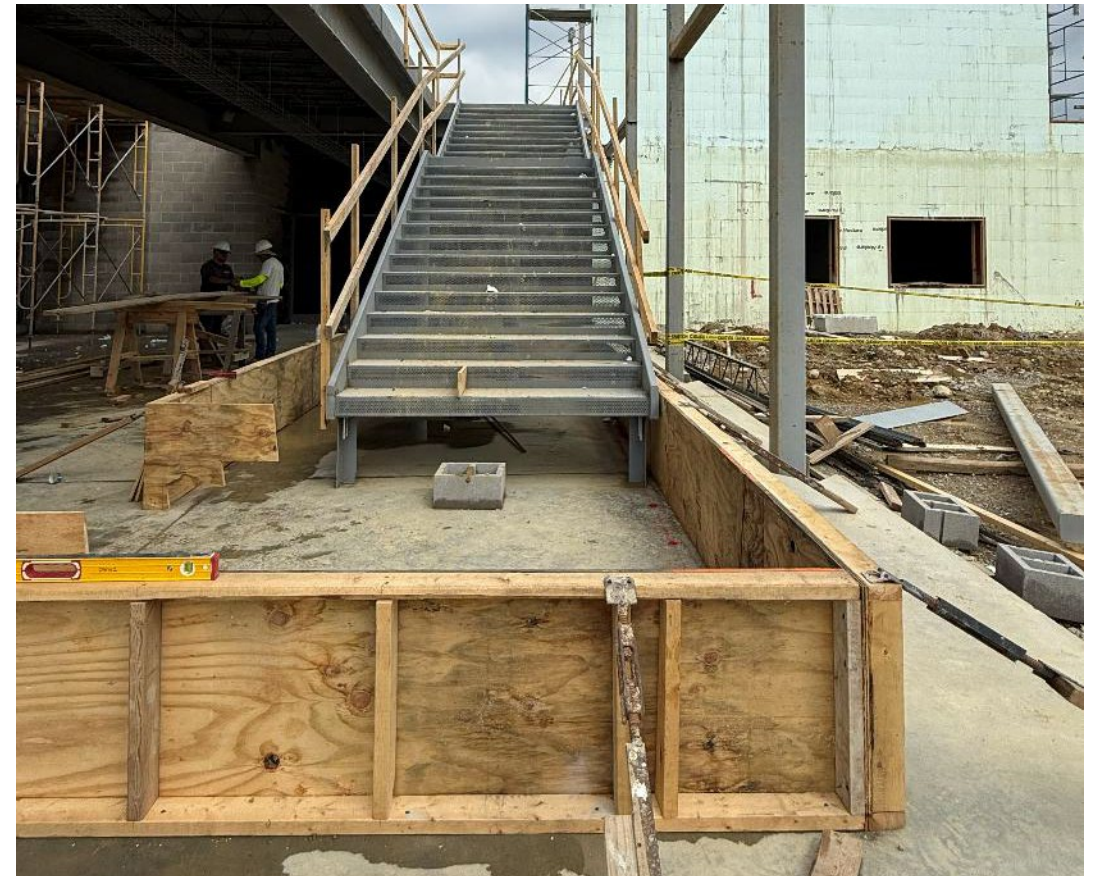

New Henry Clay High School

[Left Image]: Area G : Steel Erection for Level 3 Mechanical Platform in Progress
[Right Image]: Area G: Steel Erection for East Lobby Curtain Walls & Roof in Progress



New Henry Clay High School

Level 2 Area D (Multi-Purpose Rm/Storm Shelter): Storefront Frames Installed & CMU Furring Walls in Progress



New Henry Clay High School

[Left Image]: Level 2 Area E (Gym): Hollowcore Concrete Planks in Place at South Upper Bleachers

[Right Image]: Level 1 Area E (Gym): Underslab Preparations in Progress at South Locker Rooms



New Henry Clay High School



Level 4 Area B (Mechanical Penthouse): CMU Walls & Floor Slab w/ Mech Openings is Complete.
Steel Erection for Penthouse Roof to Begin Soon



New Henry Clay High School

Roofs at Areas A & B (Classroom Wings): Areas are Dried-In W/ SBS & Standing Seam Roof Systems in Progress



Week Ending July 10, 2026
