


New Henry Clay High School

- **Completed/Work in Progress:**
 - ICF placing and pouring, and the installation of IFAs at ICF walls is in progress.
 - Laying of CMU walls and the installation of hollow metal frames is underway.
 - Under-slab plumbing/electrical and concrete slabs are in progress.
 - Steel erection is underway in all areas.
 - Area D concrete roof structure is complete.
 - Above ceiling MEP installation is in progress at areas A,B and C.
 - Installation of stairs in all areas but the Gym is complete.
 - Exterior stone & brick veneer is in progress at Areas A, B & C.
 - Interior metal stud wall & soffit framing in progress at Areas A, B & C.
 - Area A & Area B are dried-in with roofing systems in progress.
 - Mechanical penthouse construction is in progress.
 - CMU finishing & painting, and hanging drywall is in progress at areas A & B.
- **Upcoming Look Ahead:**
 - Continue site grading.
 - Continue with ICF walls, IFA frames, laying CMU walls and installing hollow metal frames.
 - Continue with under-slab plumbing and electrical at Areas F & C.
 - Continue pouring concrete slabs on grade at Areas F & C.
 - Continue with steel erection A, C, E, F and G.
 - Continue with above ceiling MEP installation at all areas.

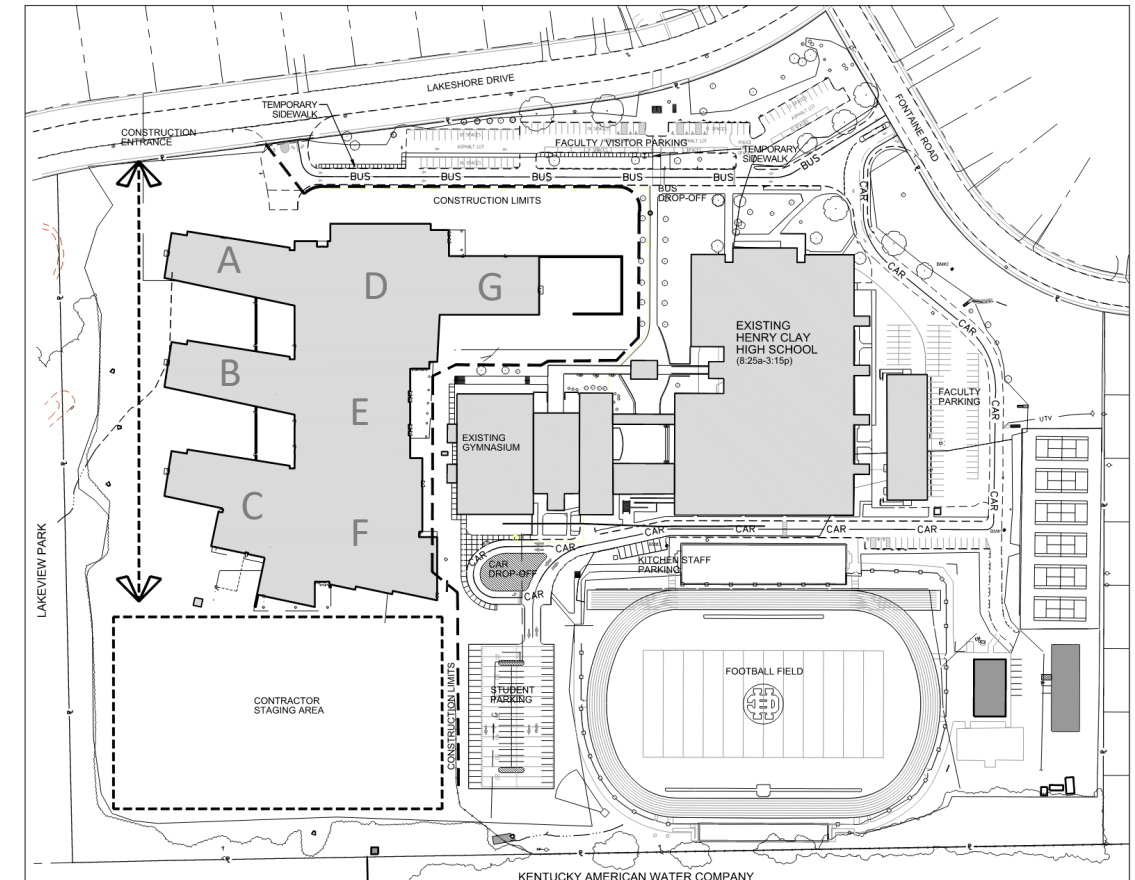

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Areas A, B & C (Classroom Wings): Stone & Brick Veneer Masonry is in Progress



Week Ending July 24, 2026

New Henry Clay High School

Areas A, B & C (Classroom Wings): Stone & Brick Veneer Masonry is in Progress



Week Ending July 24, 2026

New Henry Clay High School



Level 2 Area G (Media Center & Med Clinic): ICF Walls, Framed Openings, CMU Walls, Steel Erection and Site Grading in Progress



Week Ending July 24, 2026

New Henry Clay High School

Level 2 Area G (Media Center & Med Clinic): ICF Walls, Framed Openings, CMU Walls and Steel Erection in Progress



New Henry Clay High School



Level 2 Area D (Main Admin): Site Grading Complete, ICF Walls & Under-Slab Preparations in Progress




Week Ending July 24, 2026

New Henry Clay High School



Area E (Gym): Installation of Stairs and Upper Bleacher Railings is in Progress

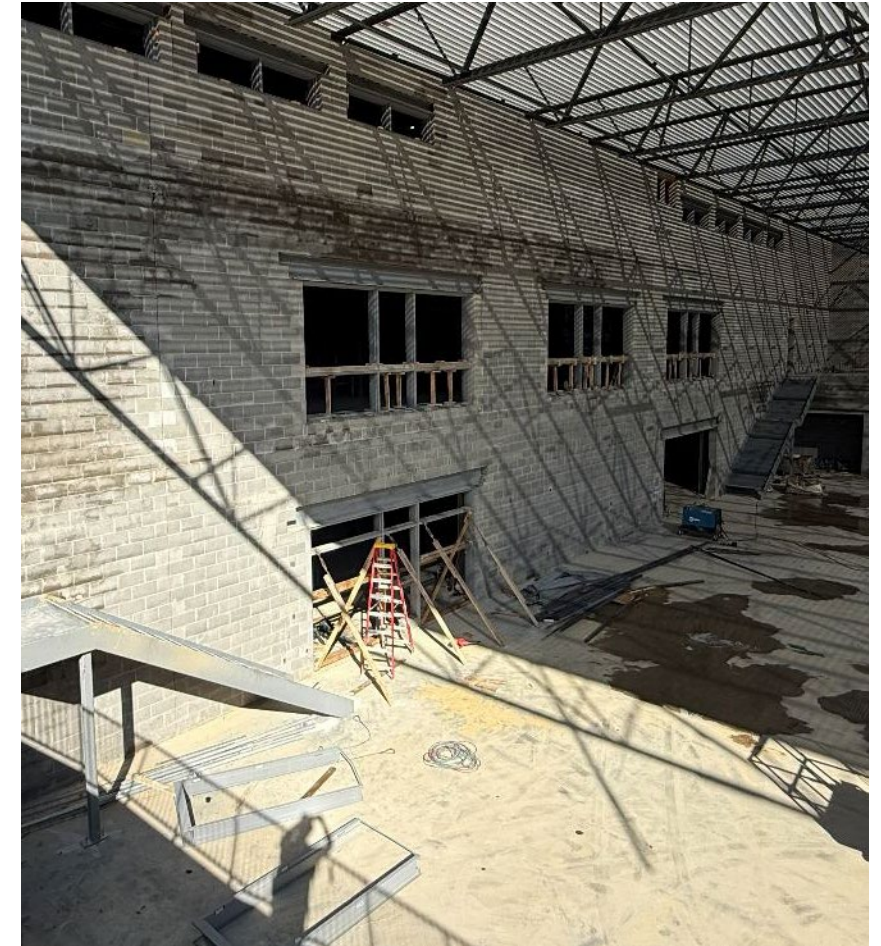

Week Ending July 24, 2026

New Henry Clay High School

[Left Image]: Area C (Kitchen): Parapet Wall, Fascia, and Brick Veneer Installation in Progress

[Right Image]: N-S Corridor Roof: SBS Roofing System Installation in Progress

