


New Henry Clay High School

➤ Completed/Work in Progress:

- ICF walls and ICF wall framed openings are complete in all areas except for where in progress at areas C, D, F and G.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are complete except where in progress at areas C, D, F and G.
- Above ceiling MEP installation is in progress at areas A, B and C.
- Installation of stairs in all areas but the Gym is complete.
- Exterior stone & brick veneer is complete in areas A & B, and in progress in area C.
- Interior metal stud wall & soffit framing in progress at areas A, B & C.
- Areas A, B and C are dried-in with roofing systems in progress.
- CMU finishing & painting, and hanging drywall is in progress at areas A, B and C.

➤ Upcoming Look Ahead:

- Continue with under-slab plumbing and electrical and pouring slabs on grade at areas F & C.
- Continue roof joist and deck at Areas E, F & G.
- Begin roofing at areas D and E.
- Continue above ceiling MEP and wall rough-ins.
- Continue interior metal stud wall and soffit framing in areas A, B & C.
- Begin trim and window seals.

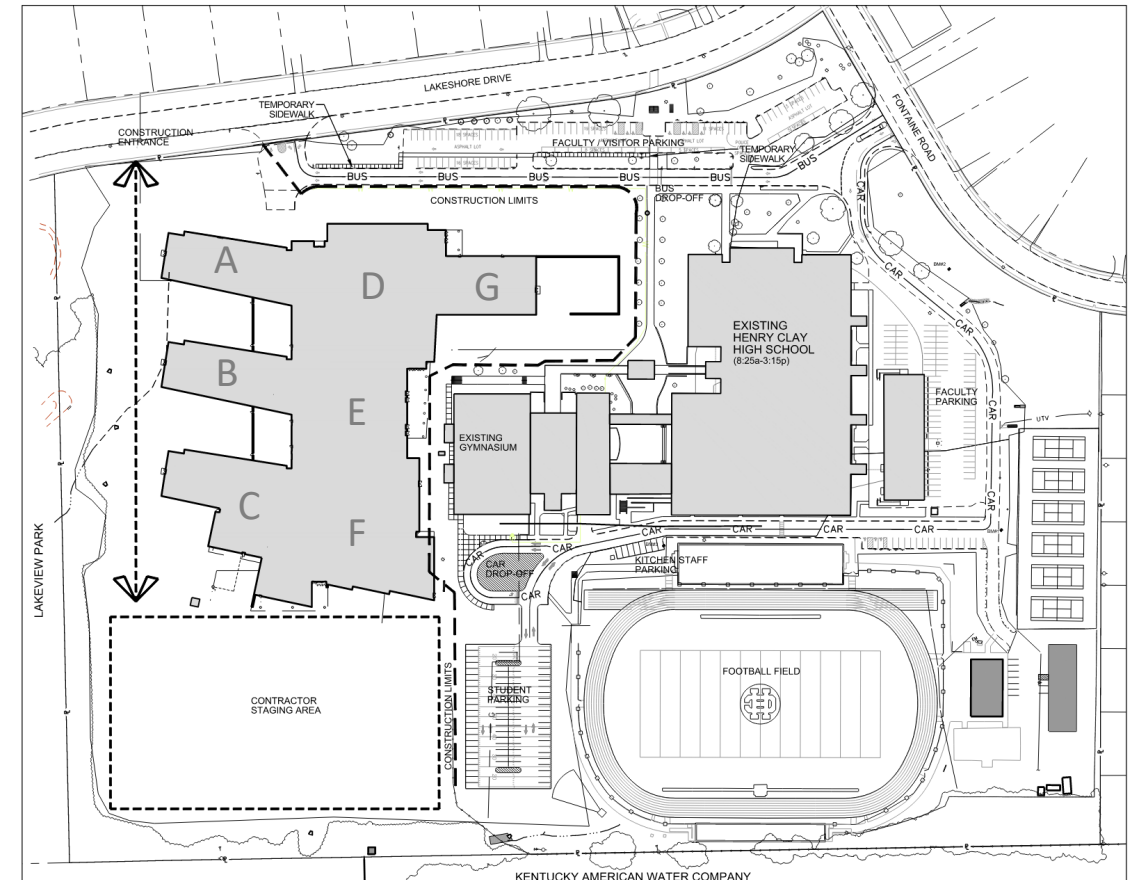

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Areas A, B & C (Classroom Wings): Stone & Brick Veneer Masonry is in Progress



Week Ending July 31, 2026

New Henry Clay High School

Areas A, B & C (Classroom Wings): Stone & Brick Veneer Masonry is in Progress



New Henry Clay High School

Level 2 Area G (Media Center & Med Clinic): Steel Erection for Roof and Curtain Walls is in Progress



Week Ending July 31, 2026

New Henry Clay High School

Level 2 Area G (Media Center & Med Clinic): ICF Walls, Framed Openings, CMU Walls and Steel Erection is in Progress



Week Ending July 31, 2026

New Henry Clay High School

Level 2 Area D (Main Admin): Hollowcore Plank Concrete Topper and Concrete Slab on Grade is Complete with ICF Walls in Progress



New Henry Clay High School

Area C (Cafeteria): ICF Walls and Steel Erection for Curtain Walls and Roof is in Progress



Week Ending July 31, 2026

New Henry Clay High School

[Left Image]: Area C (Kitchen): Parapet Wall, Fascia, and Brick Veneer Installation in Progress
[Middle & Right Images]: N-S Corridor Roof: SBS Roofing System Installation in Progress

