

BOND CONSTRUCTION UPDATE - July 2026

#ThankYouVoters

ADDITIONAL WORK ITEMS STARTED

- Modular wall installation has started to enclose collaboration spaces at WHS to create nine additional classrooms
- Two new Activity Buses have been ordered
- Design of Concession-Restroom facility at WHS Athletic Field in progress
- Daikin Stadium elevator refurbishment, blinds, and carpet are all released, and ordered new water fountains and trash cans
- Upgrades to Daikin Stadium access control, technology network, and cameras are all released



WHS Partition Walls

2022 BOND - PRIORITY 1 PROJECTS



Districtwide Improvements

- **Fire Alarm Upgrades**
 - FSE, TES, RRE, & SJH - substantially complete and punch list work in progress
- **Intrusion/Access Control Upgrades** - remains in progress at all campuses
- **Graphics Design Packages** - all campuses complete
- **LED Lighting Upgrades** - approximately 99% complete throughout
- **Mechanical Upgrades** - work is substantially complete with punch lists items being corrected
- **Punch Lists** - identification and corrections are ongoing - approximately 60% complete
- **SJH** - new classroom and library furniture has been received and installed

Priority 1 Improvements




SJH Classroom Furniture

Priority 1 Improvements



SJH Library Furniture

Priority 1 Improvements

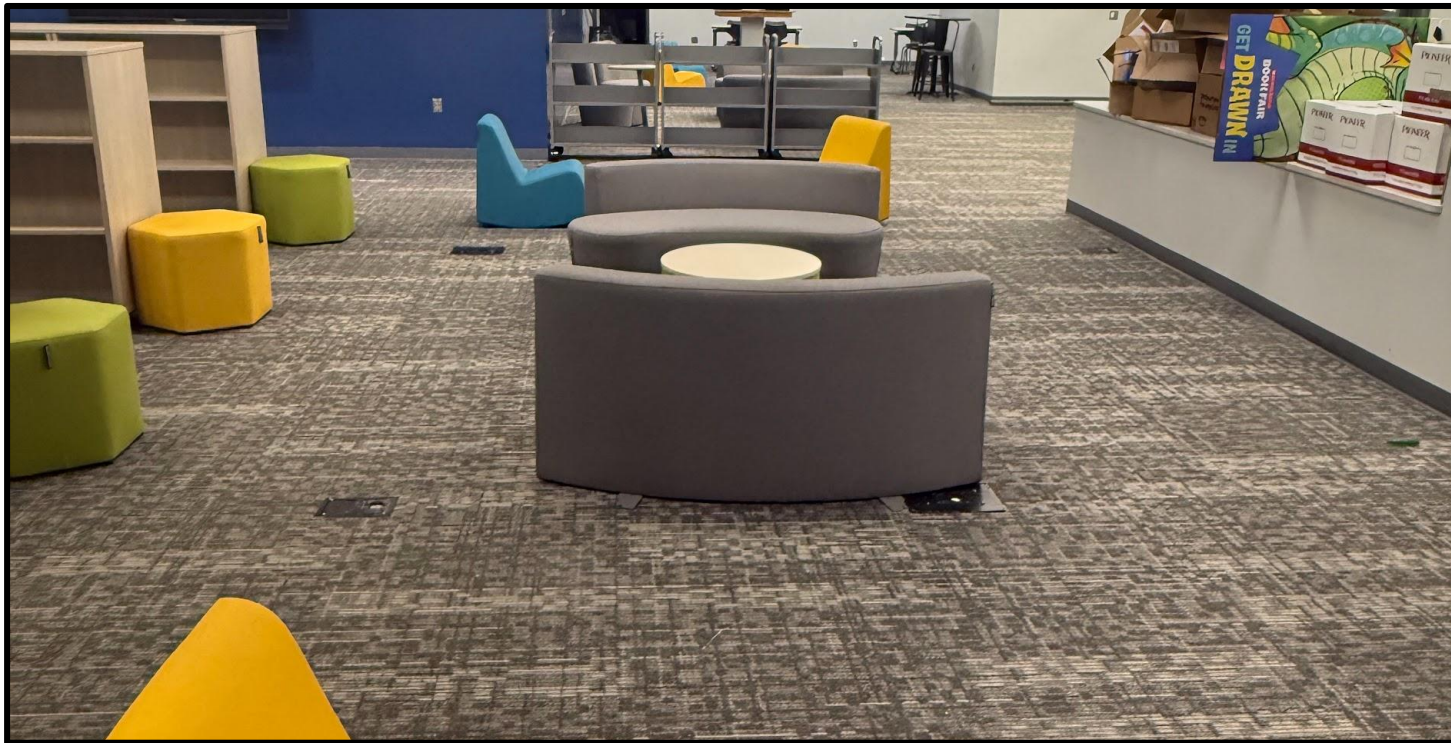

SJH Library Furniture

Priority 1 Improvements




SJH Library Furniture

Priority 1 Improvements



SJH Library Conference Room

2024 - \$702 M BOND

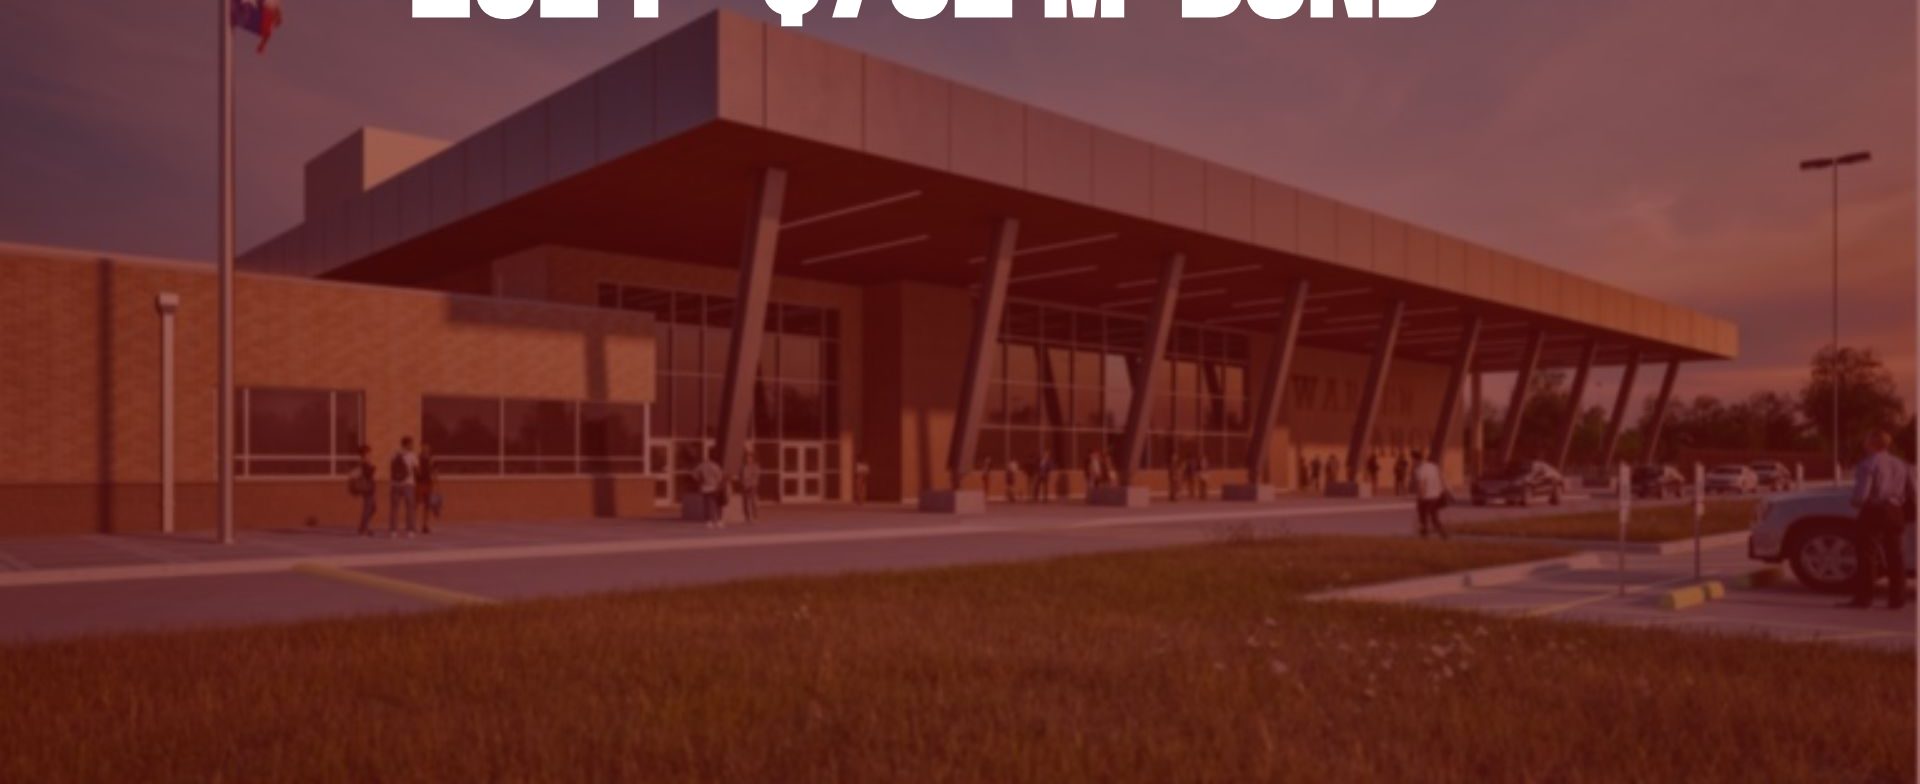

- **Warren Ranch High School** - construction started and opening in 2028
- **Johnson Junior High** - construction start and opening TBD
- **Elementary #9** - construction started and opening in 2027
- **Elementary #10** - construction start and opening TBD
- **Land & Buses** - ongoing; 15 buses ordered and delivered
- Demographic Update scheduled for Summer 2026

- High school building slab on grade is 100% complete
- Building slab at Ag Barn is complete
- Grade beams are in progress at stadium fieldhouse
- Site paving is nearly complete
- CMU walls at the Central Plant are complete and started in the locker room areas of the main building
- Structural steel is being erected utilizing two cranes
- Lightweight concrete roof decks and fireproofing are in progress
- MEP hangers and overhead has commenced following the fireproofing



Front
Elevation
Rendering


WALLER ISD **BOND** 24 WARREN RANCH HIGH SCHOOL



Site Overview

WALLER ISD
CONSTRUCTION

WALLER ISD **BOND** 24 WARREN RANCH HIGH SCHOOL

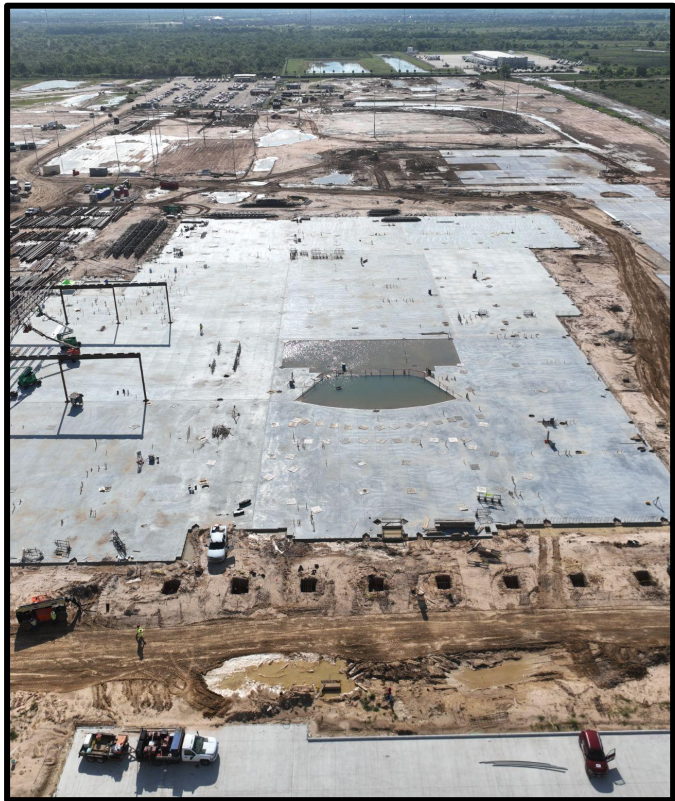

Building Slab

WALLER ISD
CONSTRUCTION

WALLER ISD **BOND** 24 WARREN RANCH HIGH SCHOOL



Steel Erection

WALLER ISD
CONSTRUCTION

WALLER ISD
BOND

24

WARREN RANCH HIGH SCHOOL



Roof Decking

WALLER ISD
CONSTRUCTION

WALLER ISD **BOND** 24 WARREN RANCH HIGH SCHOOL



CMU Walls at Gym/Locker rooms

WALLER ISD
CONSTRUCTION

WALLER ISD **BOND** 24 WARREN RANCH HIGH SCHOOL



MEP and Fireproofing
Progress

WALLER ISD
CONSTRUCTION



Grade Beams at Stadium Fieldhouse

WALLER ISD **BOND** 24 WARREN RANCH HIGH SCHOOL



Building Slab at Ag Barn

WALLER ISD
CONSTRUCTION

WALLER ISD **BOND** 24 WARREN RANCH HIGH SCHOOL



Central Plant Exterior CMU and Lightweight Roof

WALLER ISD
CONSTRUCTION

- All building piers are complete
- Underground piping in the building has been completed
- Grade beams are complete in Area A, B, and E. Area C has starting.
- SOG is complete in Area A, B, and E.
- Entire front and 600 yards of paving of the rear parking lot has been poured
- Structural steel erection in Area A has finished with Area E started
- Area B Steel arrives on July 10
- Opening scheduled in August 2027



Rendering

ELEMENTARY #9



Site Plan



Aerial View - Looking South



Aerial View - Looking East



Aerial View - Looking North



Aerial View - Looking West



Area A



Area B Slab



Area E Steel Erection



Elevator Pit

A photograph of a classroom filled with children of various ages, from young children to teenagers. They are all expressing excitement, with many having their arms raised in the air. The children are seated at small, light-colored tables with blue chairs. The classroom has white walls, a tiled ceiling, and various educational posters and supplies visible in the background. The entire image is overlaid with a semi-transparent red filter.

#ThankYouVoters

Waller
Independent School District
