


New Henry Clay High School

Completed/Work in Progress:

- ❑ ICF walls and ICF wall framed openings are complete in all areas except for where in progress at areas C, D, F and G.
- ❑ Laying of CMU walls and the installation of hollow metal frames is underway.
- ❑ Under-slab plumbing/electrical and concrete slabs are complete except where in progress at areas C, D, F and G.
- ❑ Above ceiling MEP installation is in progress at areas A, B and C.
- ❑ Installation of stairs in all areas but the Gym is complete.
- ❑ Exterior stone & brick veneer is complete in areas A & B, and in progress in area C.
- ❑ Interior metal stud wall & soffit framing in progress at areas A, B & C.
- ❑ Areas A, B and C are dried-in with roofing systems in progress.
- ❑ CMU finishing & painting, and hanging drywall is in progress at areas A, B and C.

Upcoming Look Ahead:

- ❑ Continue with under-slab plumbing and electrical and pouring slabs on grade at areas F & C.
- ❑ Continue roof joist and deck at Areas E, F & G.
- ❑ Begin roofing at areas D and E.
- ❑ Continue above ceiling MEP and wall rough-ins.
- ❑ Continue interior metal stud wall and soffit framing in areas A, B & C.
- ❑ Begin trim and window seals.

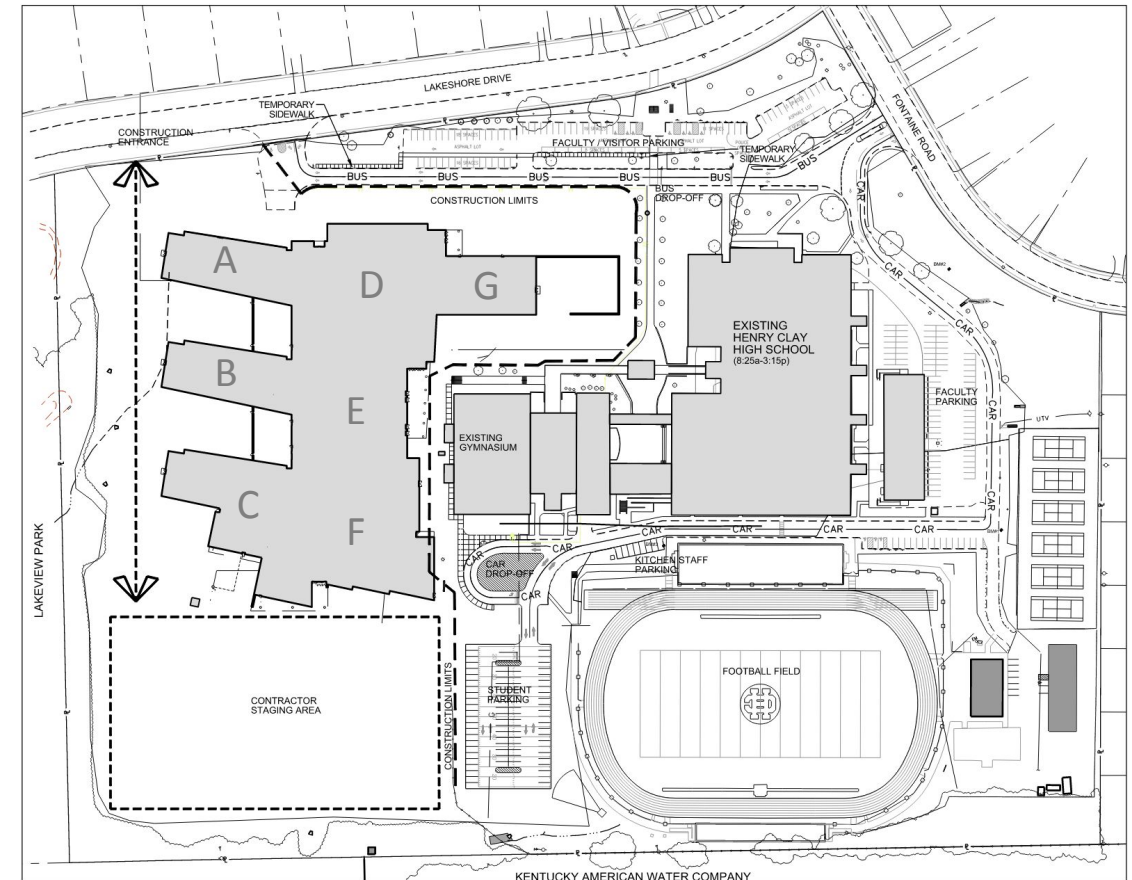

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School


Area E (Gym): Stone & Brick Veneer Masonry is in Progress



Week Ending August 28, 2026

New Henry Clay High School

Area F (Music Classrooms & Theater): Stone & Brick Veneer Masonry is in Progress

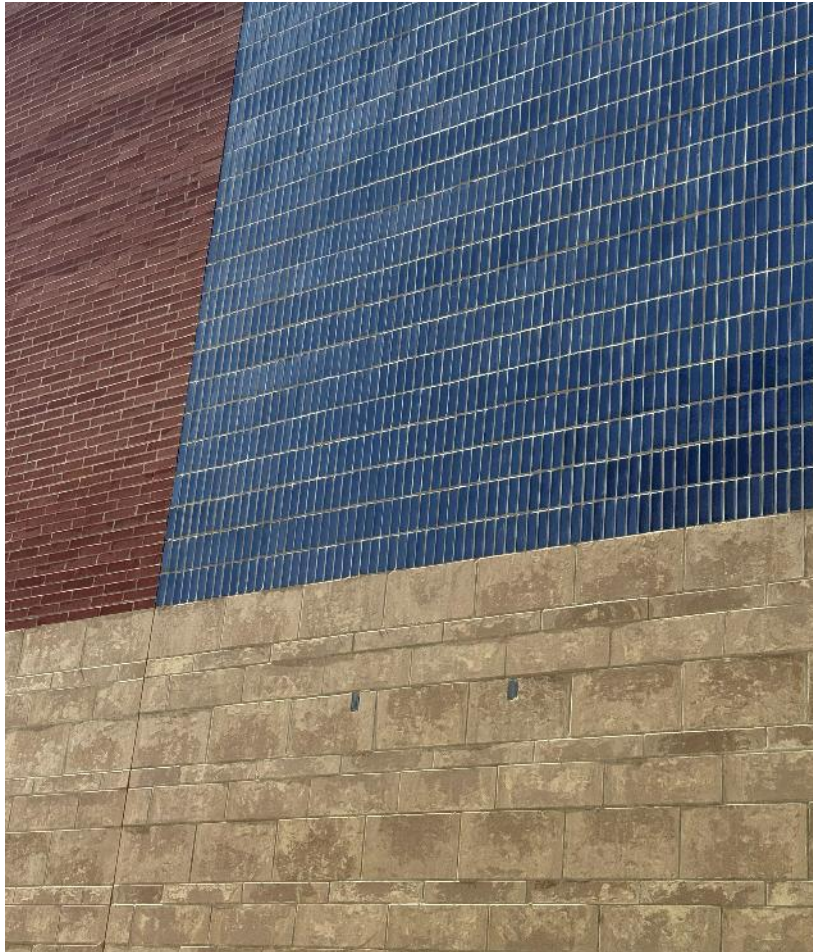

Week Ending August 28, 2026

New Henry Clay High School

Level 2 Area G (Media Center & Med Clinic): ICF Walls, Framed Openings, Air Barrier Application, CMU Walls and Steel Erection is in Progress




New Henry Clay High School

Level 2 Area D (Main Admin): Concrete Slab on Grade is Complete with ICF, CMU Walls, Hollow Metal Frame Installation and Steel Erection in Progress



New Henry Clay High School


Area F (Theater & Music Classrooms): ICF Walls, Framed Openings, CMU Walls & Steel Erection is in Progress

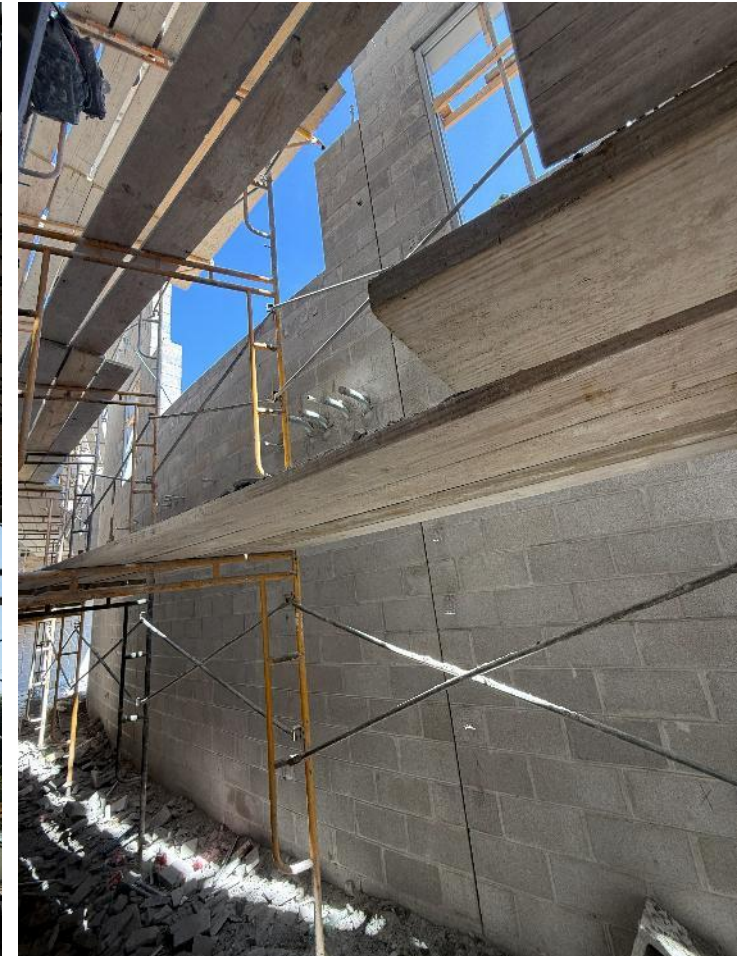

Week Ending August 28, 2026

New Henry Clay High School

Area G (Media Center & Med Clinic): Installation of Ships Ladders and Walkovers in Progress

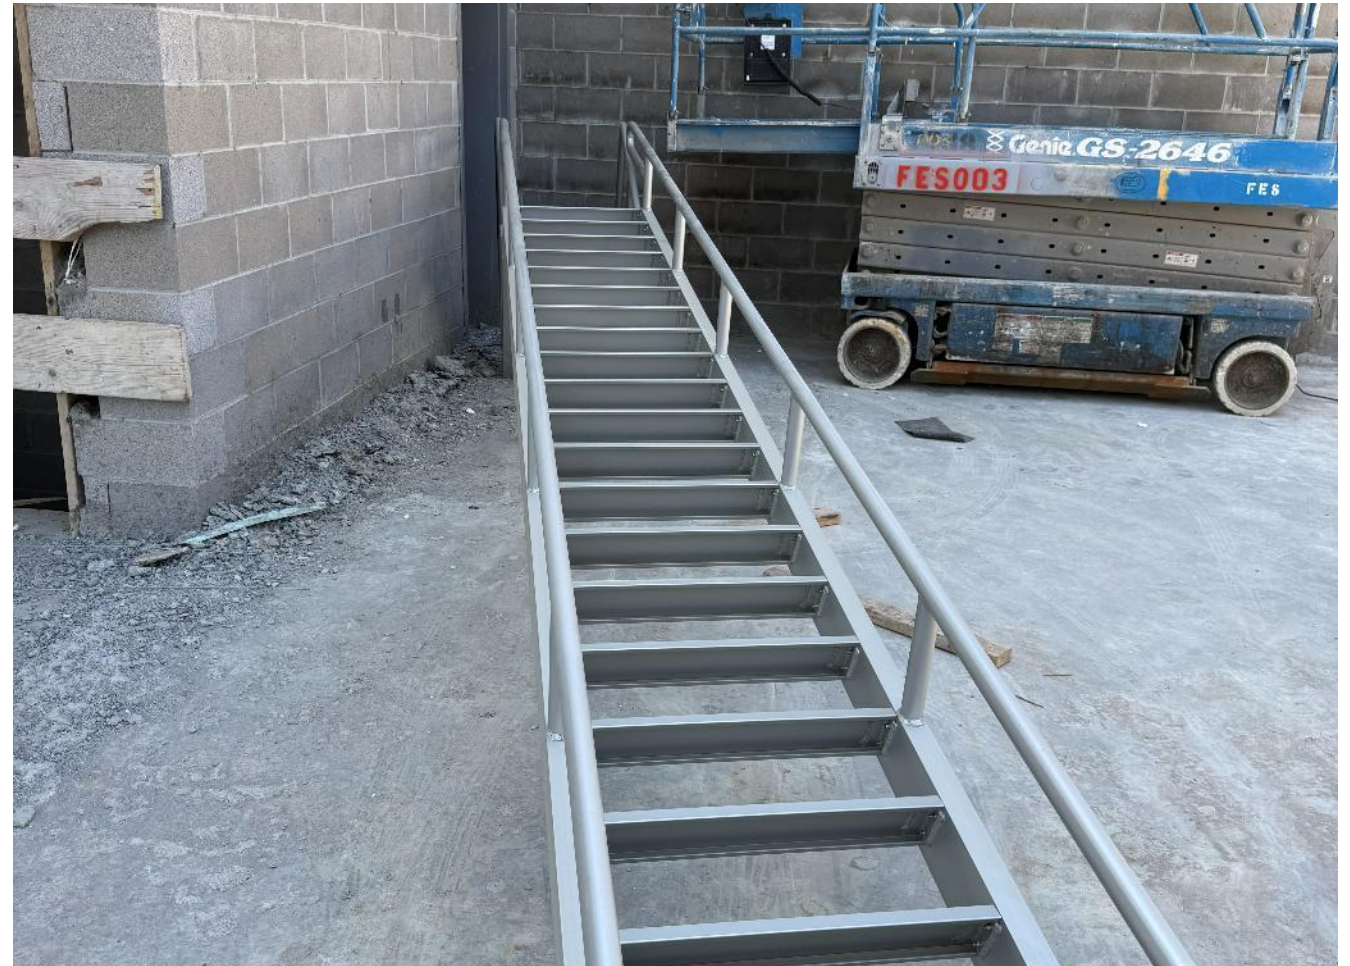

Week Ending August 28, 2026
