


New Henry Clay High School

Completed/Work in Progress:

- ❑ ICF walls and ICF wall framed openings are complete in all areas except for where in progress at areas F and G.
- ❑ Laying of CMU walls and the installation of hollow metal frames is underway.
- ❑ Under-slab plumbing/electrical and concrete slabs are complete except where in progress at area F.
- ❑ Above ceiling MEP installation is in progress at areas A, B and C.
- ❑ Installation of stairs in all areas but the Gym is complete.
- ❑ Exterior stone & brick veneer is complete in areas A & B, and in progress in area C, E & F.
- ❑ Interior metal stud wall & soffit framing is in progress at areas A, B, C, D, E & G.
- ❑ Areas A, B, C, D are dried-in with roofing systems in progress.
- ❑ CMU finishing & painting, and hanging drywall is in progress at areas A, B and C.
- ❑ Window trim, sills, and aluminum window installation is in progress at Areas A, B & C.
- ❑ Installation of terrazzo flooring and wall bases is in progress at Level 3 in areas A, B and C.

Upcoming Look Ahead:

- ❑ Begin steel erection at Area F.
- ❑ Continue above ceiling MEP and wall rough-ins.
- ❑ Continue interior metal stud wall and soffit framing in areas A, B & C.

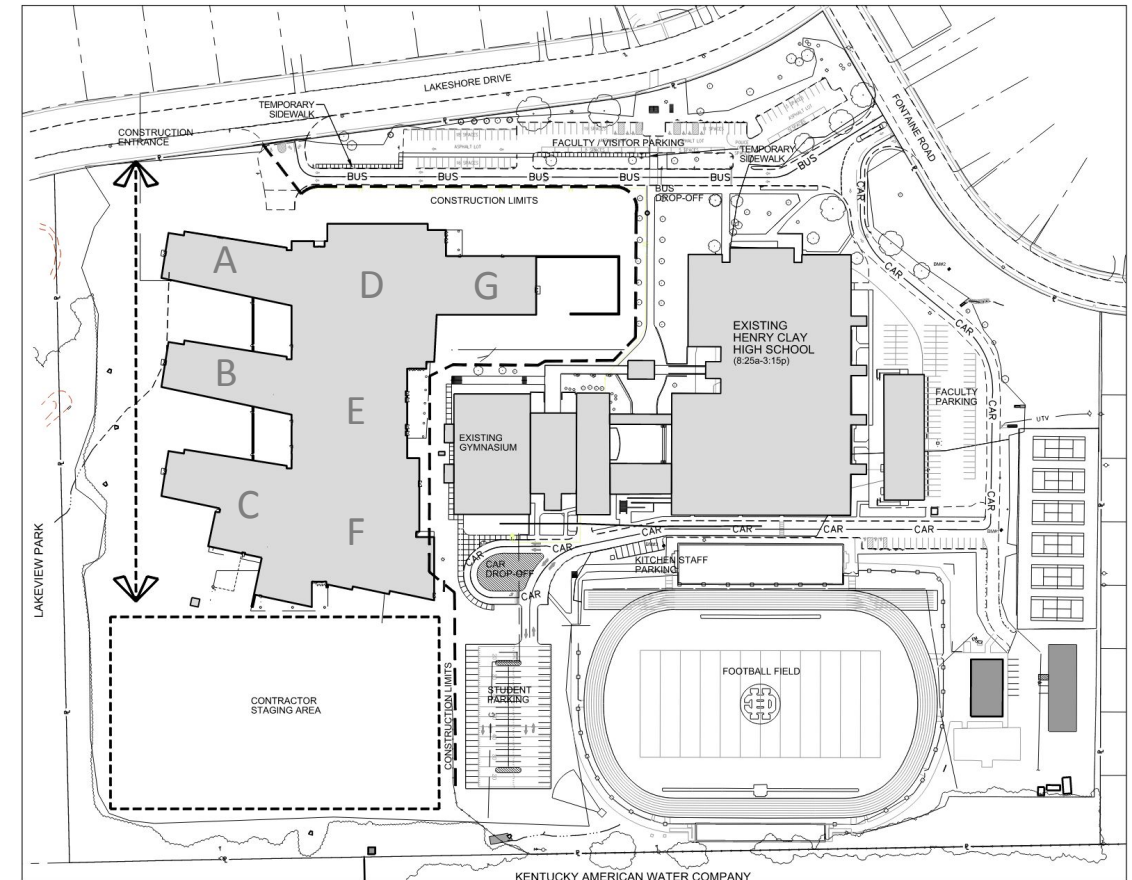

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Areas A, B, C (Classroom Wings): Installation of Aluminum Windows is in Progress



Week Ending September 04, 2026


New Henry Clay High School

Areas A, B, C (Classroom Wings): Installation of Aluminum Windows is in Progress



New Henry Clay High School

Area A (Classroom Wing): Drywall Taping and Mudding in Progress

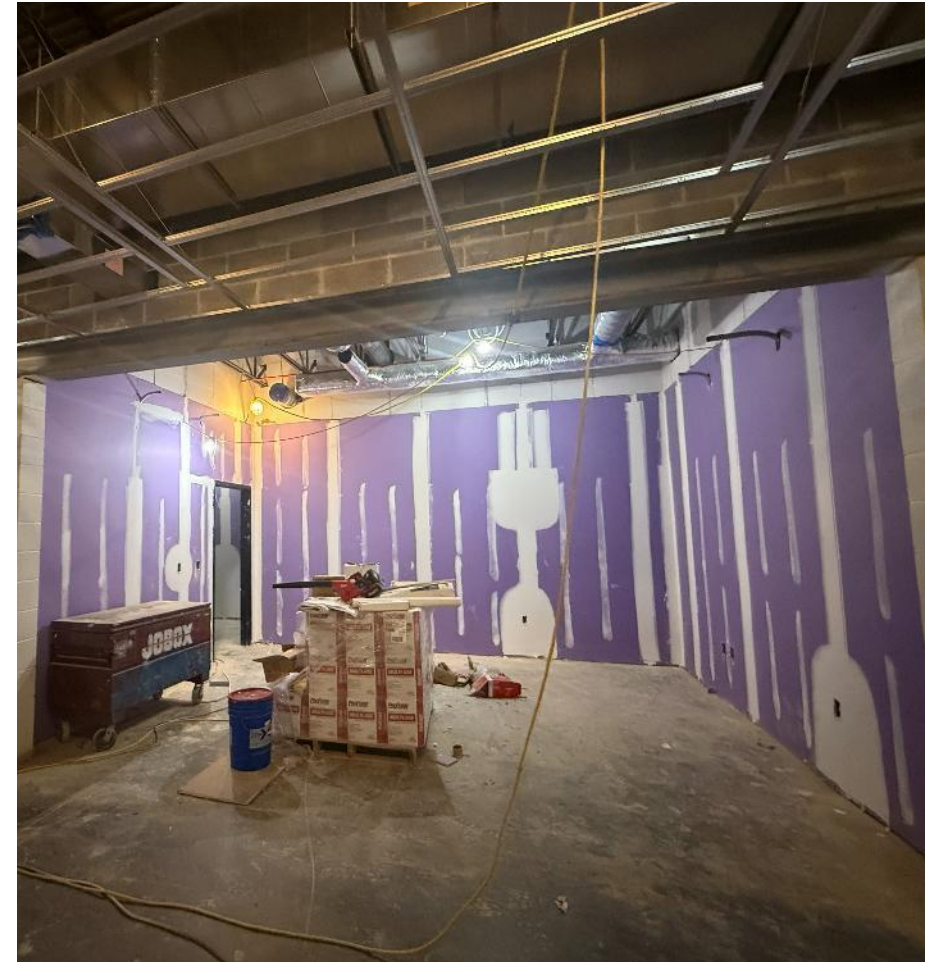

Week Ending September 04, 2026

New Henry Clay High School



Area D (Storm Shelter/Multi-Purpose Rm): SBS Roofing System Installation in Progress



Week Ending September 04, 2026

New Henry Clay High School

Area E (Gymnasium): SBS Roofing System Installation in Progress



Week Ending September 04, 2026

New Henry Clay High School

Level 3 Areas A, B, C (Classroom Wings): Spreading of Terrazzo Resin & Chip Mixture in Progress



Week Ending September 04, 2026
