



Measure H

STAY IN THE LOOP WITH UPDATES AND ANNOUNCEMENTS!

AT A GLANCE

- **Crocker Updates!**
- **North Jungle**
- **West MPR and Fire Alarm Replacement**



Pictured above : Grading and site infrastructure work

Crocker MPR & Admin

The project continues to make steady progress across the site. Site infrastructure and temporary facilities are advancing. The power and internet connections and plumbing work have been completed. Electrical, low-voltage, and data connections to the existing buildings have also been completed. Coordination of underground utilities continues, including review of existing conditions and new installations to support development of an updated utility plan.

The drive aisle and parking lot paving and striping have been completed, along with the pedestrian aprons for the ADA walkway.

Fence line adjustments, tree protection zones, and building pad grading are currently in progress, with grading anticipated to continue for approximately another few weeks.

Crocker & North Updates

Makerspace, Culinary Arts, North Jungle

Makerspace

Since construction began in June 2026, the former Lecture Hall has undergone significant renovation to support its transformation into Crocker's new Makerspace.

With the classroom improvements and finishes taking shape, the space has come together significantly, bringing the vision for the new Makerspace to life.

The renovated space is designed to support hands-on learning, creativity, and collaboration.



Pictured above : Casework and countertop installation

Culinary Arts

Phase II construction began in June 2026, bringing significant improvements to the Culinary Arts classroom.

The space has since taken shape with updated finishes, classroom infrastructure, and key installations that bring the overall design together.

With the major elements in place, the project continues to take shape through additional enhancements and finishing touches.



Pictured above : Casework, flooring, and ceiling tile installation

North Elementary School Jungle

The North Jungle project is currently progressing through the conceptual design phase, with the project team shaping the overall vision and evaluating potential layouts and features for the space.

Design development is focused on creating an outdoor environment that responds to the needs of both students and staff. The project supports the District's goal of enhancing the campus with a welcoming outdoor space that encourages learning, recreation, and student engagement.



West Updates


MPR, Fire Alarm Replacement

West MPR

The West MPR project continues to make progress across both exterior and interior areas. Site paving, striping of the drive aisle and parking lot striping are progressing. The remaining concrete flatwork is anticipated to be poured in mid-September, followed by landscape planting in October. Exterior building work is also advancing, with the canopy roof scheduled for installation next week, fiber cement installation continuing, and exterior painting anticipated to be completed in a few weeks.



Pictured above : Site paving progress

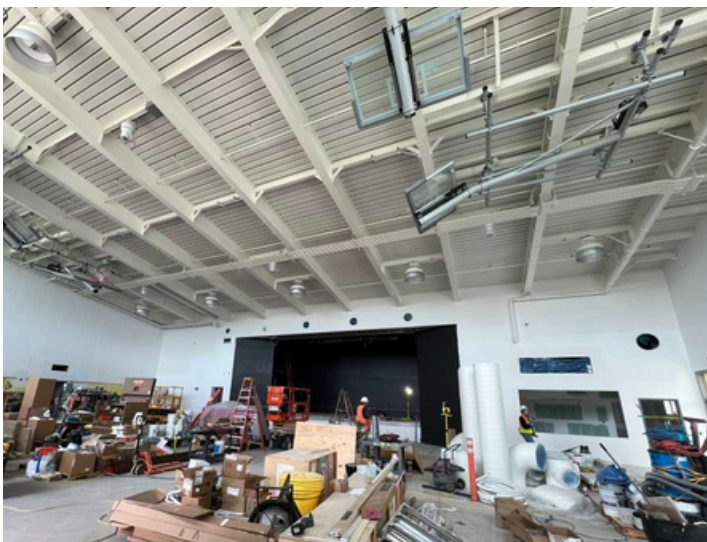

Pictured above : Interior and stage construction progress

Interior finishes and building systems are progressing as well. Epoxy flooring is expected to be completed. Tectum wall panel installation is scheduled to begin in the coming days, along with continued wood ceiling and wall panel work. At the stage, sheathing and stair framing are underway, after which production rigging and lighting installation will follow.

Kitchen equipment is being finalized, while coordination continues on the stage drapery and other remaining architectural and finish items.

West Fire Alarm Replacement

Fire alarm upgrades at the West campus began in June 2026 and have progressed through the major installation and system cutover activities. The project replaced older equipment with upgraded technology designed to improve detection, reliability, and overall fire protection.

The project has now transitioned into the closeout phase, with the primary construction and system work completed. The team is focused on addressing any remaining corrective items, completing final documentation, and coordinating the necessary closeout requirements to formally complete the project.



Please visit our website at:

<https://www.hcsdk8.org/measure-h/measure-h-projects>

for detailed Measure H Project updates!
