


# New Henry Clay High School

## ➤ Completed/Work in Progress:

- ICF walls and ICF wall framed openings are complete in all areas except for where in progress at area F.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are complete except where in progress at area F.
- Above ceiling MEP installation is in progress at areas A, B, C, D, E & G.
- Installation of stairs in all areas but the Gym is complete.
- Exterior stone & brick veneer is complete in areas A & B, and in progress in area C, E, F & G.
- Interior metal stud wall & soffit framing is in progress at areas A, B, C, D & E.
- Areas A, B, C, D are dried-in with roofing systems in progress.
- CMU finishing & painting, and hanging drywall is in progress at areas A, B and C.
- Window trim, sills, and aluminum window installation is in progress at Areas A, B & C.
- Installation of terrazzo flooring and wall bases is in progress at Level 3 in areas A, B and C.

## ➤ Upcoming Look Ahead:

- Continue steel erection at Area F.
- Continue above ceiling MEP and wall rough-ins.
- Continue interior metal stud wall and soffit framing.

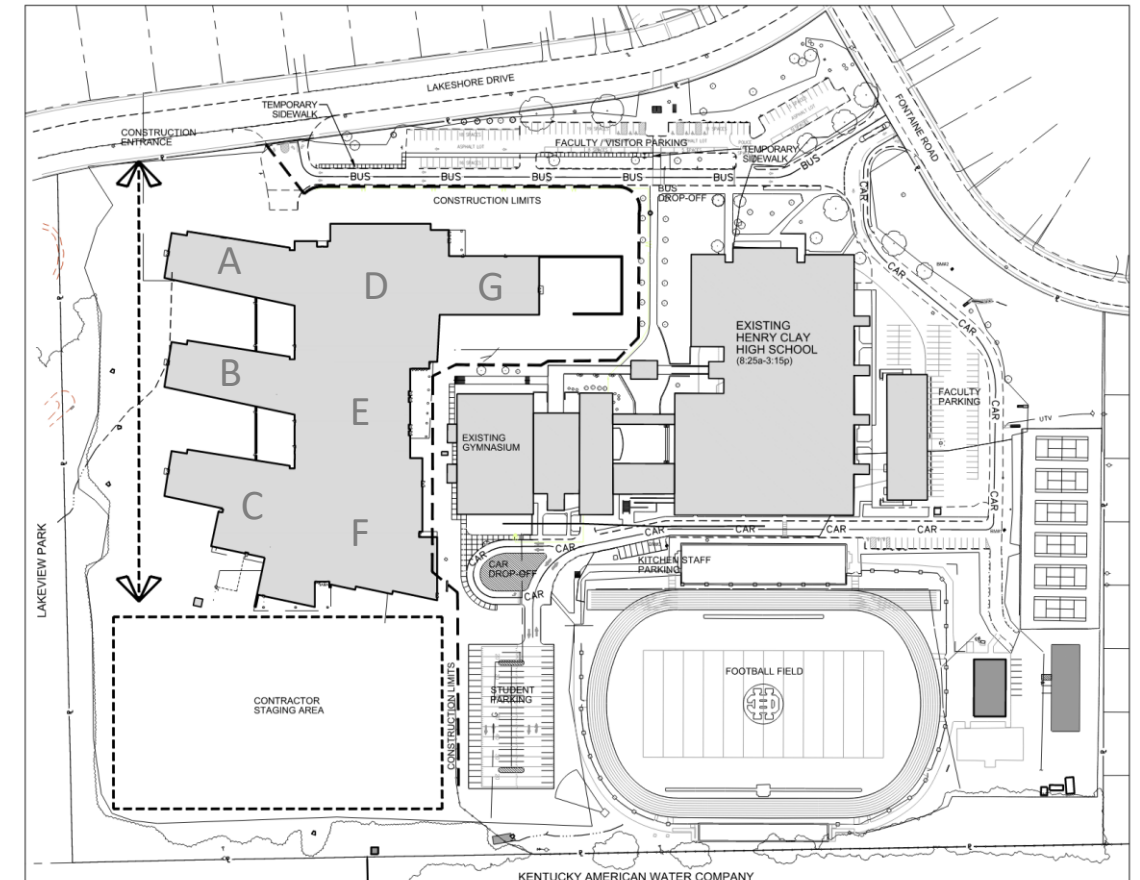

**B** PHASE 1 - BUILDING CONSTRUCTION CIRCULATION  
SCALE: N.T.S.

# New Henry Clay High School

Areas A, B, C (Classroom Wings): Installation of Aluminum Windows is in Progress



Week Ending September 11, 2026

# New Henry Clay High School

Area G (Media Center, Med Clinic, Classrooms): Installation of Stone Masonry Veneer is in Progress



Week Ending September 11, 2026

# New Henry Clay High School

Area F (Theater, Gymnasium): Installation of Stone & Brick Masonry Veneer is in Progress



Week Ending September 11, 2026

# New Henry Clay High School



Area F (Theater): CMU Walls, Hollow Metal Frames & Steel Erection is in Progress



Week Ending September 11, 2026

# New Henry Clay High School

Area F (Music Wing): ICF Walls, Stalla Frames, Foundations and Concrete Slabs on Grade is in Progress



Week Ending September 11, 2026

# New Henry Clay High School



Area G (Media Center & Medical Clinic): CMU Walls, Soffit Framing and Steel Erection is in Progress



Week Ending September 11, 2026

# New Henry Clay High School

Area G (Media Center & Medical Clinic): CMU Walls, Soffit Framing and Steel Erection is in Progress



Week Ending September 11, 2026
