



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

PROGRESS THIS WEEK:

- Pour In Place 1st Layer Installed – Site Playground
- Spectator Seating Area Poured – Site Pump Track
- High-Performance Coating – Area B2 Natatorium

GOALS NEXT 2 WEEKS:

- Pour Main Lobby & Vestibule – Area B1 Ground Floor
- Stone/Prep Gymnasium Floor
- Pave Binder Course East Side Of Parking Lot

PROJECT HIGHLIGHT THIS WEEK:

- West Parking Lot Passed Proof Roll; Paving On-going
- New Corridor Framed Providing Access From Area A1 Level 2 to Area A2 Level 2

Photos or Visual Assets:

DATE: October 2nd , 2026

MRCC PROJECT PROGRESS:



MILESTONE CHECKLIST:

- ☒ Construction Start – 9/18/25
- ☒ Foundations Complete 3/25/26
- ☐ Steel Complete
- ☐ Enclosed
- ☐ MRCC Substantial Completion
- ☐ Playfield Completion



Paving – Site West Parking Lot



Pour In Place 1st Layer Installed – Site Playground



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

DATE: October 2nd , 2026

MORE PROGRESS PHOTOS:




High-Performance Coating – Area B2 Natatorium



Spectating Area Concrete Poured – Site Pump Track



Water Meter Excavation – Site Northeast Corner

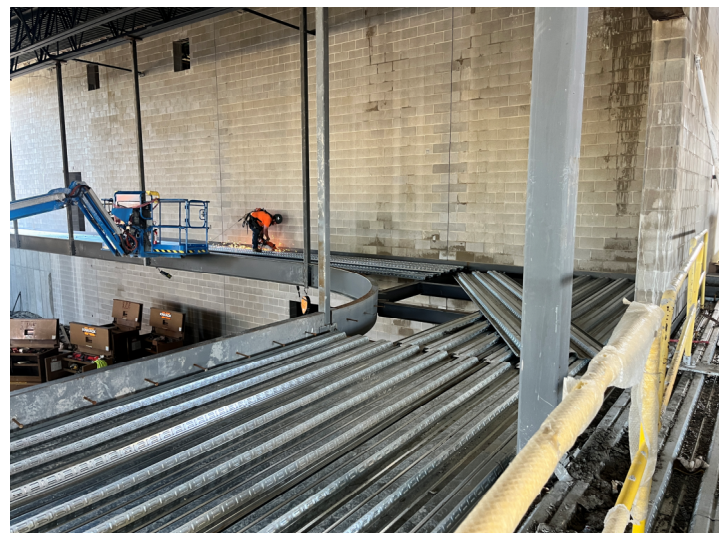

Walking Track Decking Installed – Area C2 Gymnasium
