



Altadena Flooring Project

Construction Progress Update

Report Date: 7/31/2026

Reporting Period - From:7/27/2026 To:7/31/2026


Prepared By: Martin Martinez

Summary of Work Completed:

- Construction is underway on the Altadena Elementary Flooring Replacement Project.
- Demolition has been completed in:
 - The Lobby
 - Lobby Hallways
 - Modular Classrooms
- Of the 39 spaces scheduled for new flooring, 29 spaces have already received the new LVT flooring.
- Flooring installation is progressing steadily, with work continuing throughout the campus.
- Installation of flooring began in the library and the modular classrooms.
- Contents have also been moved back in the finished classrooms.

Description: Demolition and preparation for new flooring.

Photos:

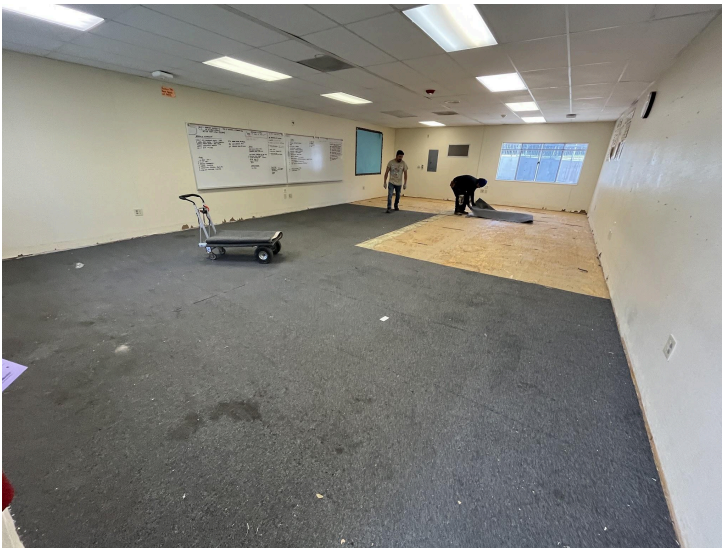

Description: Finished classrooms with contents back in.

Photos:



Construction Alerts

- **Description:** Demolition and preparation for new flooring is ongoing. The finished classrooms are receiving the contents back.
- **Site Impact:** Work continues throughout the site.

Upcoming Work: Preparation for new flooring is ongoing in the main lobby and the lobby walkways. Flooring installation will continue at the modular classrooms and the library.

Notes/Comments:

Thank you for your continued cooperation and patience as these improvements continue.

Reviewed By: Michael Dunning
