



Longfellow Modernization Progress Update

Construction Progress Update

Report Date: 7/24/2026

Reporting Period - From: 6/29/2026 To: 7/24/2026


Prepared By: Martin Martinez

Summary of Work Completed:

- Construction has officially begun on the Longfellow Elementary Modernization Project.
- All furniture, equipment, and classroom materials were successfully relocated from Longfellow to the Allendale swing site.
- The relocation effort took four full days to pack, transport, and unload all campus contents.
- Following the move, the contractor mobilized by installing temporary fencing and protective floor coverings throughout the campus.
- Areas that will remain in place during construction have been protected to prevent damage.
- Demolition is underway in Building B.
- Existing flooring, ceiling systems, and restroom fixtures have been removed.
- Demolition of Building B is approximately 90% complete.

Description: Packing and moving from Longfellow.

Photos:

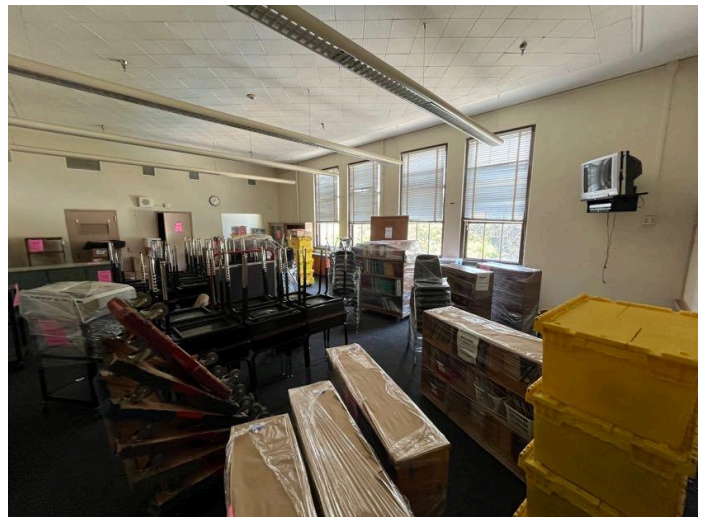

Description: Preparation for construction.

Photos:



Description: Demolition in building B.

Photos:



Construction Alerts

- **Description:** The site was completely emptied. The school contents were relocated to Allendale. The contractor took over the site and secured it for construction. Demolition is ongoing at both buildings A and B.
- **Site Impact:** The site is completely closed off. Approved personnel have to wear full PPE whenever onsite.

Upcoming Work: Demo will continue in both buildings.

Notes/Comments:

Thank you for your continued cooperation and patience as these improvements continue.

Reviewed By: Michael Dunning
