



Jackson ES Restroom and Utility Upgrades

Construction Progress Update

Report Date: July 10, 2026

Reporting Period - From: July 06, 2026 To: July 10, 2026


Prepared By: Dean Ramirez

Summary of Work Completed:

- Phase 4 Pre K and Kinder Restrooms - Started 6/8
- Kinder Restroom - Underground plumbing completed.
- Outdoor Portable Restroom - Dismantled and hauled off.

Photos:

Description: Kinder Restroom

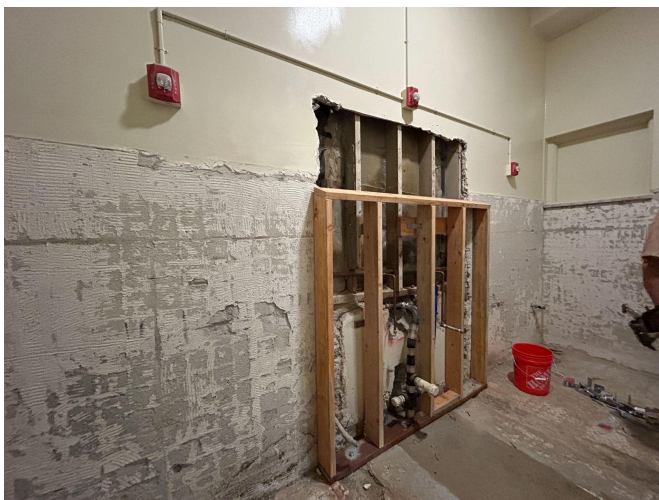

Description: Outdoor Portable Restroom



Construction Alerts

- **Description:** Phase 4 of the Restroom and Utility project will continue
- **Site Impact:** Please keep students and staff away from construction zones. We will continue to maintain clean and safe construction areas.

Upcoming Work:

- Pre K Restroom: Minor paint will be completed once the Kinder restroom is in the painting phase
- Kinder Restroom: Plumbing and electrical will continue. Tile prep will follow

Notes/Comments:

We thank you for your patience as we work to provide new, updated restrooms to serve students and staff at Jackson ES.

Reviewed By: Michael Dunning
