



## Altadena Flooring Project

### Construction Progress Update

**Report Date: 7/24/2026**

**Reporting Period - From:7/6/2026 To:7/24/2026**

**Prepared By: Martin Martinez**

---

#### Summary of Work Completed:

- Construction is underway on the Altadena Elementary Flooring Replacement Project.
  - Existing carpet is being removed and replaced with new luxury vinyl tile (LVT) flooring.
  - Demolition has been completed in:
    - Building A
    - Building B
    - Community Room
    - Teachers' Lounge
    - Principal's Office
  - Of the 39 spaces scheduled for new flooring, 25 spaces have already received the new LVT flooring.
  - Flooring installation is progressing steadily, with work continuing throughout the campus.
- 

**Description:** Demolition and preparation for new flooring.


#### Photos:





**Description:** Installation of the flooring.

**Photos:**

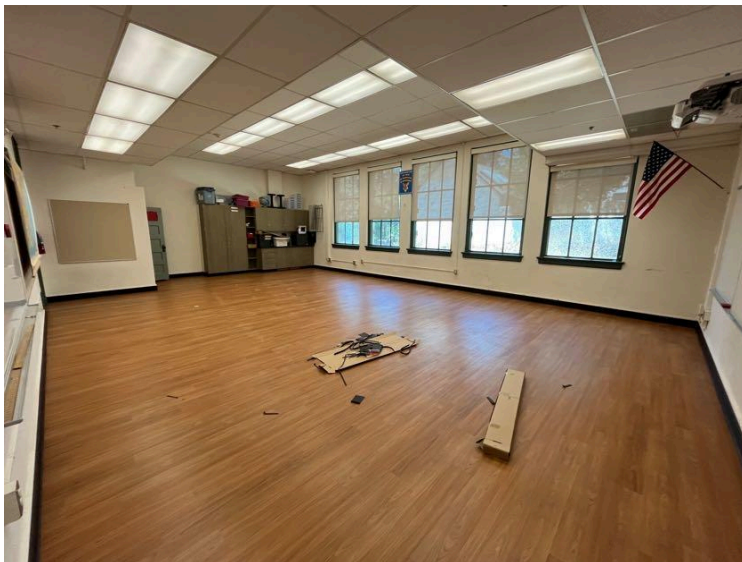


---

### Construction Alerts

- **Description:** Demolition and preparation for new flooring is ongoing. New flooring installation also began and is ongoing.
  - **Site Impact:** Work continues throughout the site.
-

**Upcoming Work:** Demolition of the main lobby and teacher workroom is set to commence on 7/27. Furniture will also begin to go back in the finished classrooms.

---

**Notes/Comments:**

Thank you for your continued cooperation and patience as these improvements continue.

---

**Reviewed By: Michael Dunning**
