



Altadena Flooring Project

Construction Progress Update

Report Date: 8/14/2026

Reporting Period - From:8/3/2026 **To:**8/14/2026


Prepared By: Martin Martinez

Summary of Work Completed:

- Construction was completed at Altadena Elementary Flooring Replacement Project.
 - Of the 39 spaces scheduled for new flooring all of them have been completed.
 - Cleaning crews also completed all the spaces. The only space remaining is the MPR and Stage.
 - All the teacher's contents were moved back in.
-

Description: New flooring was installed in all the spaces that had carpet.

Photos:

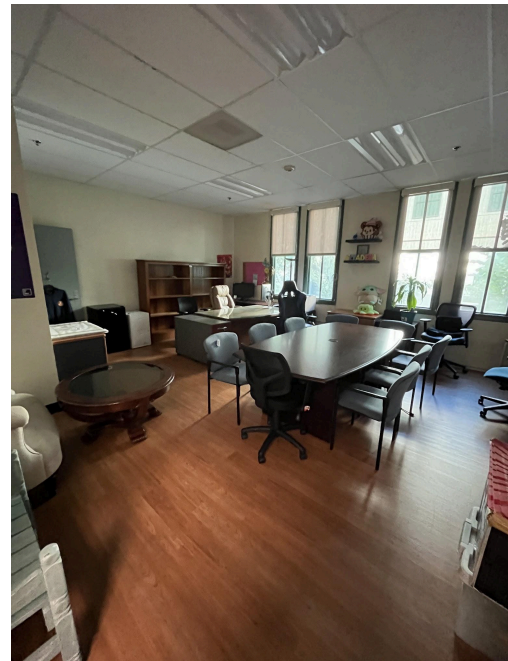

Description: Cleaning crews completed cleaning in the spaces floor was replaced.

Photos:



Construction Alerts

- **Description:** Flooring installation was completed. After the installation cleaning crews completed cleaning. Movers assisted in pushing the teachers' contents back in.
- **Site Impact:** None.

Upcoming Work: The cleaners are actively working inside the MPR and stage. Once finished they will demobilize.

Notes/Comments:

Thank you for your continued cooperation and patience as these improvements continue.

Reviewed By: Michael Dunning
