



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

PROGRESS THIS WEEK:

- Stone/Prep Floor – Area C2 Gymnasium
- Monoslope Install Ongoing – Site
- Sports Courts Paint & Striping – Site Sport Courts

GOALS NEXT 2 WEEKS:

- Install Windows – Area C1 South & West Elevation
- Pour Gymnasium Floor
- Pour Concrete For Splash Pad

PROJECT HIGHLIGHT THIS WEEK:

- Pour In Place Surface Completed – Site Playground
- Pump Track Concrete Pours Complete

Photos or Visual Assets:



Pour In Place Surface Completed – Site Playground



Sports Courts Painted & Striped – Site Sports Courts

DATE: October 9th , 2026

MRCC PROJECT PROGRESS:



MILESTONE CHECKLIST:

- ☒ Construction Start – 9/18/25
- ☒ Foundations Complete 3/25/26
- ☐ Steel Complete
- ☐ Enclosed
- ☐ MRCC Substantial Completion
- ☐ Playfield Completion




Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

DATE: October 9th , 2026

MORE PROGRESS PHOTOS:

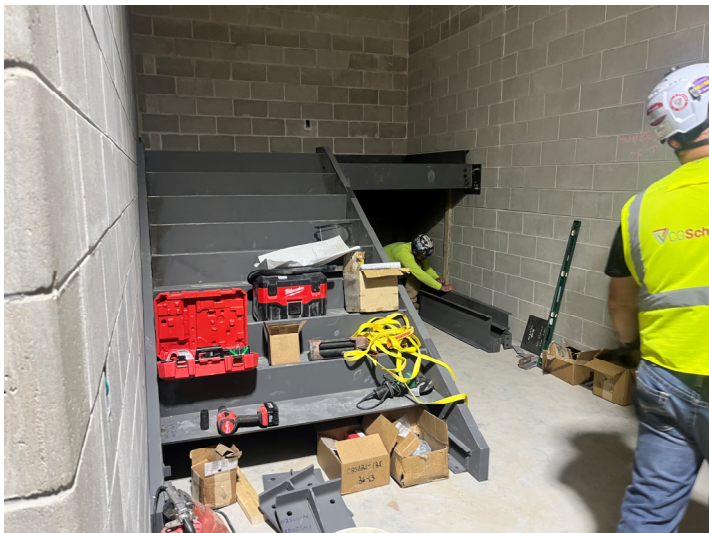

Stairs Install Progress – Area B1 Stair 4



Wood Floor Patching – Area A1 3rd Floor Classrooms



Monoslope Install Ongoing – Site West Of Playground



Stone/Prep Floor – Area C2 Gymnasium
