

New Henry Clay High School


➤ Completed/Work in Progress:

- ICF walls and ICF wall framed openings are complete in all areas except for where in progress at area F.
- Laying of CMU walls and the installation of hollow metal frames is largely complete except where underway at Area F.
- Under-slab plumbing/electrical and concrete slabs are complete except where in progress at area F.
- Above ceiling MEP installation is in progress at areas A, B, C, D, E & G.
- Installation of stairs in all areas but the Gym is complete.
- Exterior stone & brick veneer is complete in areas A & B, and in progress in area C, E, F & G.
- Interior metal stud wall & soffit framing is in progress at areas A, B, C, D & E.
- Areas A, B, C, D & E are dried-in with roofing systems in progress.
- CMU finishing & painting, and hanging drywall is in progress at areas A, B, C & D.
- Window trim, sills, and aluminum window installation is in progress at Areas A, B & C & G.
- Installation of terrazzo flooring and wall bases is in progress at areas A, B and C.
- Installation of Alum. curtain wall systems is in progress at Area A.

➤ Upcoming Look Ahead:

- Continue steel erection at Area F.
- Continue above ceiling MEP and wall rough-ins.
- Continue interior metal stud wall and soffit framing.

Week Ending October 09, 2026

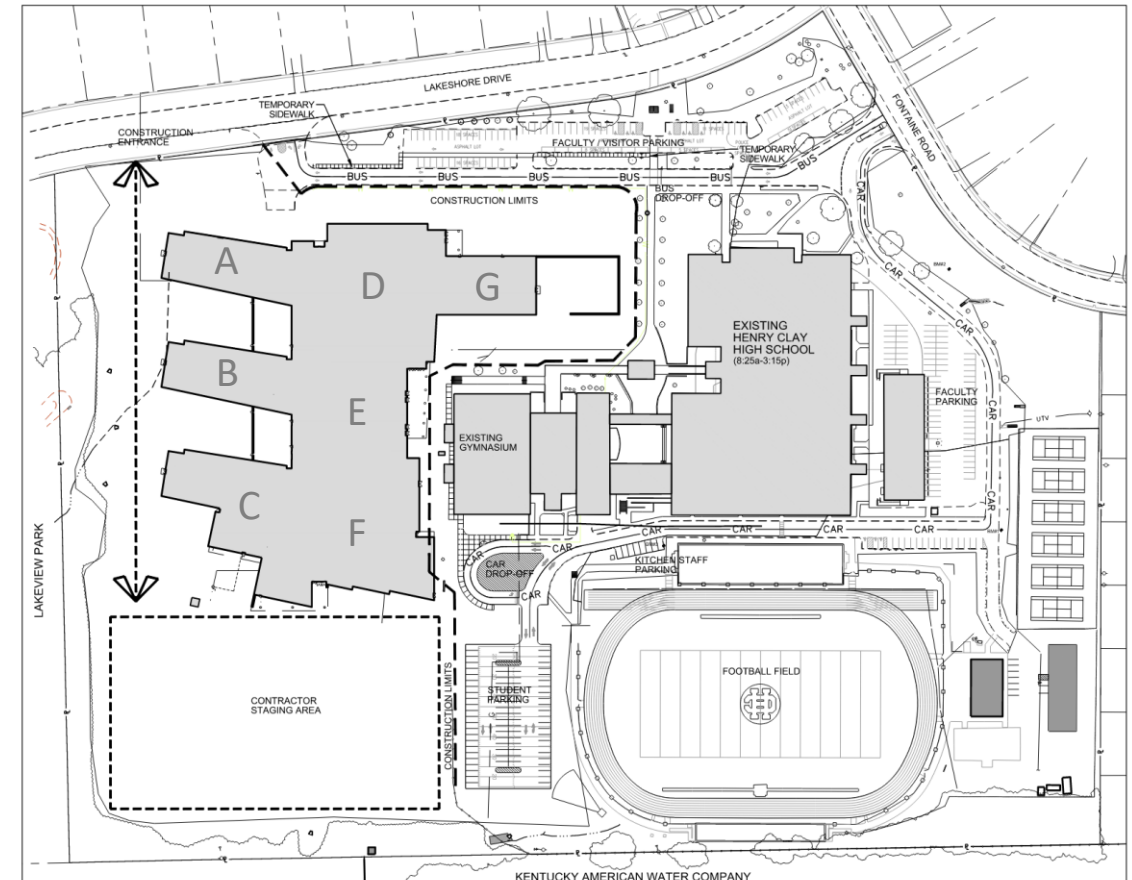

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Area A (Classroom Wing): Aluminum Curtain Wall Installation Underway at Stairwell



Week Ending October 09, 2026

New Henry Clay High School

Area D (Main Admin): Stone Veneer Installation in Progress




New Henry Clay High School

[Left Image]: Area G (Media Center): Stone Veneer and Cold-Formed Metal Framing Installation in Progress
[Right Image]: Area D (Main Admin): Cold-Formed Metal Framing & SBS Roofing System in Progress at Canopy



New Henry Clay High School

Level 2 Area D (Main Admin): Hollow Metal Frames and Framing of Light-Guage Metal Stud Walls is in Progress

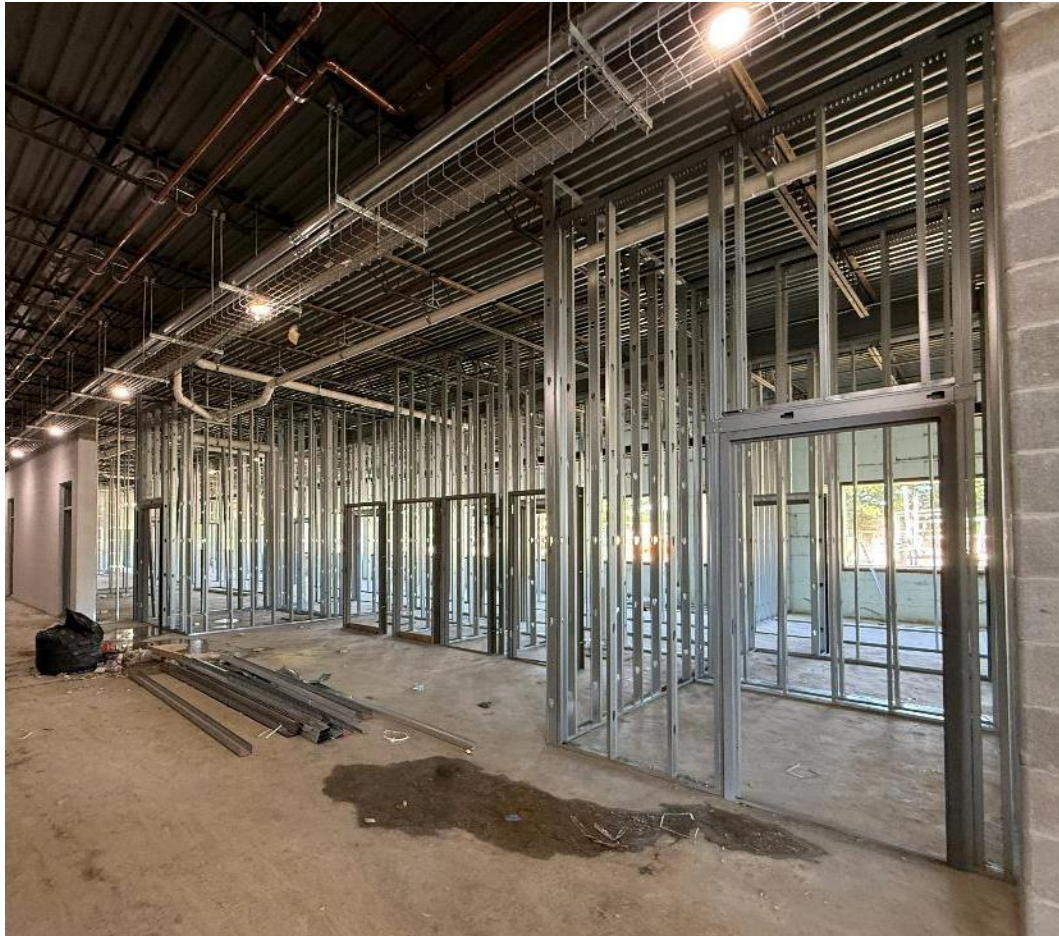

New Henry Clay High School



Area E (Gymnasium): Foundations & Steel Erection for Canopy is in Progress



New Henry Clay High School

Areas C & F (Cafeteria & South Lobby): Cold-Formed Metal Framing in Progress at Canopy/Overhang



Week Ending October 09, 2026

New Henry Clay High School



Area F (Music Classrooms): ICF Walls, CMU Walls, Hollow Metal Frames & Steel Erection is in Progress

