


New Henry Clay High School

➤ Completed/Work in Progress:

- Completed foundations in theater.
- Completed erection of roof bearing steel at area F.
- Completed pouring terrazzo flooring at classroom wings A, B & C.
- Completed hanging drywall in classroom wings of Areas A, B & C.
- Installation of sprinkler main in progress.
- Installation of ductwork is in progress at level 3.
- Installation of aluminum windows, curtain walls and storefront systems is in progress.
- Stone and brick veneer is in progress at areas D & F.
- Metal stud wall framing in progress at all areas except for area F.
- Block filler, priming & first coat of paint in progress at areas A, B & C.
- Drywall priming and painting in progress at area A.

➤ Upcoming Look Ahead:


- Complete ICF in area F.
- Complete electrical under-slab rough-ins at area F.
- Complete structural steel.
- Continue site work.
- Continue brick & stone veneer in areas D & F.
- Continue and complete roof dry-in
- Continue terrazzo flooring and wall base at north-south corridors.
- Continue framing metal stud walls and soffits at areas D, E & G.
- Continue installing aluminum windows, storefront and curtain wall systems.

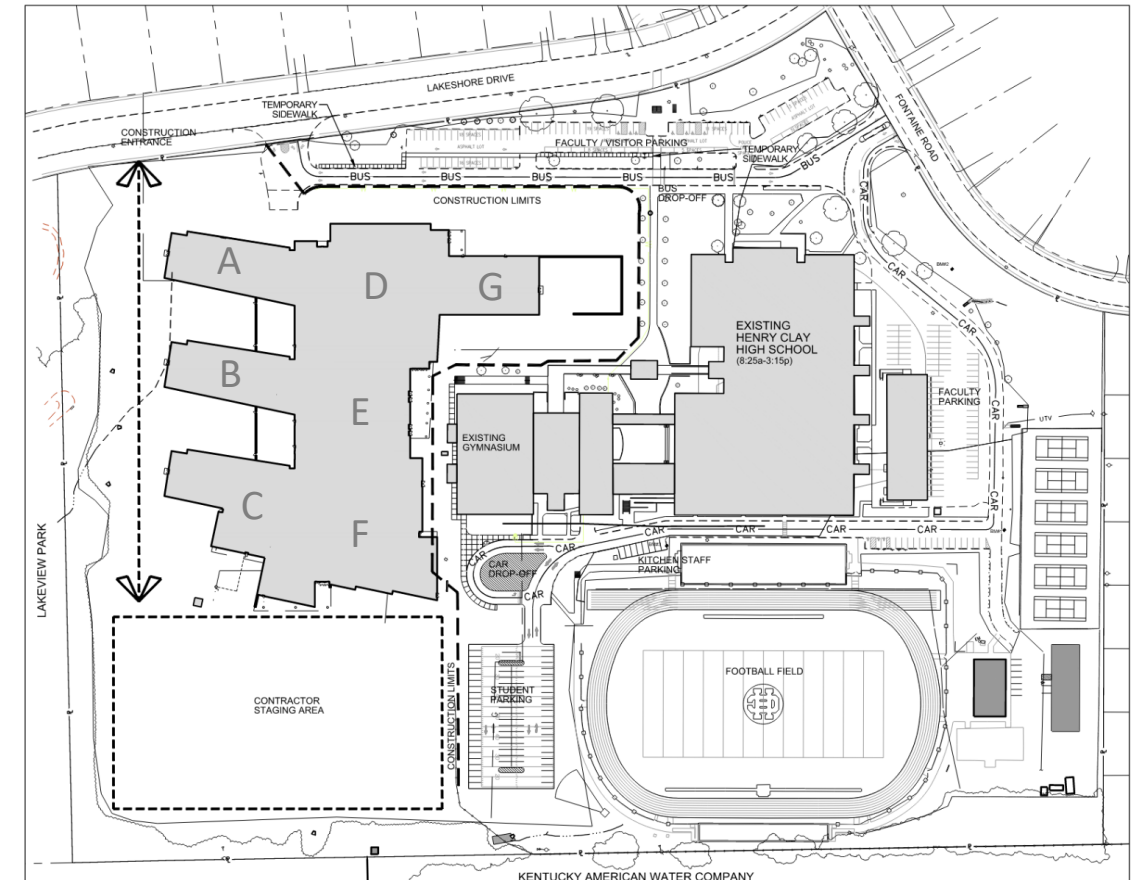

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Areas A, B & C (Classroom Wings): Aluminum Curtain Wall Installation Underway at Stairwells

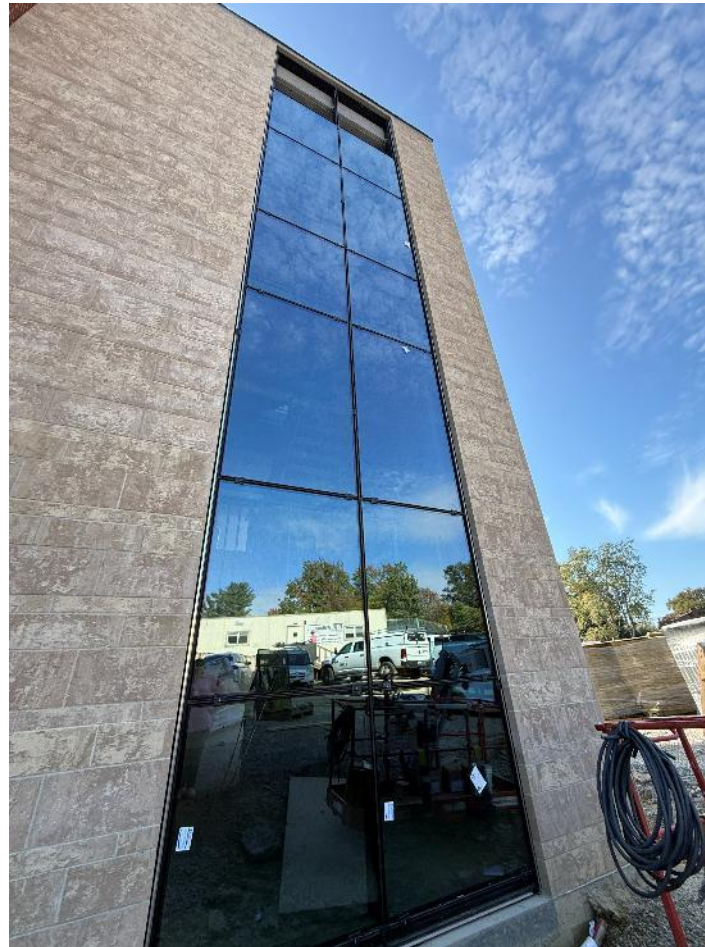


Week Ending October 16, 2026

New Henry Clay High School




Area D (Main Admin): Stone Veneer Installation in Progress

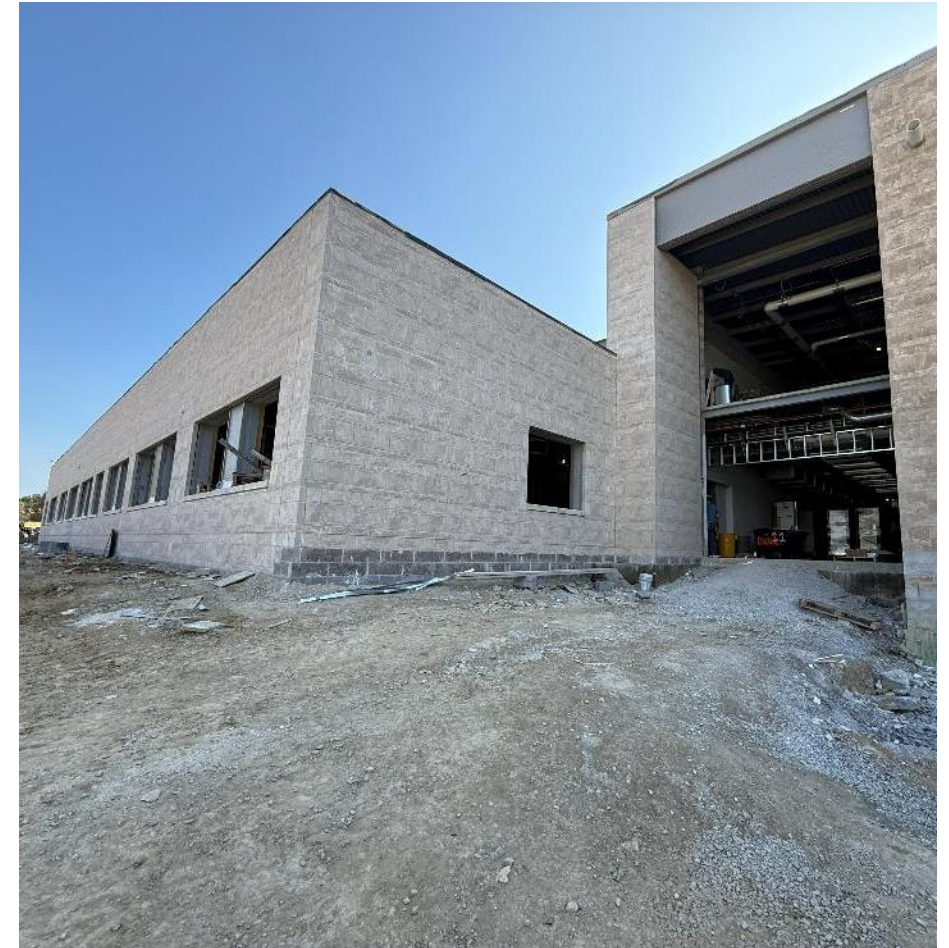

Week Ending October 16, 2026

New Henry Clay High School

Level 2 Area G (Media Center, Med Clinic, Athletic Offices): Framing of Light Gauge Metal Stud Walls in

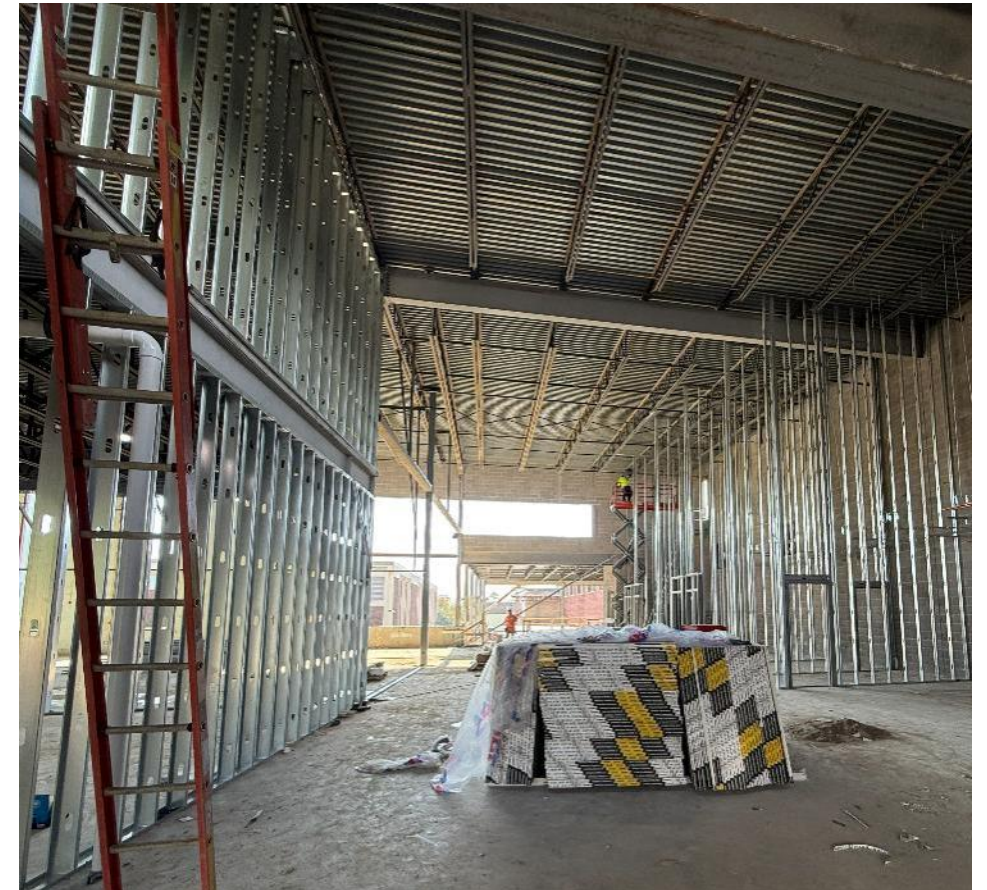

Week Ending October 16, 2026

New Henry Clay High School



Area E (Gymnasium): Canopy Steel Erection is Complete



New Henry Clay High School

[Left Image]: Areas A, B, & C (Classroom Wings): CMU Finishing & Priming and Terrazzo Flooring in Progress


[Right Image]: Areas A, B, & C (Classroom Wings): Hanging of Drywall Continues at Walls, Ceilings and Soffits

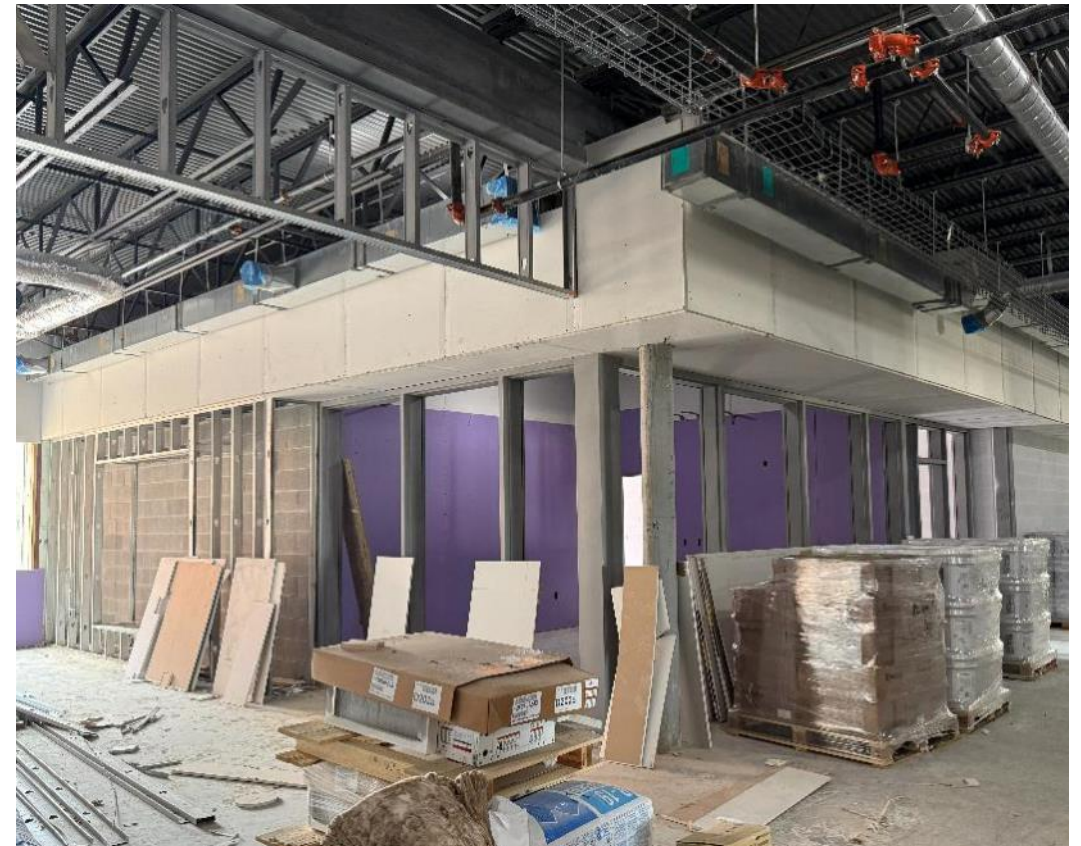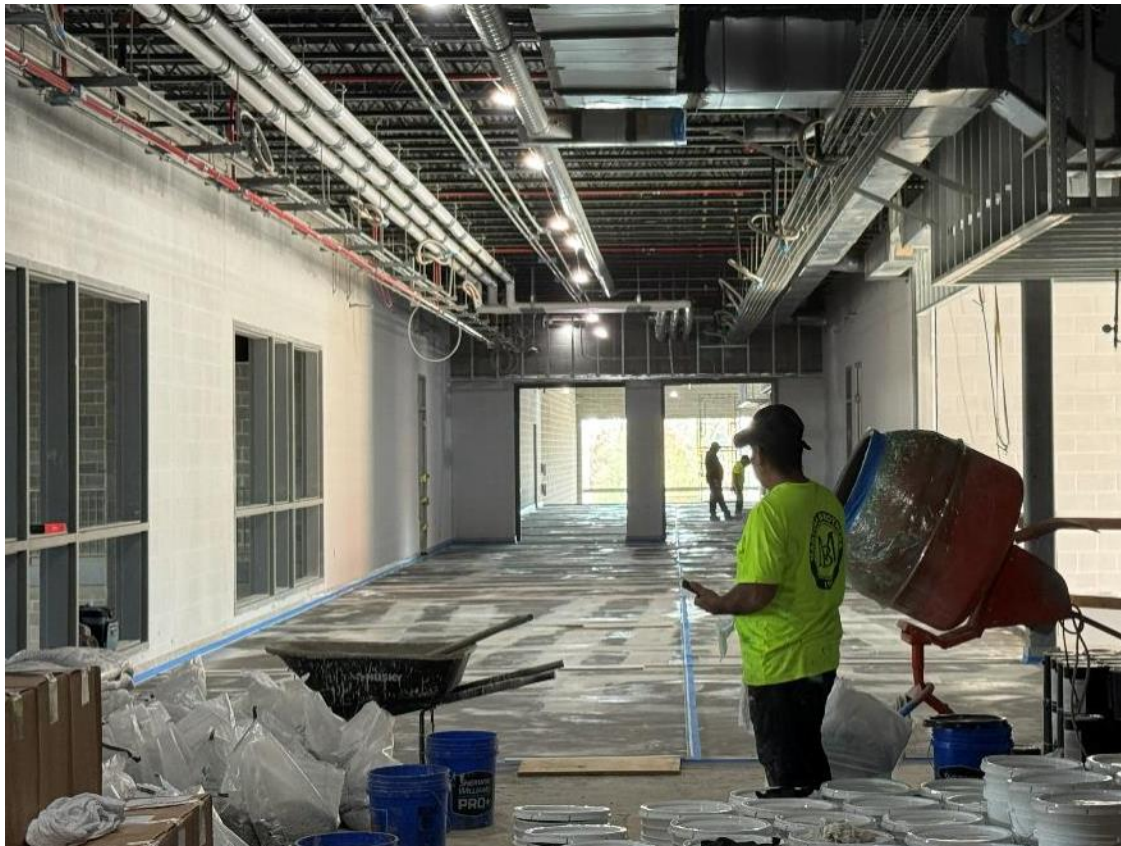

New Henry Clay High School



Level 1 Area A (Classroom Wing): Painting of Accent Walls and Gypsum Ceilings in Progress

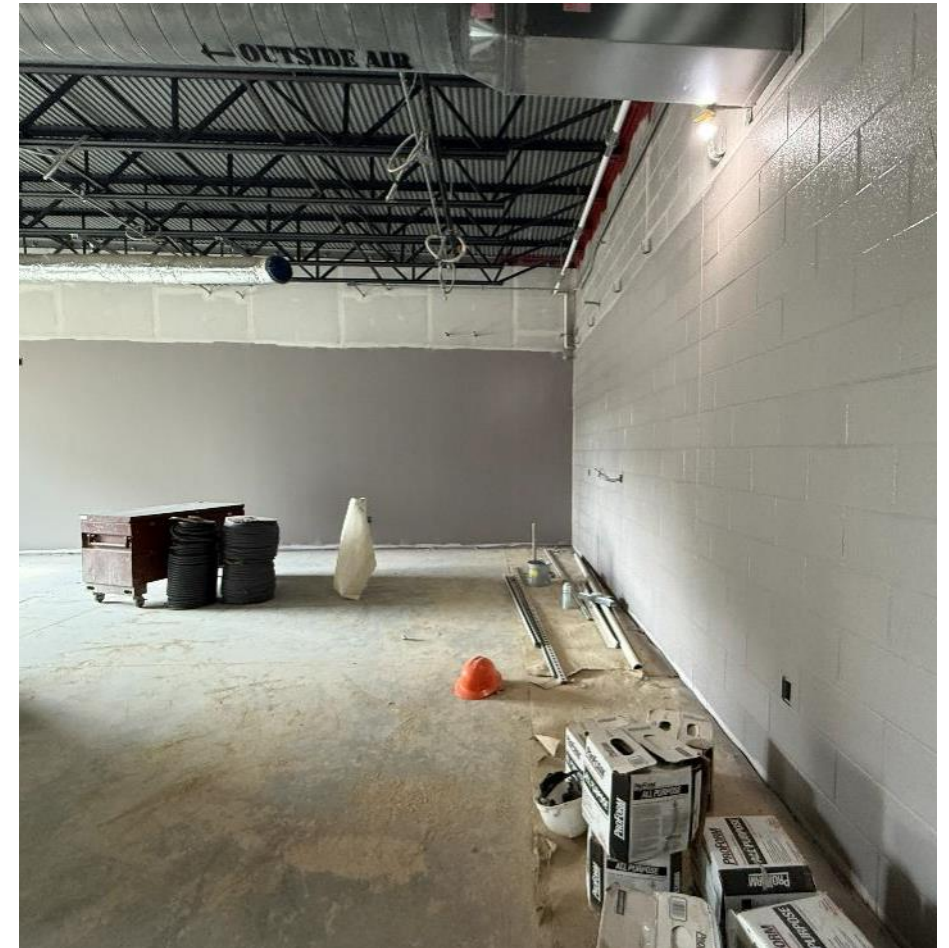

Week Ending October 16, 2026

New Henry Clay High School



Areas A, B, & C (Classroom Wings): Installation of Aluminum Storefront Systems is Underway



Week Ending October 16, 2026
