


PIERCE SCHOOL WEEKLY UPDATE, 10/23/26

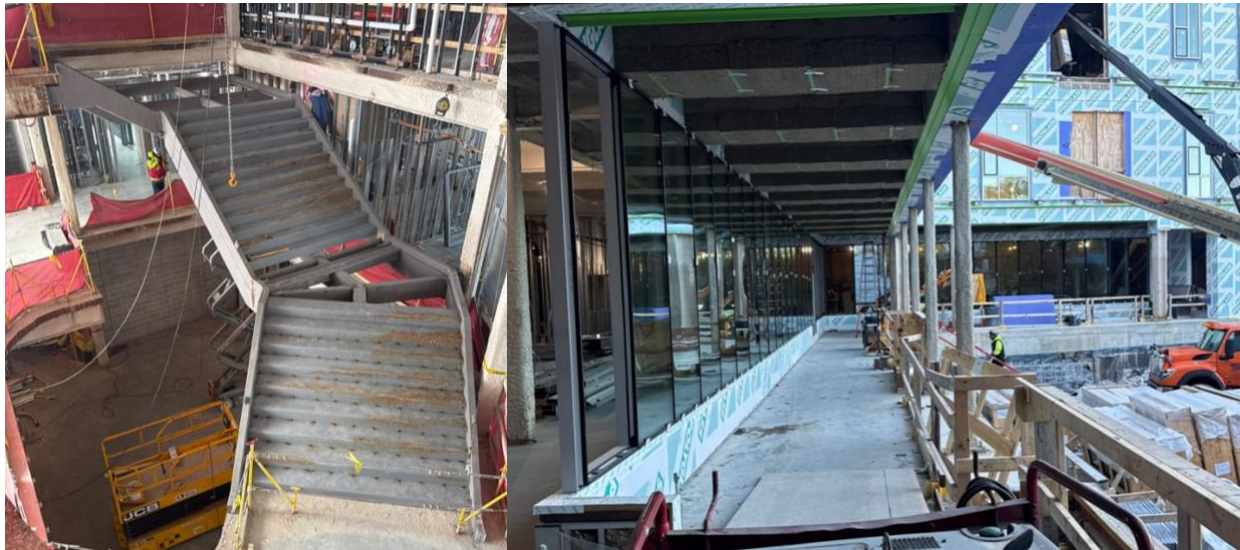

Note: there is work anticipated for Saturday 10/24

THIS WEEK (Oct. 20-24)

- Inspect and close up walls on B3
- Continue with drywall, reveals on A3
- Continue with OH MEP's and inspections, B3
- Interior framing on A1
- Drywall in mechanical room, A1
- Installation of Stair #1 (main stair)
- Brick finishes on South B, starts on West
- Metal panels complete A West
- Install glazing at cafeteria curtainwall
- OH duct, plumbing rough, elect @ Hist. Bldg.
- Stair work, Historic Building South end
- Infill basement door North, Hist. Bldg.
- Continue amphitheater footings, Pierce vestibule structure and backfill

ANTICIPATING NEXT WEEK (Oct. 27-31)

- Inspect and close up walls on B3
- Continue with OH MEP's on A2 West, B3
- Interior framing on A1
- Lay out MEP pads in mechanical room, A1
- Complete installation of Stair #1 (main stair)
- Brick continues on B West, begins B North
- Complete slate East Building B
- Install glazing B West
- Continue with coping at roof edge
- OH duct, plumbing rough, elect @ Hist. Bldg.
- Wall opening at Hist. Bldg. entrance NW
- Prep generator pad, Historic Building
- Continue amphitheater site walls, Pierce vestibule structure

Narrative:

Pierce Park/School Street:

Punch list work was ongoing. The grass continues to grow well; fence will be relocated the week of 10/26 to open the sidewalks and basketball court to the public. Test pits continued on School Street this week with additional police details to manage traffic.

Building A:

Walls on A3 continue to be finished, in classrooms and corridors. Overhead mechanical/fire protection piping, duct and insulation is ongoing on A2, along with drywall wall tops, acoustic sealing, firestopping and blocking. On Level 1, the mechanical room drywall at walls and the sound ceiling accelerated, and overhead pipe continued along with pressure testing. Painting the CMU in the gyms began this week.

On the exterior, metal panels are nearly complete on the West elevation, and roof edge work is progressing from the North

to the West. Window pressure plates and snap caps were installed. Sitework continued with further excavation in the amphitheater area for site walls; initial footings were placed with more to follow.

Building B:

Overhead mechanical/fire protection piping, plumbing, duct and insulation continued on B3; inspections were ongoing as areas were ready. On B1, the floor slab on the SW side is being ground down to correct some elevation issues. Stair #1 installation continued with treads and risers installed from L2 to L3.

On the exterior, the masonry crew finished brick on the South/West elevation and will relocate the hydromobile to the North side on Saturday. The slate installation on the East is now about 90% complete. The curtainwall at the cafeteria received glass this week, closing in one of the remaining large openings in the building. Framing of the overhang at the West end was completed this week.

Historic Building:

Interior framing and drywall continued, and the electrical in-wall work was ongoing. Plumbing rough continued, and wall furring was ongoing at the South Stair. MEP overhead work progressed in the basement. The area around the North entrance was backfilled, and the door to the basement has been prepared to be filled in with concrete.

For other project details, please visit the Project Website: <https://www.psbma.org/district-projects/pierce-school-building-project> To sign up for Project Updates, please go to: <https://www.brooklinema.gov/list.aspx?ListID=816>

