



PROJECT STATUS Phase 1

Edison, Chalmers & Intermediate



- **BILLINGS**


- Billed 23% thru September for Phase 1

- **CONTINGENCIES & ALLOWANCES**

- Total Balances Phase 1 = \$2,481,580
- Upcoming Items – Nothing Currently




EDISON ELEMENTARY

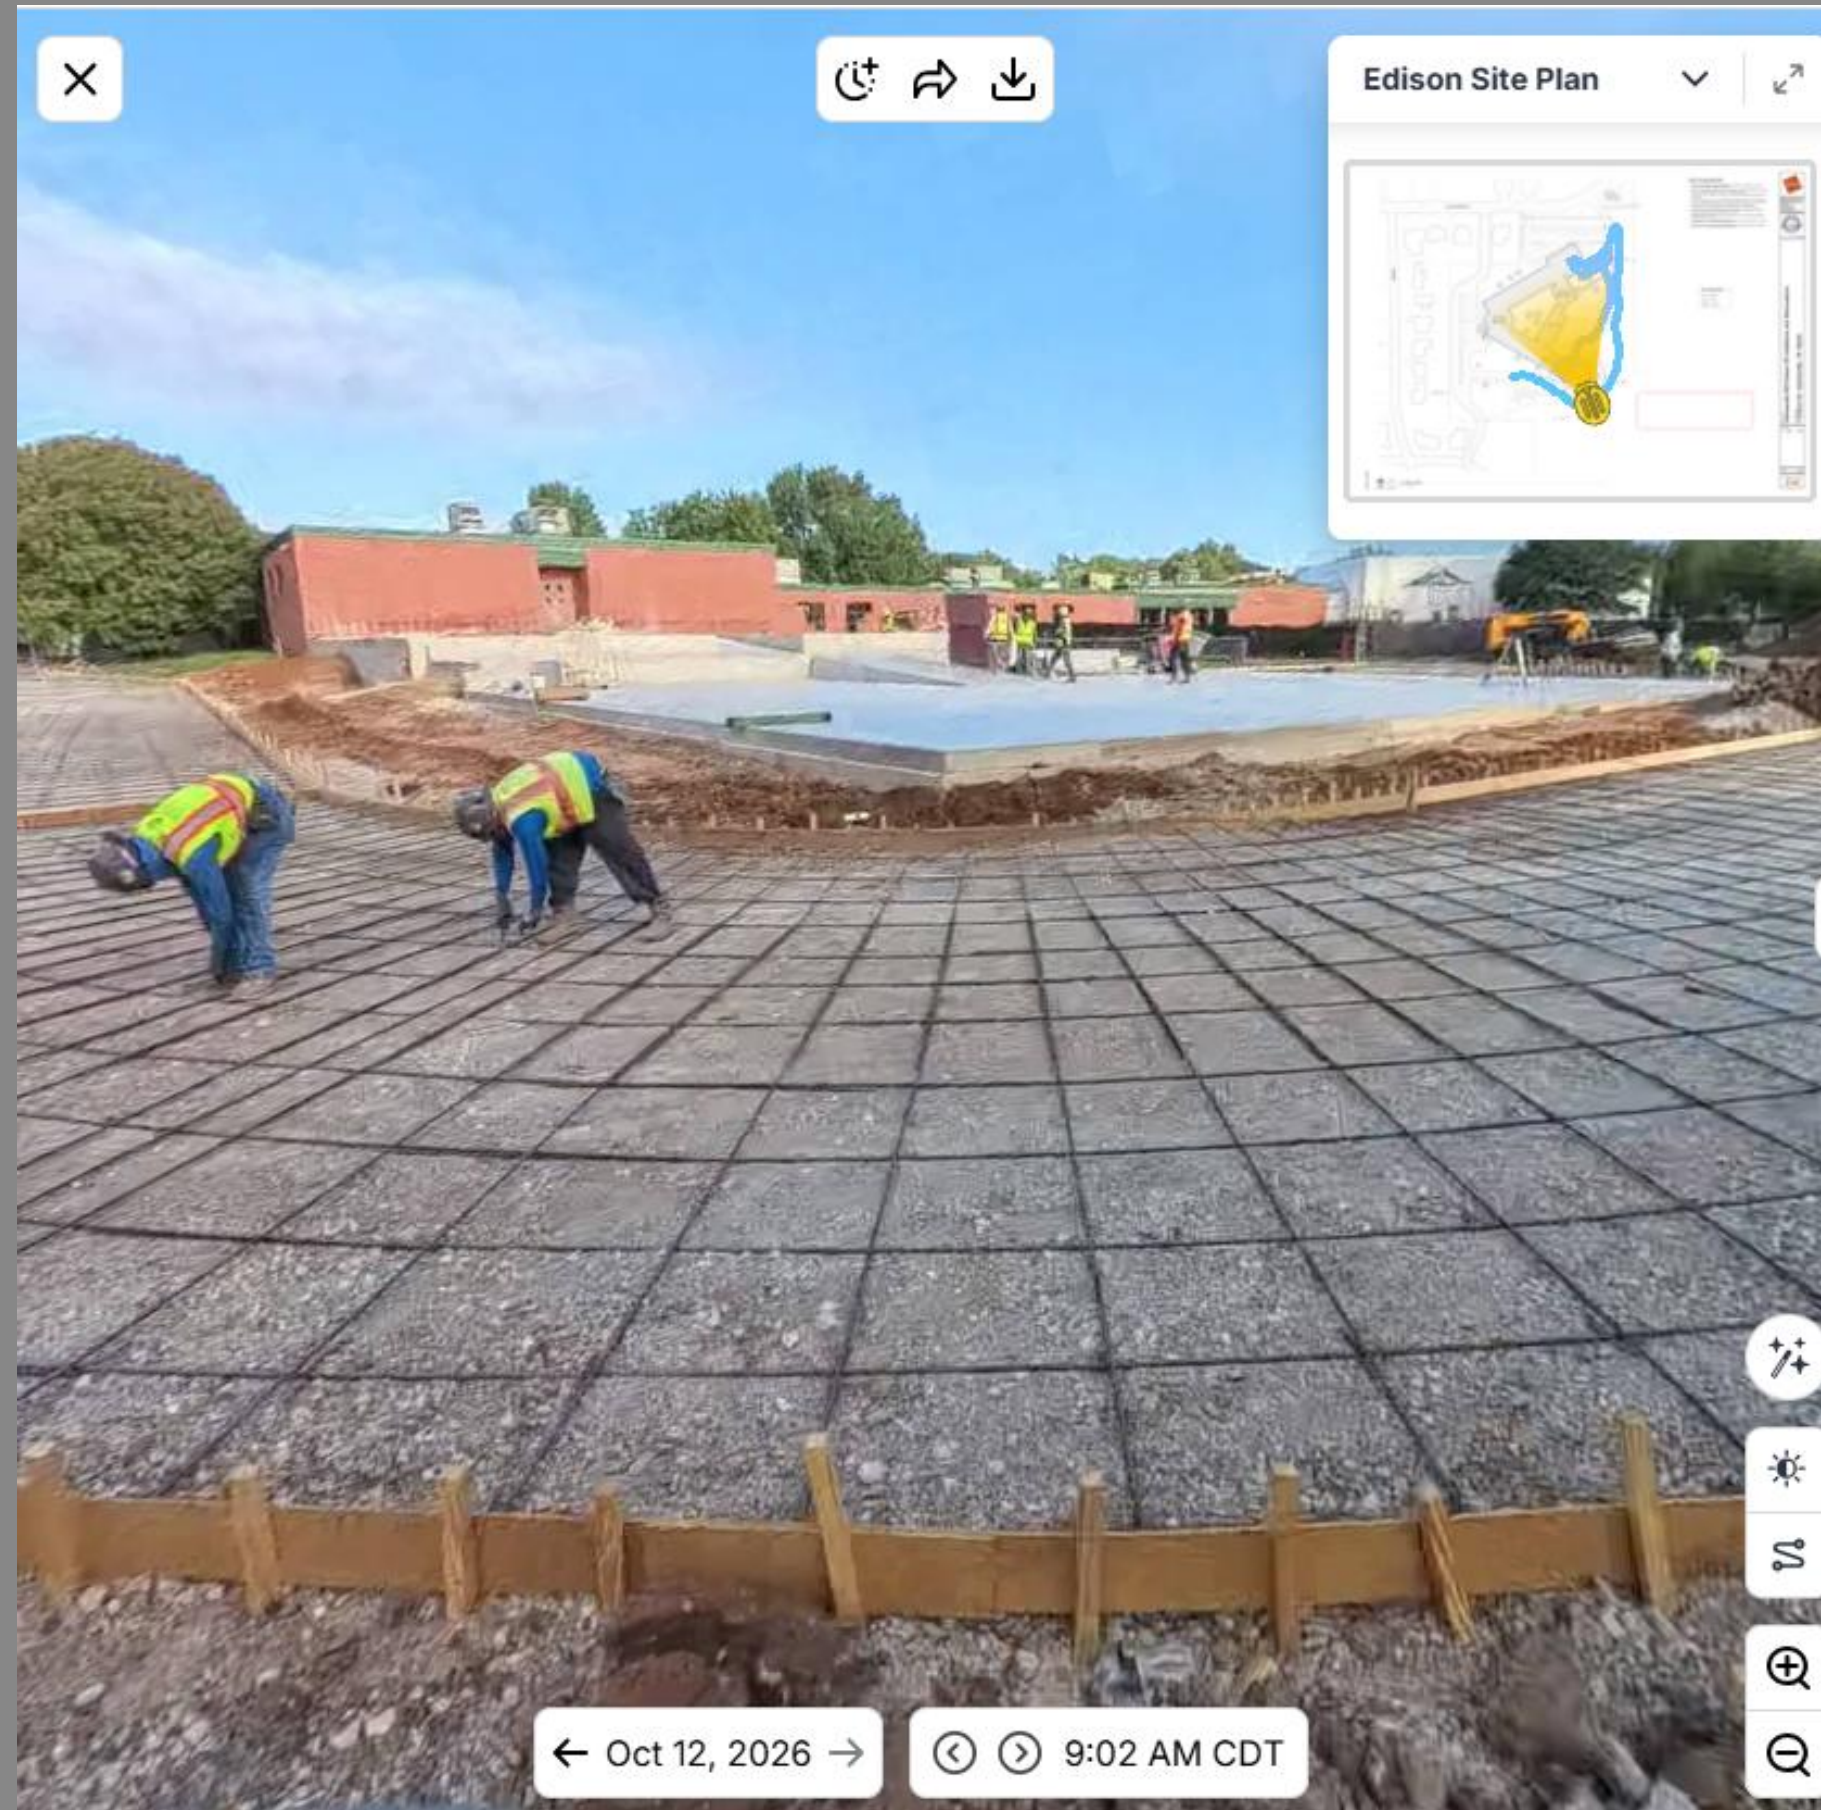

- Area F Slab Pour & Paving Prep – Sept to Oct

EDISON ELEMENTARY

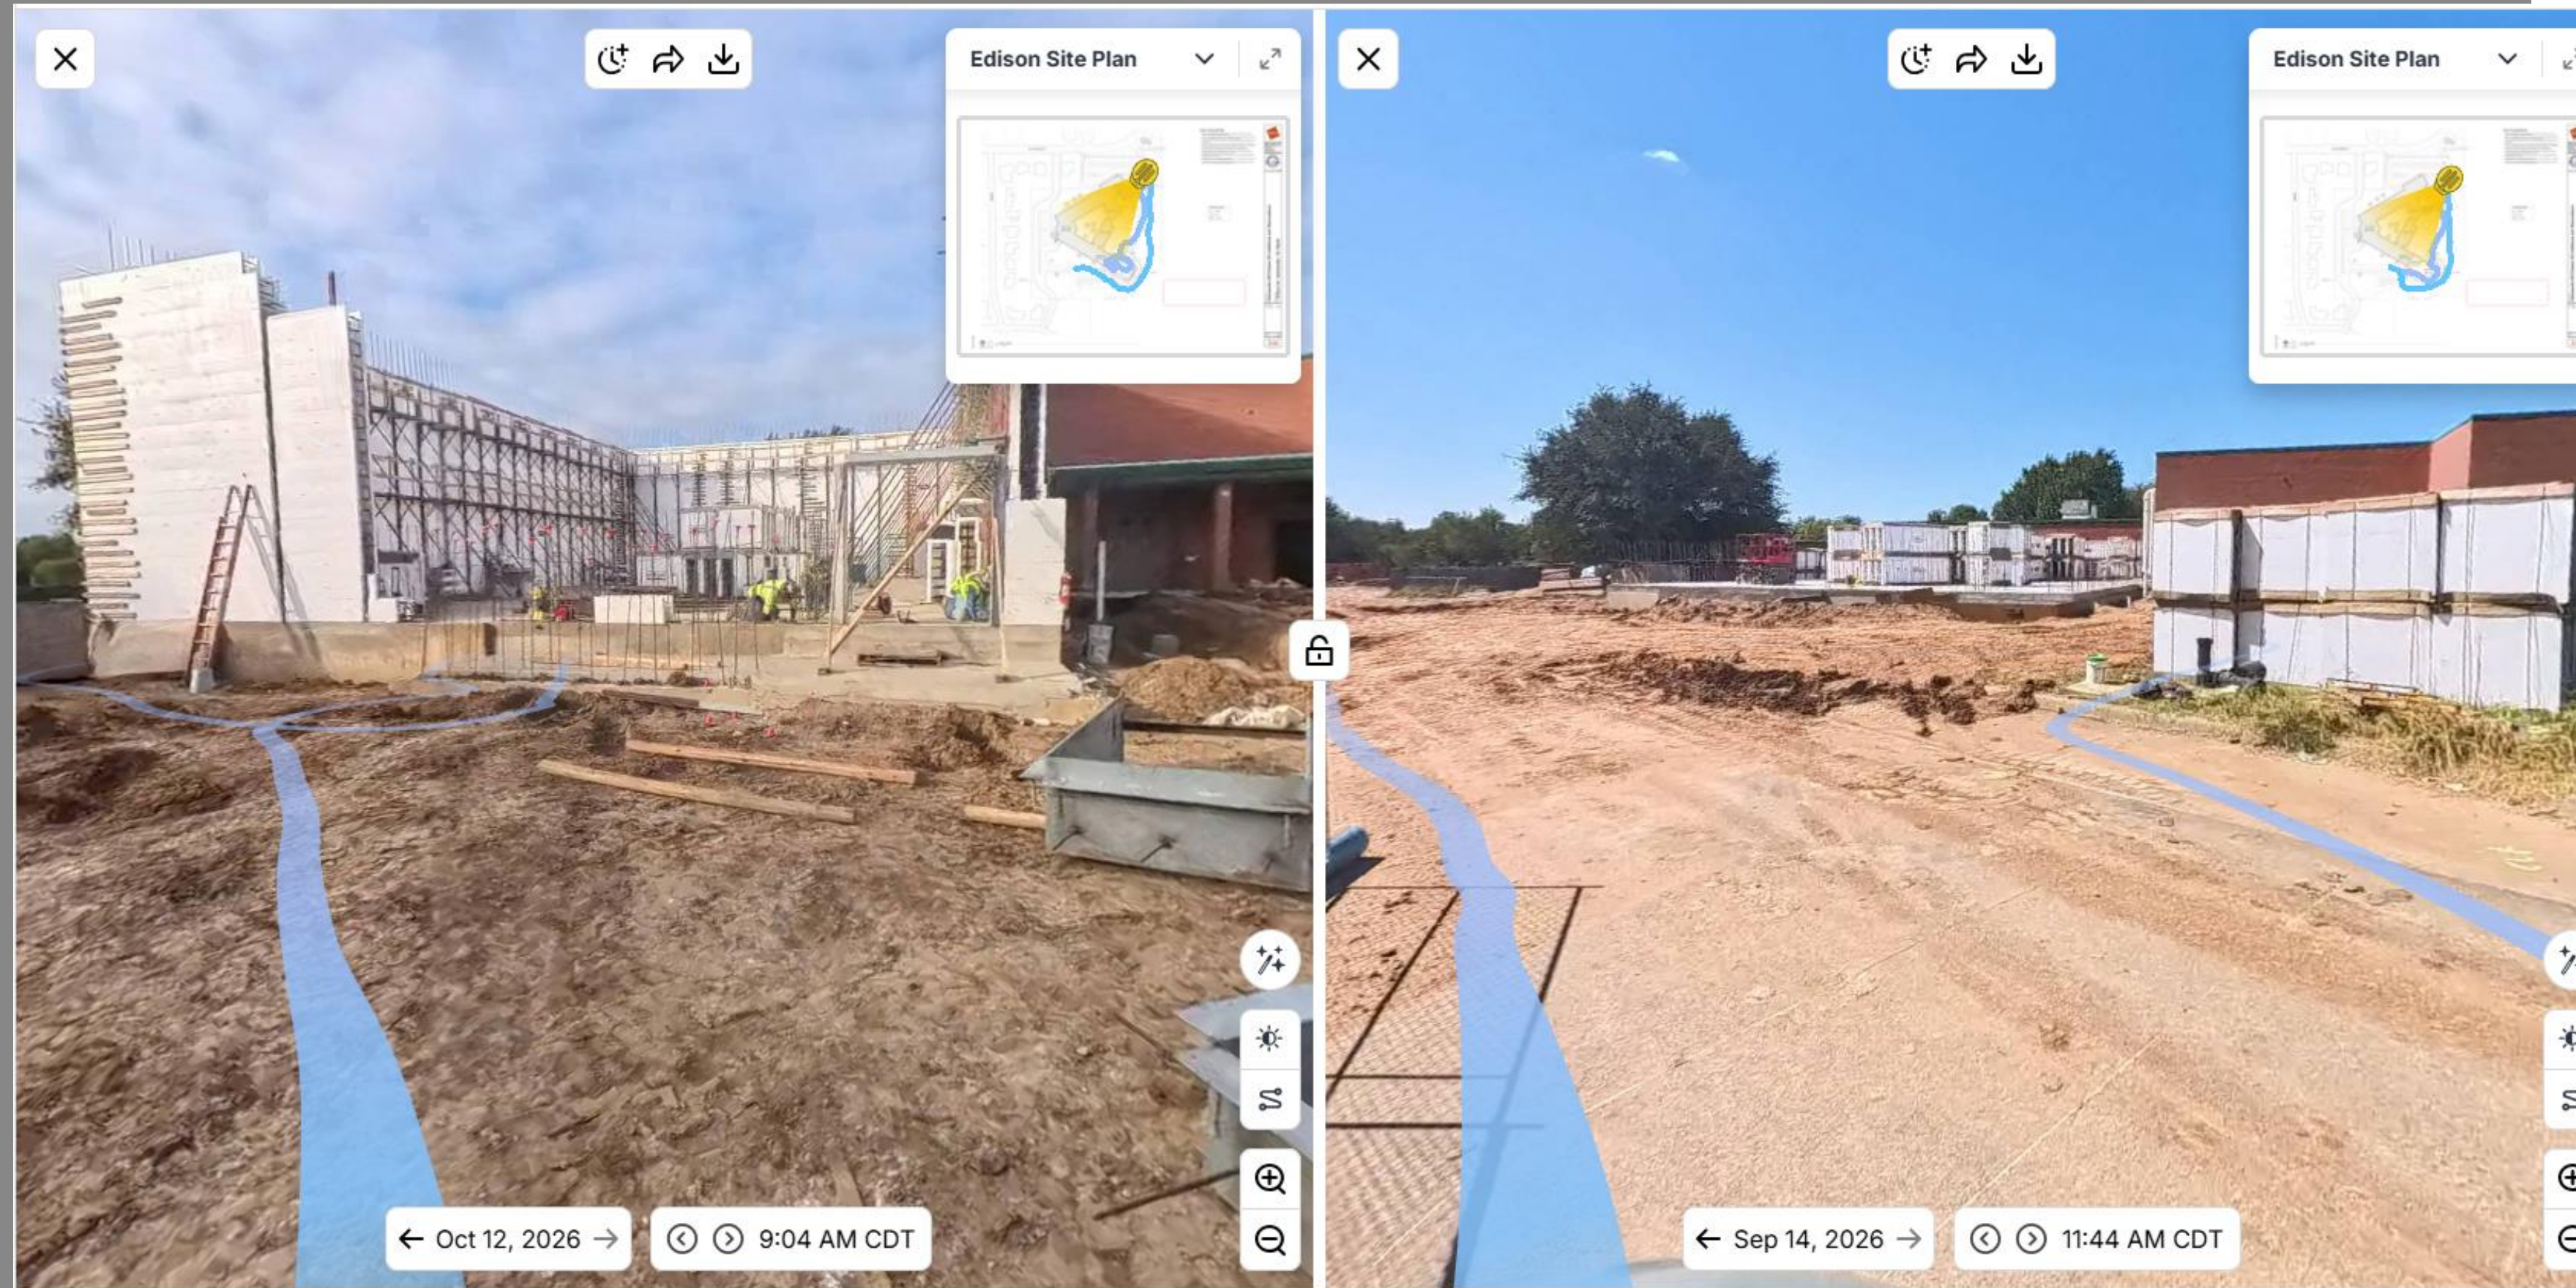

- Area C Storm Shelter Sept to Oct

EDISON ELEMENTARY



- Area C Gym





- Area F Classroom

CHALMERS ELEMENTARY



• ICF Pour

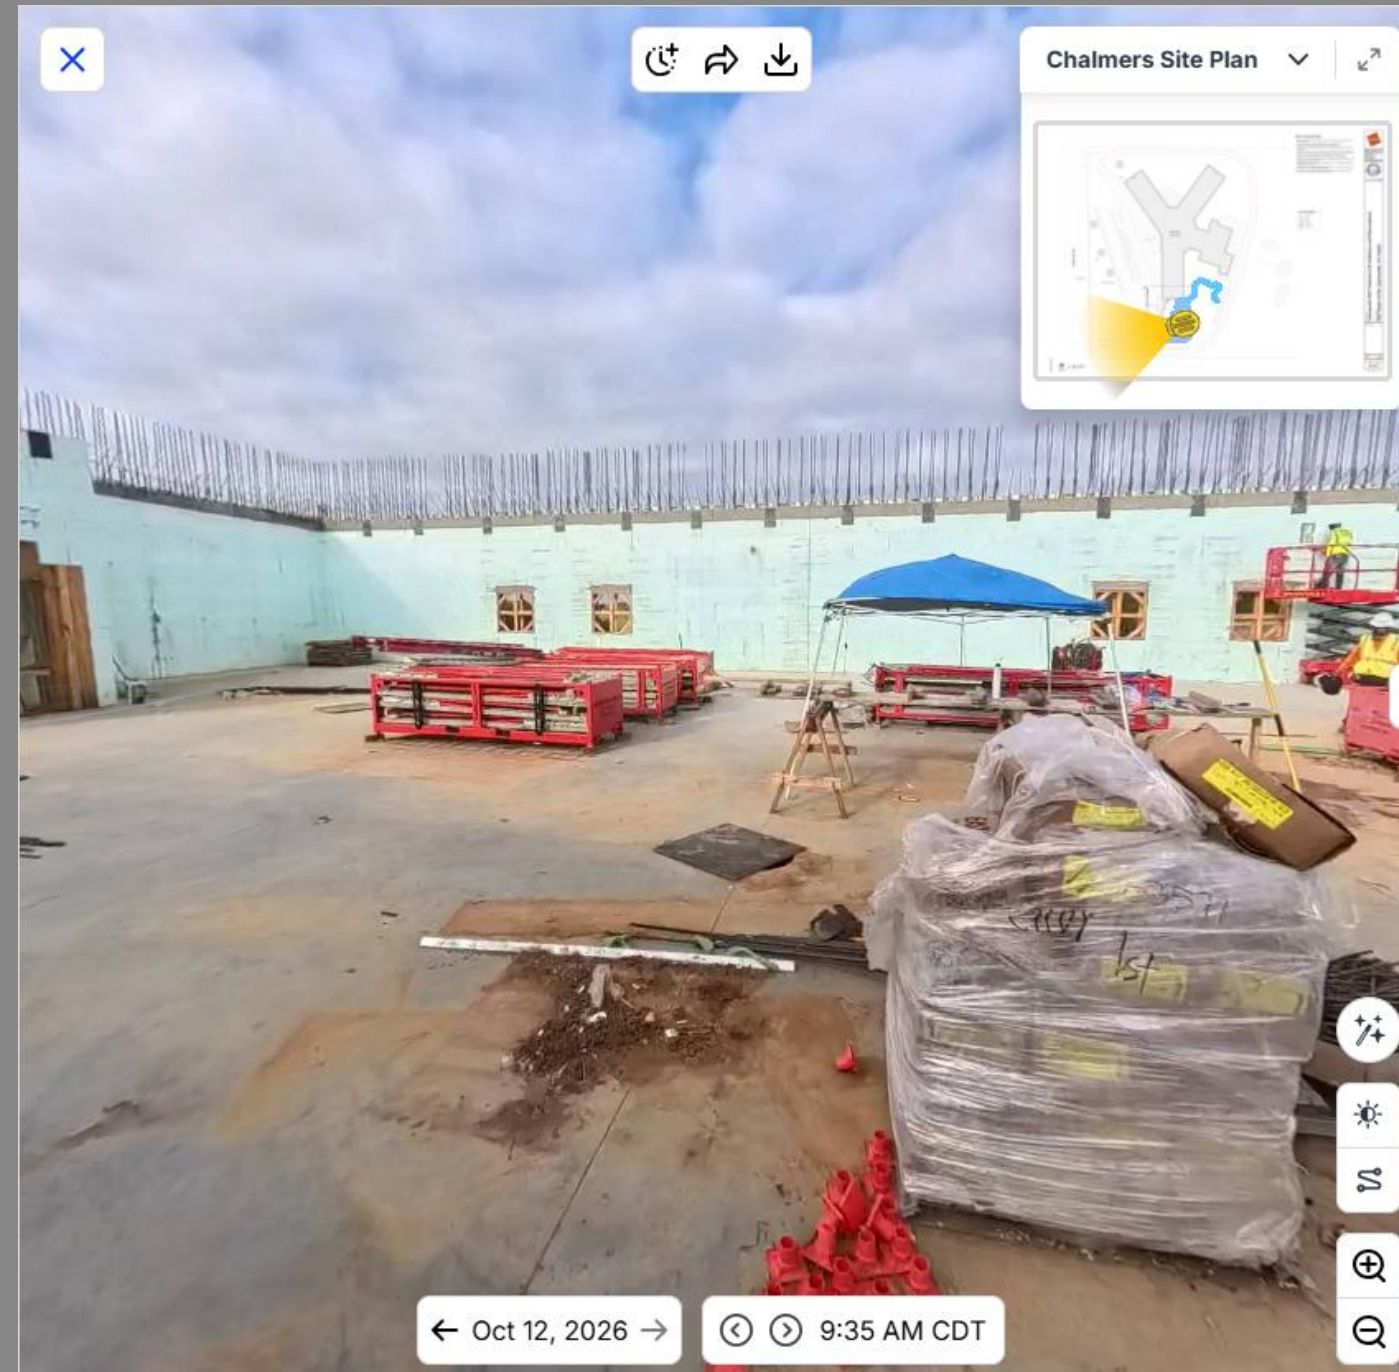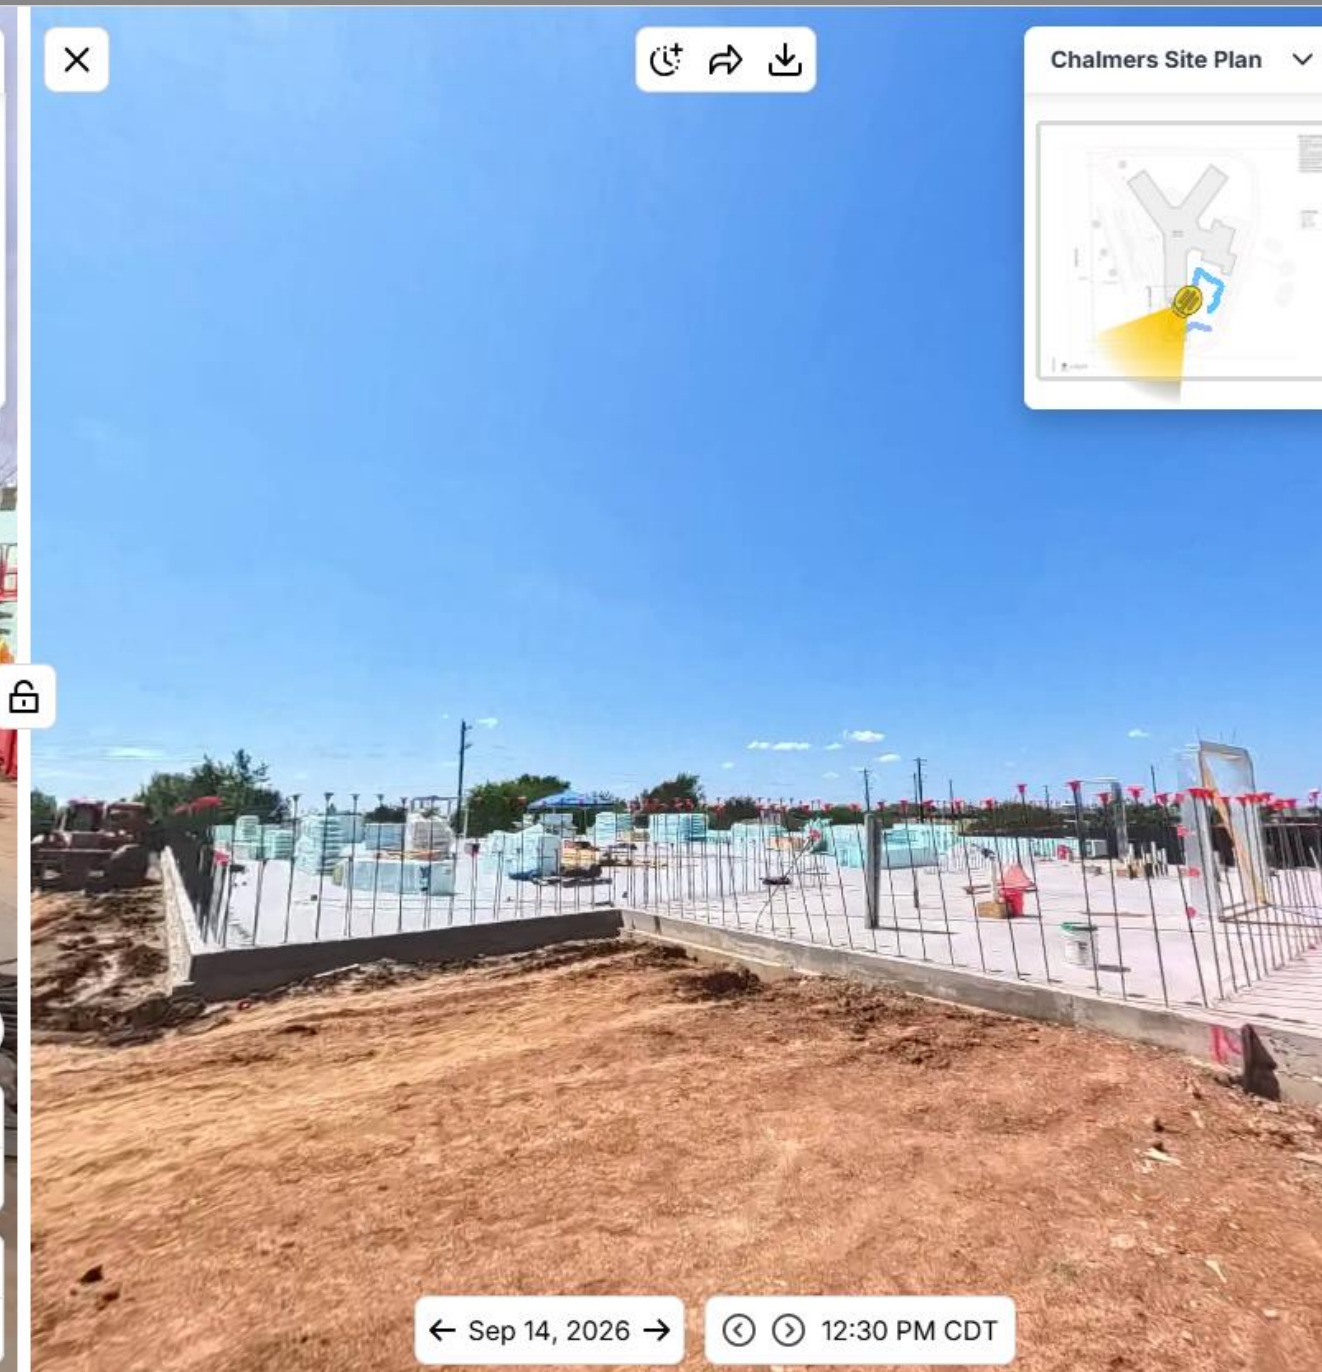


• Storm Shelter Addition Sept to Oct

CHALMERS ELEMENTARY



GAINESVILLE INTERMEDIATE

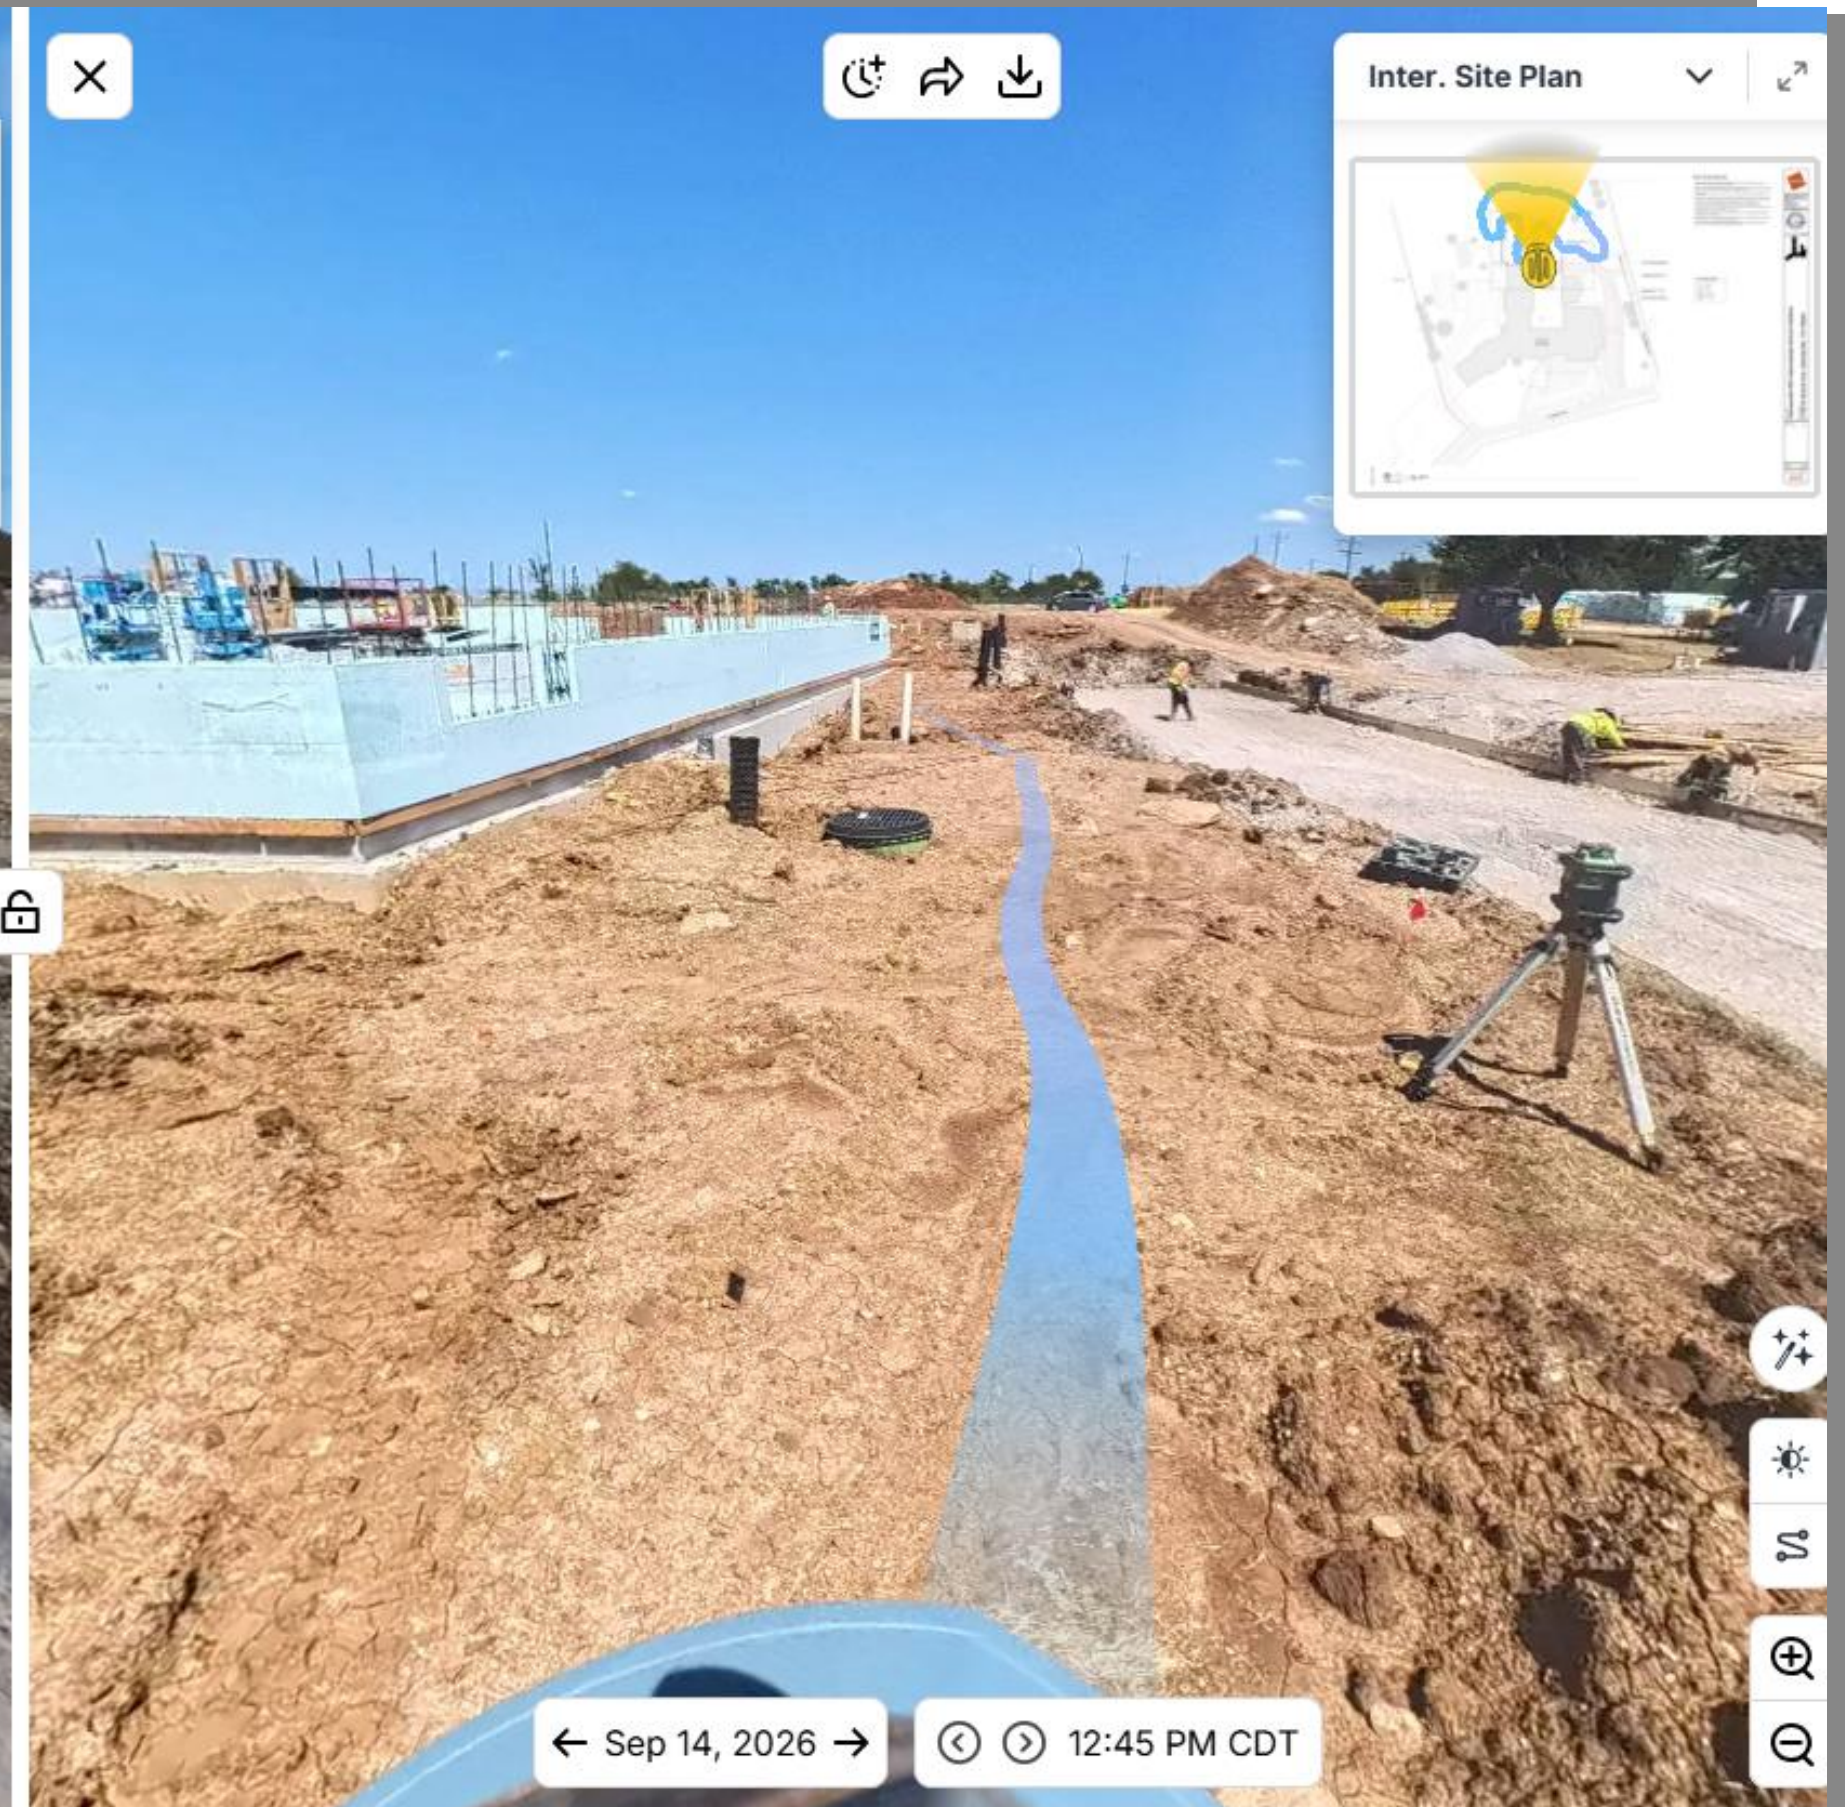


- Storm Shelter ICF Install & Paving Pour
Sept - Oct

GAINESVILLE INTERMEDIATE



SCHEDULE OVERVIEW

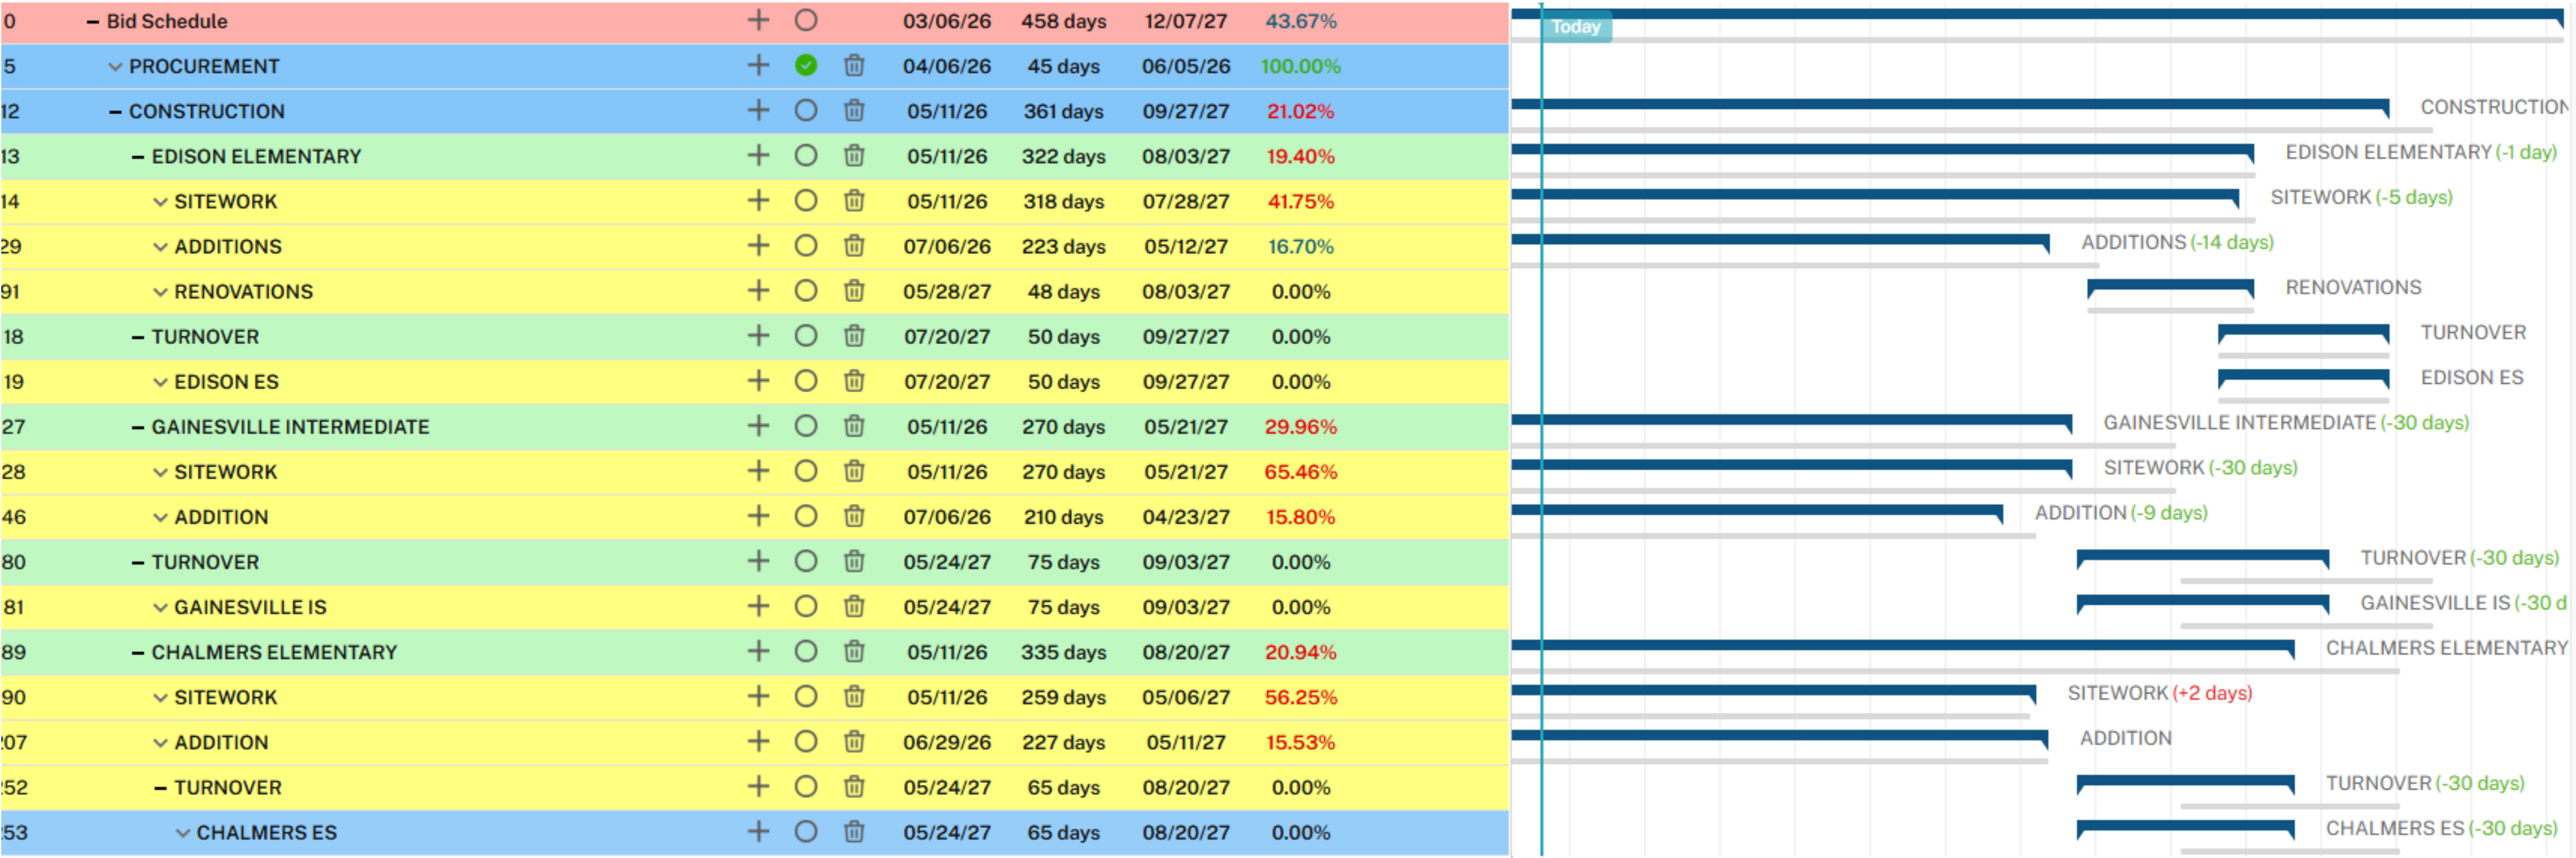



PROJECT STATUS Phase 2

High School & Junior High School



- **BILLINGS**


- Billed 0% thru September for Phase 2

- **CONTINGENCIES & ALLOWANCES**

- Total Balances Phase 2 = \$991,950



HIGH SCHOOL

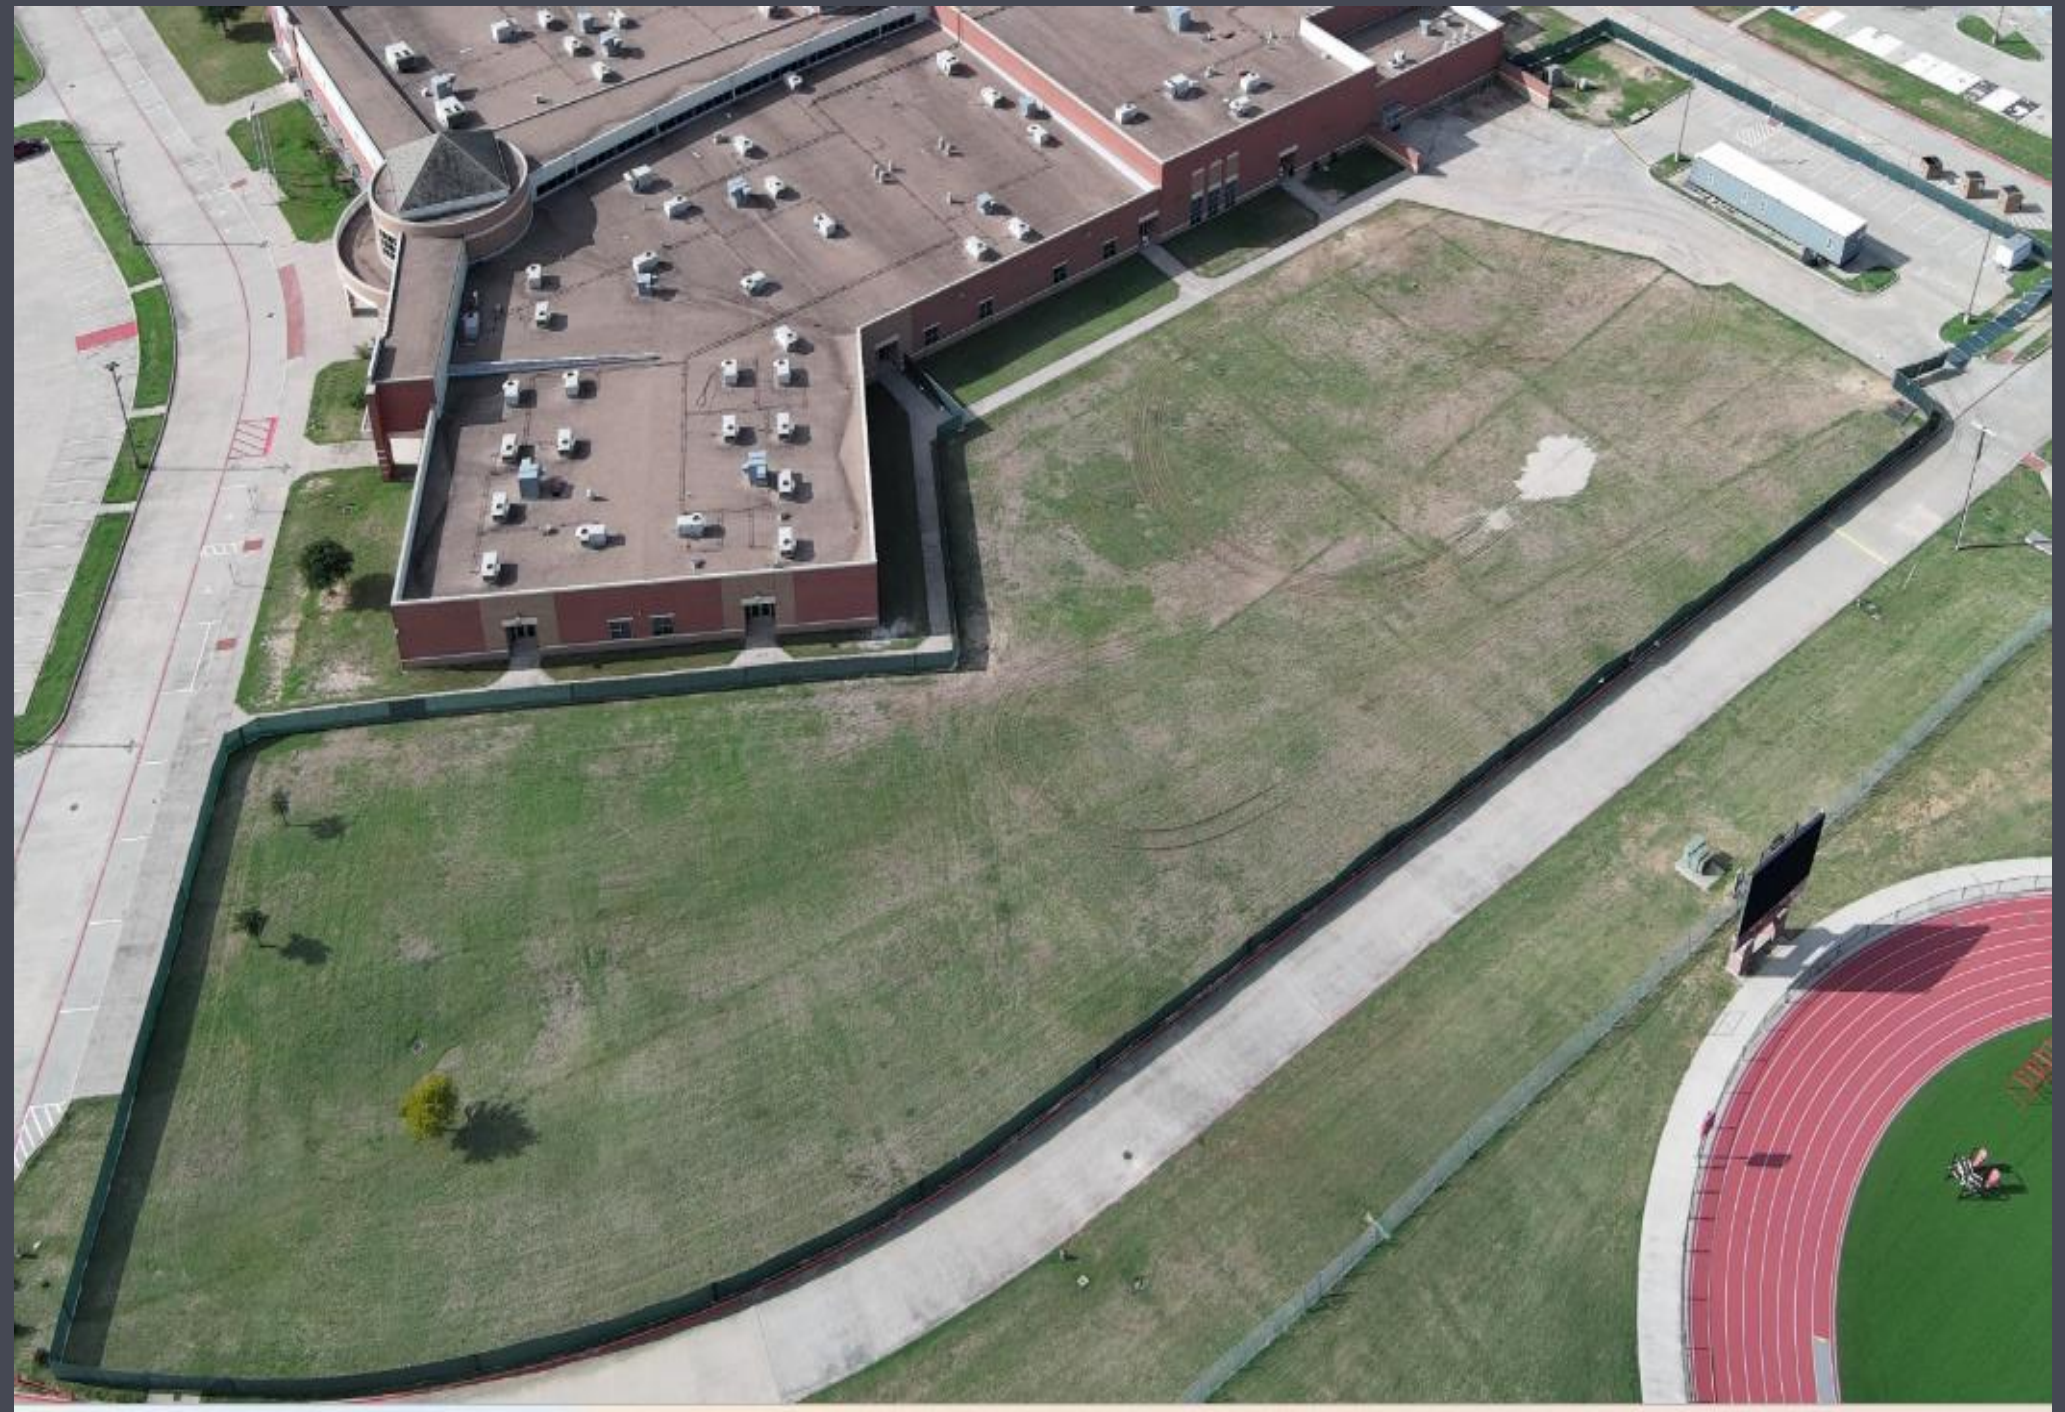

- Fence & Job Trailer Set

JUNIOR HIGH SCHOOL



- Fence & Job Trailer Set



SCHEDULE OVERVIEW

#	Activity	Actions	Start	Duration	End	Progress	Predecessors	Succ	2026				2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
									Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
0	– BID SCHEDULE	+ ○	07/23/26	468 days	01/19/28	1.71%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
