

2017 BOND PROJECTS – BOARD UPDATE

Spring Woods High School System Upgrades and Renovations

Spring Branch Independent School District
SBISD Project No. 67210
PBK Project No. 18147
November 30, 2020



1) PROJECT TEAM:

Owner:	Spring Branch ISD	Assoc. Superintendent for Ops:	Travis Stanford
		Project Manager:	Kris Drosche / Max Buja
Architect:	PBK	Partner-in-Charge:	Brandon Ross
		Project Manager:	Philip Stewart
CM @ Risk:	Satterfield & Pontikes Construction, Inc.		

2) GENERAL SCOPE OF WORK:

- Replacement of the HVAC system and renovations to the Cafeteria and Library. Also included are safety & security, structural repairs and site improvements for the campus.

3) BOND PLAN PROJECT TIMELINE:

- The following project is included in year one of the bond program. The Project Advisory Team is involved from the Schematic Design (SD) to the Design Development (DD) phase.

PROJECT ADVISORY TEAM	AUGUST 2018 – DECEMBER 2018
SCHEMATIC DESIGN	AUGUST 2018 – OCTOBER 2018
DESIGN DEVELOPMENT	OCTOBER 2018 – DECEMBER 2018
CM@R SELECTION	NOVEMBER 2018 – FEBRUARY 2019
CONSTRUCTION DOCUMENTS	NOVEMBER 2018 – FEBRUARY 2019
PERMIT RECEIVED	FEBRUARY 2019 – MAY 2019
BIDDING / BOARD APPROVAL	FEBRUARY 2019 – MAY 2019
CONSTRUCTION PHASE	MAY 2019 – AUGUST 2020
OCCUPANCY	MAY 2019 – AUGUST 2020
LIBRARY CONSTRUCTION PHASE	AUGUST 2020 – JANUARY 2021

Current Point

4) PROJECT STATUS OVERVIEW

- Library is under construction.
- Building Management and HVAC system has been installed.
- Building signage is being fabricated.
- Door hardware has been installed.

5) PAST 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

The following activities have taken place:

- Library drywall is being installed.
- Library storefront is being installed.
- Library stair structure has been completed.
- Skylights have been installed.

6) NEXT 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

- Punch list items are continuing to be worked through.
- Library construction will be completed.
- Furniture will be installed.
- Signage will be installed.

7) PHOTOGRAPHS:


Exterior view of the library storefront.



Library view from stairs.



Library interior storefront.

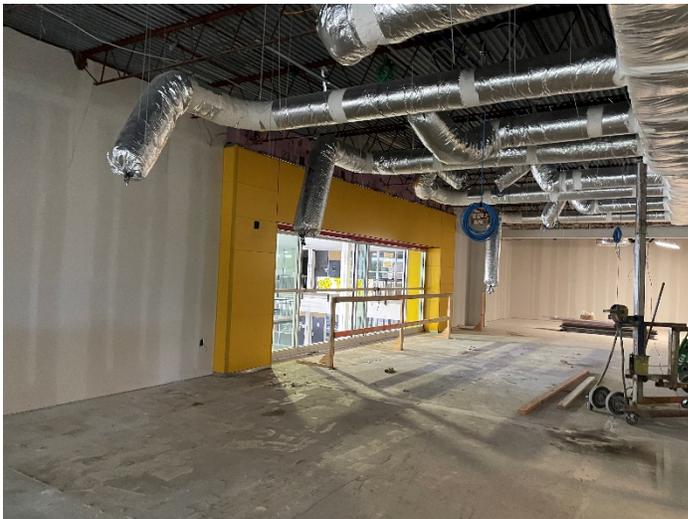

Exterior window from inside the room.
