

WHITE BEAR LAKE AREA SCHOOLS



SCHOOL BOARD UPDATE

School Board Meeting

March 28, 2022





SCHOOL BOARD UPDATE PRESENTATION AGENDA

5



- Oneka Design Update
- Construction Updates
- Questions / Discussion



Overview of Referendum Projects Scope





Referendum Projects Scope

NORTH STAR

ELEMENTARY







BIRCH LAKE FLEMENTARY

- · Add extended day office, conference room, one new classroom
- · Updated classrooms and media center, safety/security upgrades

LAKEAIRES ELEMENTARY

- · Add orchestra room and freezer
- · Updated classrooms and media center, safety/security upgrades

LINCOLN ELEMENTARY

- · Add full size gymnasium, conference room, extended day office and cooler
- · Updated classrooms and media center, safety/security upgrades

MATOSKA ELEMENTARY

- · Add freezer, specialist room, extended day office, EL room
- · Updated classrooms and media center, safety/security upgrades

ONEKA ELEMENTARY

- · Add 5 classrooms for capacity of 720 students
- · Updated classrooms and media center, safety/security upgrades

OTTER LAKE ELEMENTARY

- · Add 5 classrooms for capacity of 720 students
- · Updated classrooms and media center, safety/security upgrades

VADNAIS HEIGHTS ELEMENTARY

- · Add freezer, extended day office, orchestra room
- · Updated classrooms and media center, safety/security upgrades

WILLOW LANE ELEMENTARY

- · Add orchestra room and freezer
- · Updated classrooms and media center, safety/security upgrades

NORTH STAR ELEMENTARY

· New elementary school for 720 students (new site)

CENTRAL MIDDLE SCHOOL

- · Renovate District Office to create additional classroom space
- · Updated classrooms and media center, safety/security upgrades

SUNRISE PARK MIDDLE SCHOOL (FORMER SOUTH CAMPUS)

- · Addition/renovation to become a grades 6-8 MS, including additional gymnasium
- · Updated classrooms and media center, safety/security upgrades

WBLAHS NORTH CAMPUS

- · Addition / renovation to become single site grades 9-12 HS
- · Updated classrooms and media center, safety/security upgrades

AREA LEARNING CENTER

- Kitchen improvements and renovations to create secure vestibule
- · Updated classrooms and media center, safety/security upgrades

HUGO EARLY CHILDHOOD CENTER

· Convert for use as North Early Childhood Center

DISTRICT SERVICES CENTER (FORMER SUNRISE PARK)

· Renovation to convert for use as South Early Childhood Center, District Office, Senior Center, and Transition Education Center

TRANSPORTATION / MAINTENANCE FACILITY

· New transportation / maintenance facility (Location TBD)

- District-wide additions and renovations to accommodate projected enrollment growth
- Safety and security

improvements

- Deferred maintenance projects
- Classroom and building updates to create flexible learning spaces



Referendum Projects Completed:

- ALC Security Renovation
- Lincoln Elementary School
- Matoska Elementary School
- Vadnais Heights Elementary School
- Willow Lane Elementary School
- New Transportation / Maintenance Facility
- South Campus Phase I Addition (Gym)

Referendum Projects Bid / in

Construction:

- North Star Elementary School
- White Bear Lake Area High School
- South Campus Phase II Addition (Classrooms / Office)
- Phase I New Classroom Flexible Furniture

REFERENDUM PROJECTS UPDATE STATUS OF REFERENDUM PROJECTS

Referendum Projects Bid / in Construction (Cont.):

- Birch Lake Elementary School
- Lakeaires Elementary School
- Otter Lake Elementary School

Referendum Projects in Design:

- ALC Phase 2
- Oneka Elementary School
- Phase II New Classroom Furniture

Referendum Projects Remaining:

- Central Middle School
- Sunrise Park (future District Services Center / TEC / Early Childhood)
- Hugo Elementary (Future Early Childhood site)




REFERENDUM PROJECTS UPDATE STATUS OF REFERENDUM PROJECTS

100%
100%
100%
100%
100%
100%
68%
50%

South Campus Phase 2	35%
WBLAHS	22%
Birch Lake Elementary	21%
Lakeaires Elementary	13%
Otter Lake Elementary	4%
Central Middle School	0%
Sunrise Park	0%
*Based on percentage billed by contractors	

Design Process - Core Planning Group



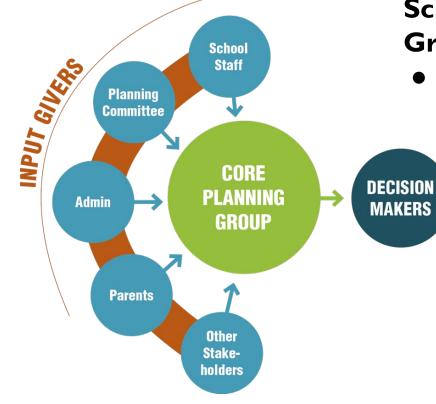


Schematic Design: Core Planning Groups

- Develop Core Planning Group for each individual building
 - Tours (Common Language)
 - Consensus on Criteria and Guiding Principles
 - Building a Common Diagram
 - Renderings / Visuals
 - Final Schematic Design

Design Process - User Groups

Design Development: User Group Process

- Involve Building Staff & Users in Details
- Every room impacted
- Builds ownership in the project
- No limit to number of meetings
- Detailed information for coordination

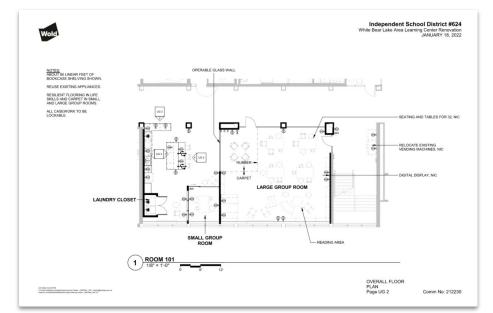







Design Update:

Oneka Elementary





Oneka Elementary School PROJECT SCOPE & SCHEDULE

Project Scope:

- Media Center Renovation
- (5) additional capacity classrooms (storm shelter)
- Additional parking stalls
- New Media Center Furniture and Classroom Furniture
- \$7.6 Million total project cost

Schedule:

- Schematic Design (Core Planning Group): October November 2021
- Design Development (User Groups): December 2021 January 2022
- Construction Documents: February 2022 April 2022
- Bidding / Construction starts: May 12, 2022
- Opens Winter 2023-2024



Oneka Elementary School FLOOR PLAN


































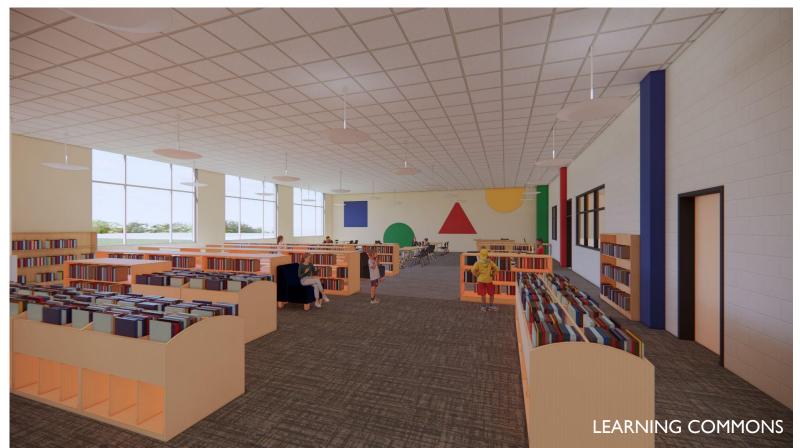



What's Under Construction?





NORTH STAR ELEMENTARY SCHOOL PROJECT SCOPE & SCHEDULE

Project Scope:

- New elementary to create a comprehensive K-5 school in Hugo, MN
- New furniture
- 101,000 square foot building
- Approximately \$43 million total project cost including building and on and off site improvements

Schedule:

- Schematic Design (Core Planning Group): January 2020 - May 2020
- Design (User Groups): May 2020 September 2020
- Construction Documents: September 2020 -November 2020
- Bid Opening: December 2020
- Bidding / Construction Starts: Spring 2021
- Open Fall 2022







NORTH STAR ELEMENTARY SCHOOL CONSTRUCTION STATUS





NORTH STAR ELEMENTARY SCHOOL CONSTRUCTION STATUS



NORTH STAR ELEMENTARY SCHOOL CONSTRUCTION STATUS





Wold K Area Sch

SOUTH CAMPUS OFFICE & CLASSROOMS ADDITION PROJECT SCOPE & SCHEDULE

Project Scope:

- Additions and renovations to create a grades 6-8 middle school, including classroom addition
- Addition of main office to create secure entry
- Renovation of media center
- New classrooms and media center furniture (future project)

Schedule:

- Schematic Design (Core Planning Group): October 2020 - December 2020
- Design Development (User Groups): January 2021 -March 2021
- Bidding / Construction Starts: late Spring 2021
- Opens in August 2022





Wold W White Bear Lake Area Schools SOUTH CAMPUS OFFICE & CLASSROOMS ADDITION CONSTRUCTION STATUS



Wold Wite Bear Lake SOUTH CAMPUS OFFICE & CLASSROOMS ADDITION CONSTRUCTION STATUS





HIGH SCHOOL PROJECT SCOPE & SCHEDULE

Project Scope:

- Additions and renovations to create a comprehensive 9-12 high school
- New furniture
- Upgrades and expansion to kitchen and cafeteria
- 375,000 square foot addition
- Approximately \$179M total project cost including building, and on and off site improvements plus \$25M LTFM

Schedule:

- Schematic Design (Core Planning Group): late January 2020 - May 2020
- Design Development (User Groups): June 2020 -February 2021
- Bidding / Construction Starts: Spring 2021
- Opens in phases over the next 4 years





HIGH SCHOOL CONSTRUCTION STATUS







HIGH SCHOOL CONSTRUCTION STATUS





HIGH SCHOOL CONSTRUCTION STATUS





REFERENDUM PROJECTS UPDATE NEXT STEPS

Next Steps:

- Birch Lake, Otter Lake, Lakeaires construction is underway
- Phase I Elementary Projects, South Campus Gym, and Transportation Facility substantially completed
- North Star Elementary will be completed for Fall 2022
- South Campus will be completed Fall 2022 (all phases)
- The unified High School:
 - Stadium will be completed for Fall 2022
 - Phase I construction (classroom towers and fieldhouse) will be completed January 2023



WHITE BEAR LAKE AREA SCHOOLS



SCHOOL BOARD UPDATE

THANKYOU!

