

MONTHLY REFFERENDUM REPORT DETAILED - as of June 30, 2022




Battery Creek High School 1 Blue Dolphin Dr, Beaufort 29906

Cluster: Battery Creek Principal: Denise Lessard

Original Appropriations:	\$56,075,773	Encumbered and Paid:	\$54,211,263
Transfers/Adjustments:	\$0	Paid to Date:	\$28,864,564
Revised Budget:	\$56,075,773	Available Budget:	\$1,864,510

2019 Bond Referendum Renovation

Project ID: 51925392-1

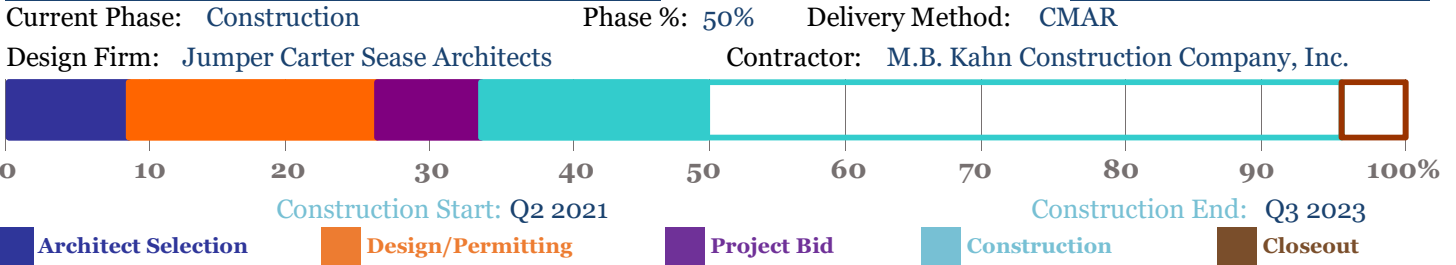

Scope: 2019 Bond Referendum

- Athletics
- CATE expansion
- Design Consultants
- FF&E
- Pre-Construction/Site Prep
- Renovations
- Renovations Construction
- Safety/Security
- Technology /Infrastructure
- Various Vendors

Project Details: Scope to include renovation work of the classroom areas, athletic improvements to the track/turf field and concession, safety/security upgrades of bullet resistant glass and security system, and renovations of existing spaces for CATE program expansion.

Monthly Progress: Construction in progress. D Hall is occupied. H Hall kitchen renovation is complete. Locker room renovations are pending flooring and fixtures. Weight room addition is nearing completion. Concession stand panels on order, and electrical in progress. Turf field and irrigation is complete. Track surface in progress. Press box, batting cages are complete. Underground utilities nearing completion. Construction has started in A and B halls. Overhead on first floor nearing completion. Started on second floor. Casework has been delivered. Loop piping is complete. Fieldhouse in progress. F hall to commence in Fall. G1 in progress. Auditorium, gym and media center improvements to take place in 2023.
