



ISD #883
Rockford Area Schools
LTFM & Abatement Bond Projects

ICS Weekly Progress Report
Friday Aug 12, 2022

Address: 6051 Ash Street, Rockford, MN 55373

Week Ending August 12, 2022

- Metro Paving patched and repaired cracks throughout parking lots
- Metro Paving began first round of seal coat and "chip" rock installation in HS
- New Look Contracting installed new drain tile, and poured curbs for relocated playground equipment

Weeks Ending August 19th and August 26th, 2022

- Metro Paving to sweep, and fog coat the HS parking lots beginning Aug 16th
- Safety First to begin reinstalling Elementary School Playground August 24th
- New Look Contracting to begin Mobilizing to Middle School and prepare for Excavations
- LTFM/Bond update meeting to discuss ongoing and future LTFM projects


Important Upcoming Dates

- August 16-18th the HS parking lot will be closed for sweeping and final fog sealant layer
- August 22nd – New Look Contracting to mobilize to Middle School site to begin erosion control and removals
- September 1st – New Look Contracting to mobilize to Elementary/High School to begin erosion control and removal

Construction Progress Photos



1st layer of seal coat being applied in the HS parking lot

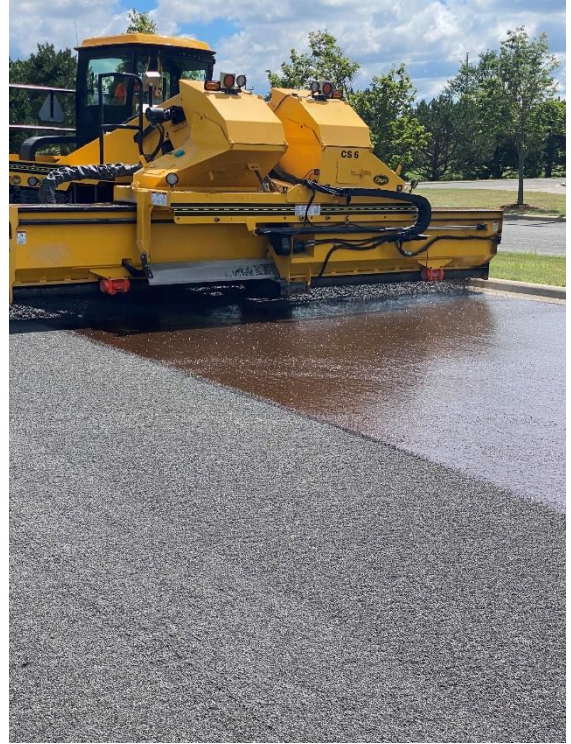

"chip" rocks being applied on top of seal coat to finish 1st layer of new surfacing



Forms Installed to set new concrete curb surrounding relocated playground



Forms pulled to reveal new curbing
