

MONTHLY REFFERENDUM REPORT DETAILED - as of July 31, 2022




Battery Creek High School 1 Blue Dolphin Dr, Beaufort 29906

Cluster: Battery Creek Principal: Denise Lessard

Original Appropriations:	\$56,075,773	Encumbered and Paid:	\$54,229,519
Transfers/Adjustments:	\$0	Paid to Date:	\$32,333,041
Revised Budget:	\$56,075,773	Available Budget:	\$1,846,254

2019 Bond Referendum Renovation

Project ID: 51925392-1

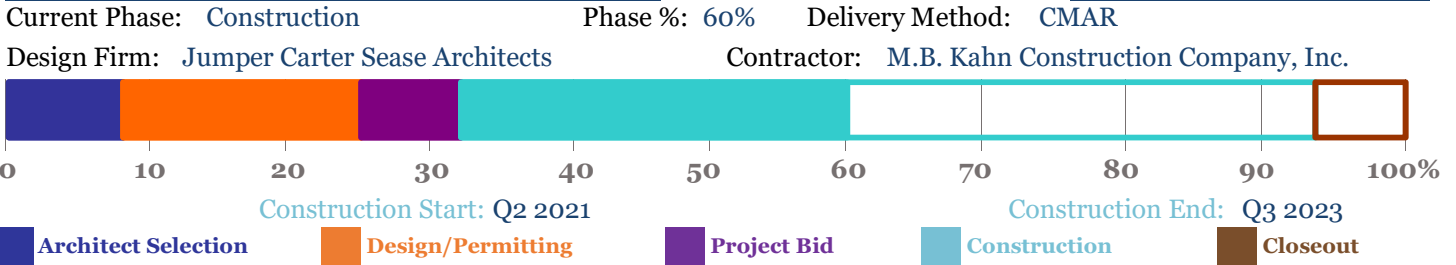

Scope: 2019 Bond Referendum

- Athletics
- CATE expansion
- Design Consultants
- FF&E
- Pre-Construction/Site Prep
- Renovations
- Renovations Construction
- Safety/Security
- Technology /Infrastructure
- Various Vendors

Project Details: Scope to include renovation work of the classroom areas, athletic improvements to the track/turf field and concession, safety/security upgrades of bullet resistant glass and security system, and renovations of existing spaces for CATE program expansion.

Monthly Progress: Construction in progress. D Hall is occupied. H Hall kitchen renovation is complete. Locker room renovations are pending flooring and fixtures. Weight room addition is nearing completion. Concession stand and fieldhouse construction pending wall board delivery. Turf field and irrigation is complete. Track surface in progress. Press box, batting cages are complete. Underground utilities nearing completion. A hall and B hall first floor construction is Loop piping is complete. Fieldhouse in progress. F hall to commence in Fall. G1 in progress. Auditorium, gym and media center improvements to take place in 2023.
