

# MONTHLY REFFERENDUM REPORT DETAILED - as of October 31, 2022




## Battery Creek High School 1 Blue Dolphin Dr, Beaufort 29906

Cluster: Battery Creek      Principal: Denise Lessard

Original Appropriations:	\$56,075,773	Encumbered and Paid:	\$55,017,663
Transfers/Adjustments:	\$0	Paid to Date:	\$38,019,524
Revised Budget:	\$56,075,773	Available Budget:	\$1,058,110

### 2019 Bond Referendum Renovation

Project ID: 51925392-1

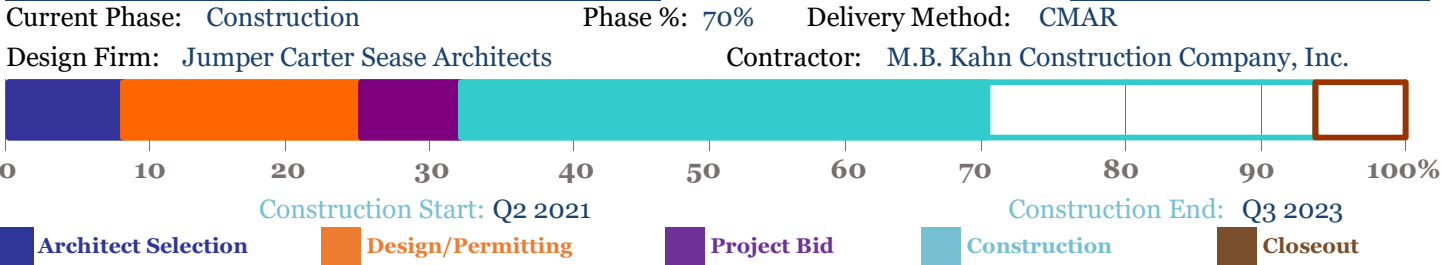

**Scope: 2019 Bond Referendum**

- Athletics
- CATE expansion
- Design Consultants
- FF&E
- Pre-Construction/Site Prep
- Renovations
- Renovations Construction
- Safety/Security
- Technology /Infrastructure
- Various Vendors

**Project Details:** Scope to include renovation work of the classroom areas, athletic improvements to the track/turf field and concession, safety/security upgrades of bullet resistant glass and security system, and renovations of existing spaces for CATE program expansion.

**Monthly Progress:** Construction in progress. A Hall, B1, and D Hall are occupied. B2 and C2 ceiling work is in progress. Classroom lighting and HVAC nearing completion. E electrical rough-in in progress. Generator has been delivered. F demolition has started. G aux gym underground demo and cmu demo is complete. Underground installation is complete. H Hall kitchen renovation is complete. Locker room renovations are pending flooring and fixtures. Weight room addition is complete, less roll-up door installation. Concession stand and fieldhouse construction pending wall board installation. Turf field and irrigation is complete. Track surface in progress. Press box, batting cages are complete. Underground utilities nearing completion. Final punch on athletics and A and B halls are in progress.
