


MONTHLY REFFERENDUM REPORT DETAILED - as of October 31, 2022



Mossy Oaks Elementary School 2510 Mossy Oaks Rd, Beaufort 29902

Cluster: Beaufort Principal: Melissa Vogt


Original Appropriations:	\$1,598,782	Encumbered and Paid:	\$3,895,515
Transfers/Adjustments:	\$2,299,382	Paid to Date:	\$121,697
Revised Budget:	\$3,898,164	Available Budget:	\$2,649

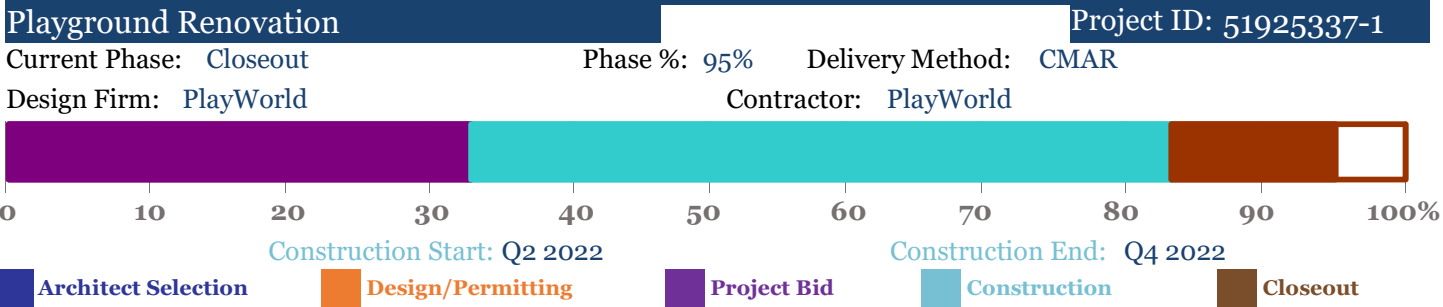

Scope: 2019 Bond Referendum
Design Services (MOES)
Design Services printing (MOES)
Playgrounds

Project Details: Scope of work includes new playground equipment and surface areas.


Monthly Progress: Installation complete. Pending final punch list item resolution.

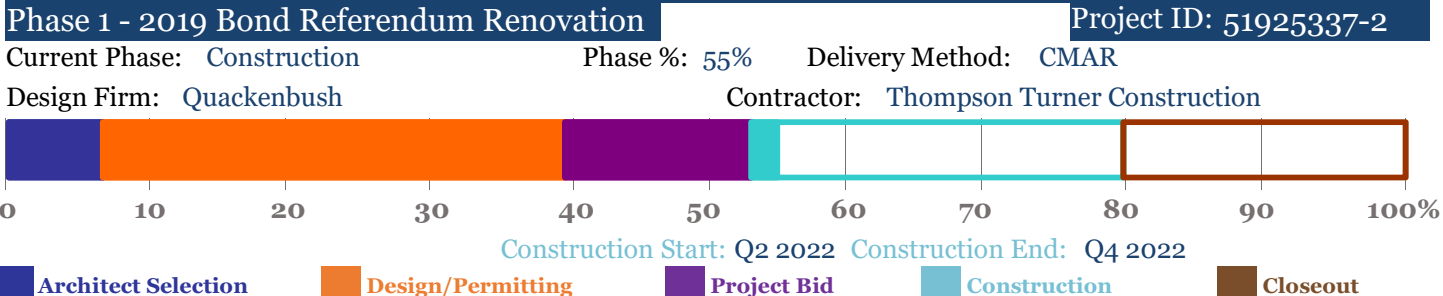

Scope: 2019 Bond Referendum
Safety/Security
Technology /Infrastructure

Project Details: Scope of work includes Safety/Security, and Technology/Infrastructure improvements.

Monthly Progress: Construction in progress. Bullet-resistant entryway is complete. Cabling ordered.

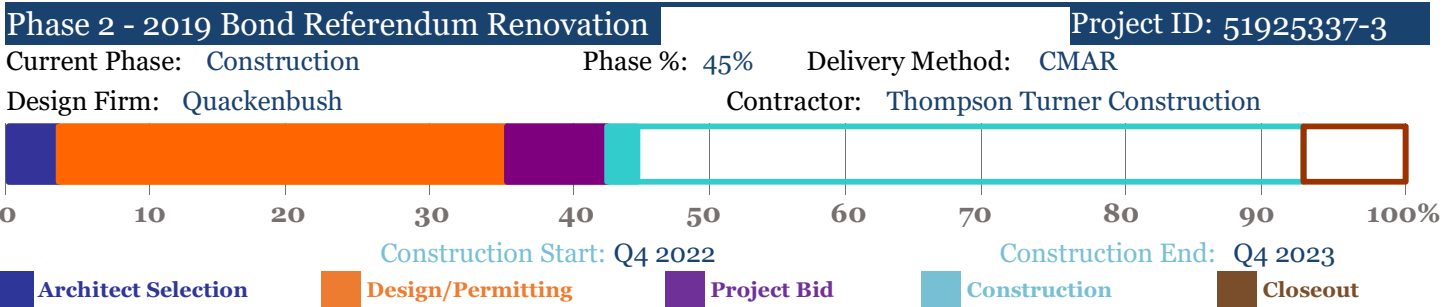

Scope: 2019 Bond Referendum
Safety/Security
Technology /Infrastructure

Project Details: Scope of work includes Safety/Security, and Technology/Infrastructure improvements.

Monthly Progress: Construction in progress. Mobilization has begun.
