


Birmingham Public Schools | September 2022 Dashboard Report



\$195 Bond Budget Breakdown




Cost to Complete Through 9.14.2022

FUNDING ALLOCATION:	Budget	Commitments/ Projected Commitments	Actuals Approved	Actual Cost To Complete	Forecasted Commitments	Reserve/Owner Contingency	Estimate At Completion	Forecasted Over/(Under)
Construction/District-Wide	\$147,074,365	\$95,641,932	\$38,771,663	\$56,870,269	\$48,593,309	\$2,839,124	\$147,074,365	\$0
FF&E	\$7,572,140	\$1,082,855	\$476,101	\$606,753	\$6,489,285	\$0	\$7,572,140	\$0
Buses	\$8,473,500	\$1,344,014	\$1,344,014	\$0	\$7,129,486	\$0	\$8,473,500	\$0
Technology/Security	\$24,643,848	\$8,289,862	\$4,240,160	\$4,049,703	\$16,353,986	\$0	\$24,643,848	\$0
Design Prime	\$7,516,147	\$1,322,922	\$1,256,550	\$66,372	\$6,193,225	\$0	\$7,516,147	\$0
OVERALL TOTALS:	\$195,280,000	\$107,681,586	\$46,088,488	\$61,593,098	\$84,759,291	\$2,839,124	\$195,280,000	\$0


Overall budget includes \$280,000 from the 2018 Bond proceeds previously approved to help fund BP 2-6. All Owner costs included represent cost through July 31, 2022. Final numbers pending owner accrual and final audited reports for year end.

Committed Cost by Category Through 9.14.2022




Construction/District-Wide










Upcoming Projects Currently in Design & Planning

- •Seaholm High School
 - »Baseball / Softball / Practice Field (April 2023 December 2023 Construction)
- Derby Middle School
 - »Renovations (May 2023 September 2023 Construction) »Outbuilding (Spring 2023 - Fall 2023 Construction)
- West Maple Elementary School
 - »Selective Playground Equipment Replacement (October 2022 Construction) »Renovations (June 2023 - August 2023 Construction)
- Pembroke Elementary School
 - »Selective Playground Equipment Replacement Phase 2 (Summer 2023)

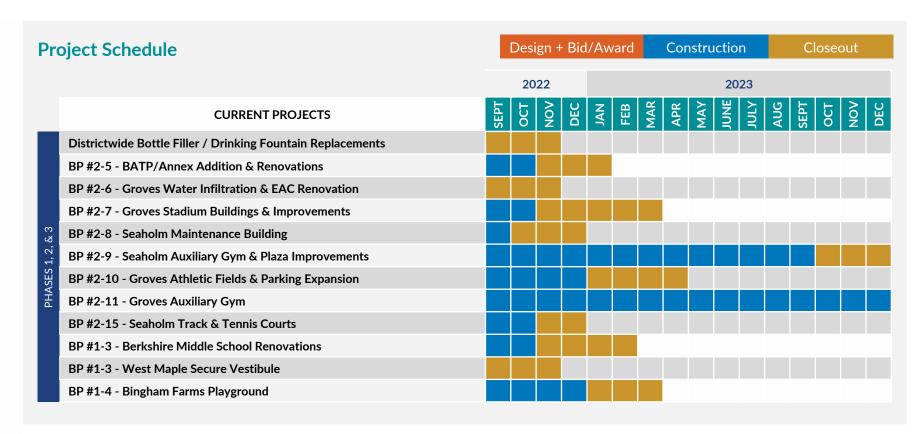



Birmingham Public Schools | September 2022 Dashboard Report

Completed Projects

2020 Projects

- SHS/GHS Stadium Sound Systems
- SHS/GHS Gym Video Scoreboards & Sound System
- SHS Stadium Lighting

2021 Projects

- Pierce Phase 1 Renovations + New Cafeteria Addition
- BCS Generator Replacement
- GHS Bleachers, Press Box & New Maintenance Building
- SHS Press Box & Selective Interior Renovations
- Transportation New Storage Building
- Midvale Parking Lot Expansion & New Generator

2022 Projects

- Roofing Berkshire, Beverly & Greenfield
- Pierce Phase 2 Renovations
- Berkshire Renovations
- West Maple Secure Vestibule & Front Entrance
- BATP Addition & Renovation
- EAC / Groves Water Infiltration & Improvements
- SHS Tennis Courts / Track / Maintenance Building
- GHS New Tennis Courts
- Districtwide Drinking Fountains & Bottle Fillers

Project Photos



BATP - New Addition



BATP - Community Room



Seaholm - Counseling Graphic



Berkshire - Kitchen Remodel



Berkshire - Cafeteria Remodel



West Maple - Entrance & Vestibule



Groves - New Concession Building



Groves - New Practice Field



Groves - Varsity Softball Field



Seaholm - New Maintenance Bldg.



Seaholm - New Tennis Courts



Seaholm - New Auxiliary Gym
