



21st Century Classroom Improvements

August 25, 2022 Board Update




CUMMING
Building Value Through Expertise

Newton Middle School Interim Housing

KPI Overview

NWMS IH

| Budget | Committed | Balance |
|----------|----------------|----------------|
| \$ 1.20M | \$ 0.83M 69.1% | \$ 0.37M 30.9% |

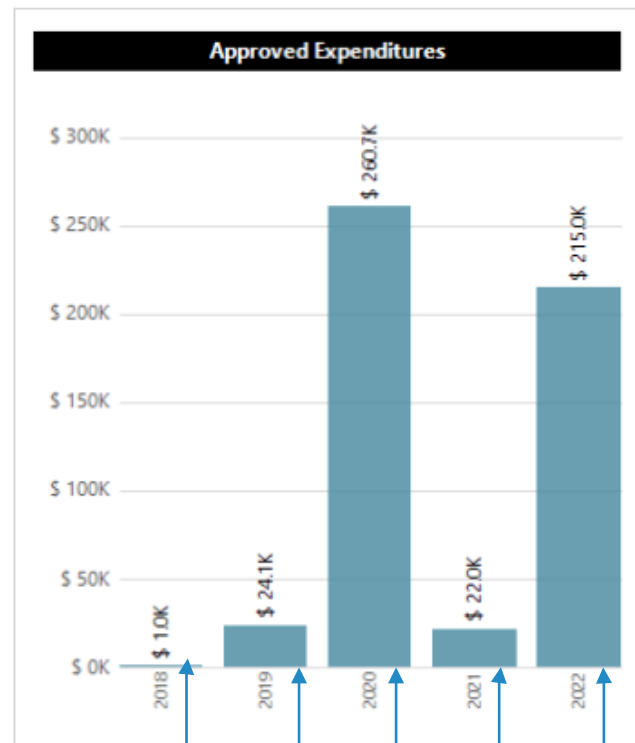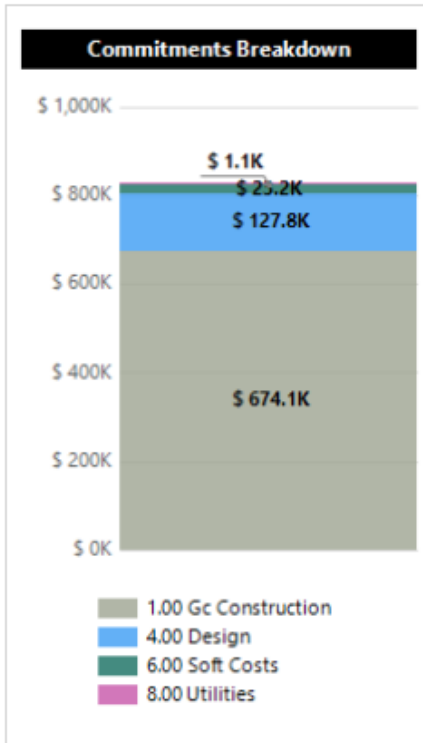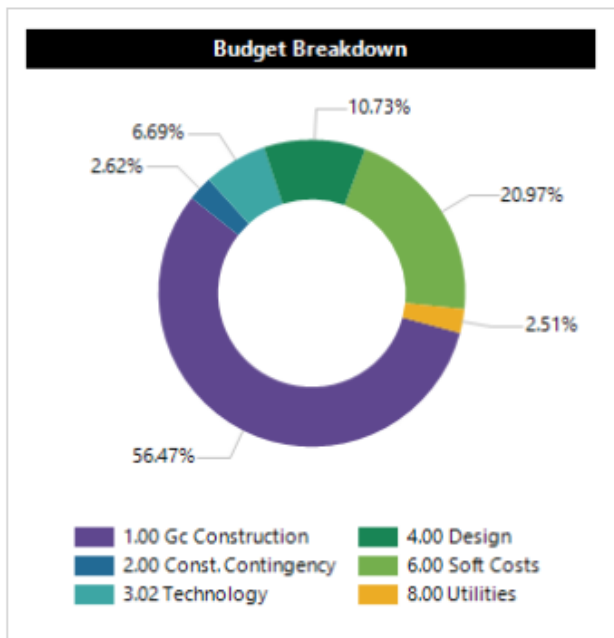

Design Payments 2018

Design Payments 2019

Design, DSA, Power, Portable Purchase

Design, Bidding and Administration

Bid & Build

Project Status

Close out




BID BUNDLE #3 PHASE 1 & 2

**BID BUNDLE #3:
SPARKS MS, NEWTON MS
&
GRANDVIEW COLLEGE PREP
21ST CENTURY CLASSROOM MODERNIZATION
Bid No. 2022-23.01**

CONSTRUCTION DURATIONS

| | |
|-------------------------|----------|
| GRANDVIEW COLLEGE PREP. | 285 DAYS |
| SPARKS MIDDLE SCHOOL | 180 DAYS |
| NEWTON MIDDLE SCHOOL | 410 DAYS |



Grandview Academy, Newton, Sparks MS


Budget Optimization

- Enrollment Analysis and Alignment with Site Capacity
- Cluster Classroom Renovations to Reduce Required DSA Access Improvements
- Value Engineer Sound System Components
- Right Sized Data Infrastructure

CURRENTLY BIDDING

Project Status

Bidding



QUESTIONS + ANSWERS

CUMMING
Building Value Through Expertise
