




21st Century Classroom Improvements


March 24, 2022 Board Update

CUMMING
Building Value Through Expertise

Newton Middle School

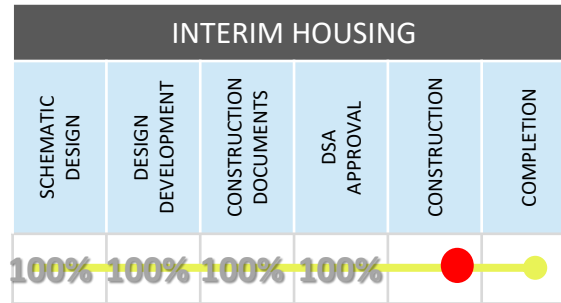

75%

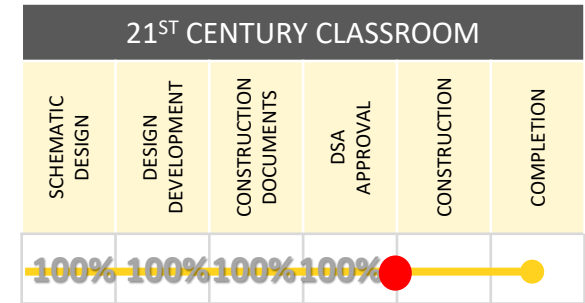

NOTES

- Interim Housing Construction Nearing Completion
- Current Tasks
 - Electrical Near Complete
 - Low Voltage
 - Fire Alarm
 - Seal Coat
 - Plumbing





Project Status

INTERIM HOUSING
SYSTEMS INSTALLATION




PROGRESS TRACKING

Newton Middle School Interim Housing Budget

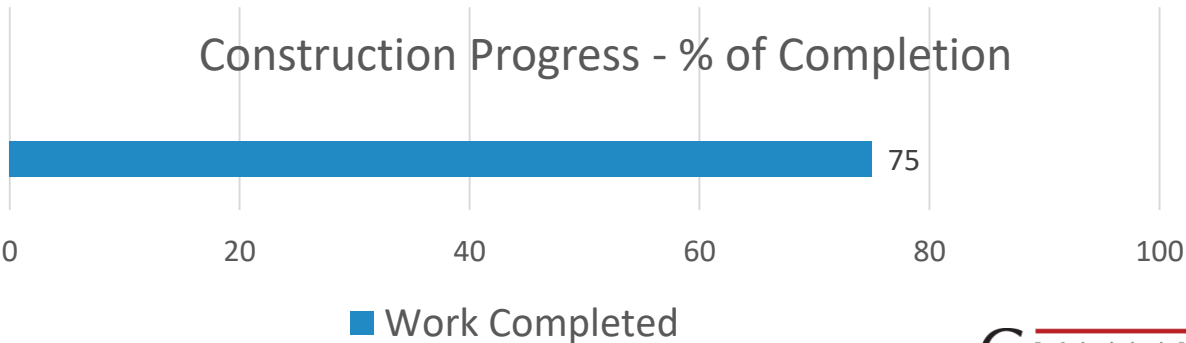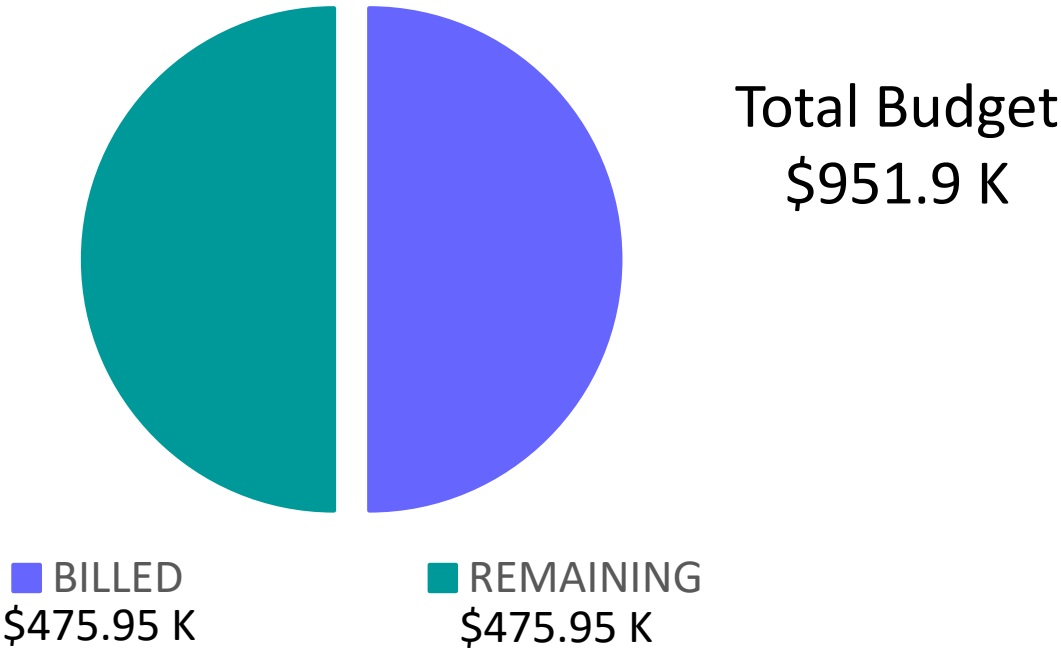

Project Status
Budget and Schedule

Newton Middle School Interim Housing Schedule

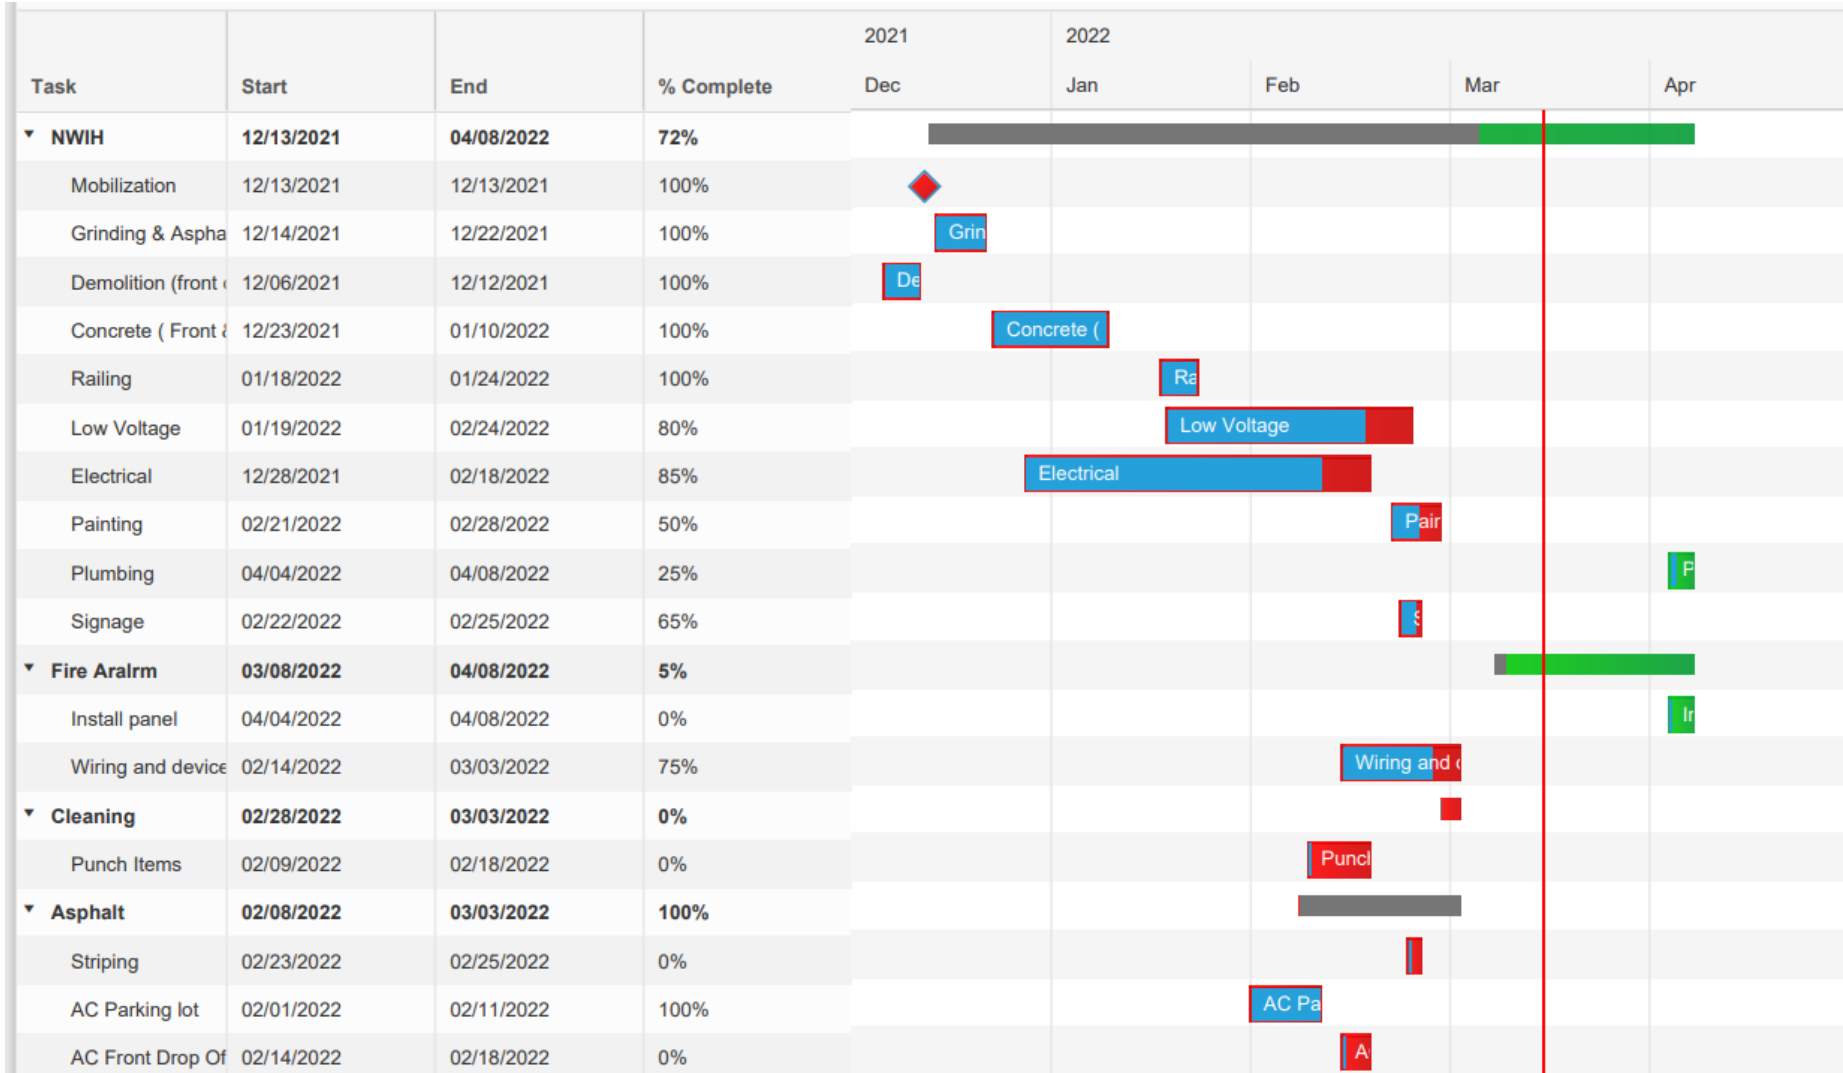



Grandview Academy, Newton, Sparks MS

21st Century Classroom Projects APPROVED BY DSA

- Newton Middle School 6-30-21
- Grandview College Prep 6-30-21
- Sparks Middle School 6-30-21
- Scope review meetings to gain stakeholder input per the Board's guidance at the Special Board Meeting on October 21, 2021

Contractor Pre-Qualifications Underway Public Qualification Period is Currently Open

Re-Programing with Associations, Teachers and Principals


- Storage
- Furniture
- Technology
- Wall Surface/Windows

Project Status
Programming & Qualifying

PROGRESS TRACKING

Newton Middle School 21st Century Classroom Improvements Budget


Total Budget
\$4.06 M

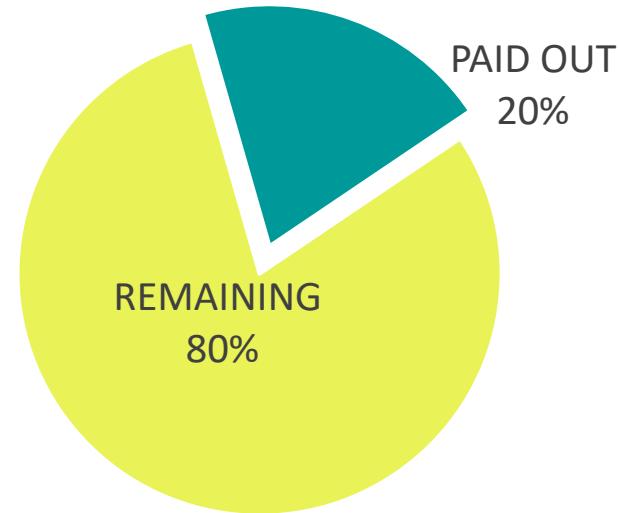

REMAINING
\$3.24 M

PAID OUT
\$0.82 M

Construction Progress - % of Completion




Work Completed

Project Status
Budget and Schedule

PROGRESS TRACKING

Sparks Middle School 21st Century Classroom Improvements Budget


Total Budget
\$3.66 M

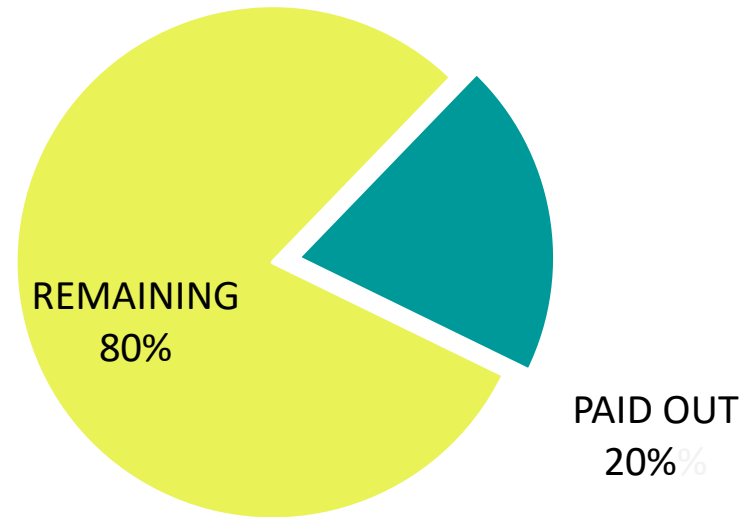

■ PAID OUT
\$0.74 M

■ REMAINING
\$2.92 M

Construction Progress - % of Completion

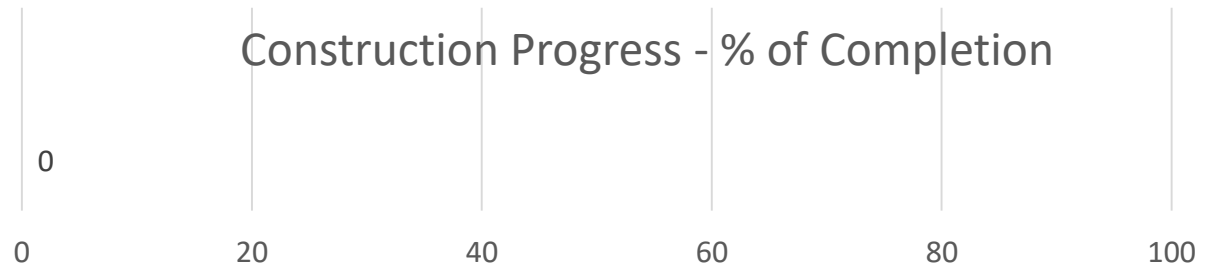


■ Work Completed

Project Status

Budget and Schedule

PROGRESS TRACKING


Grandview College Prep 21st Century Classroom Improvements Budget

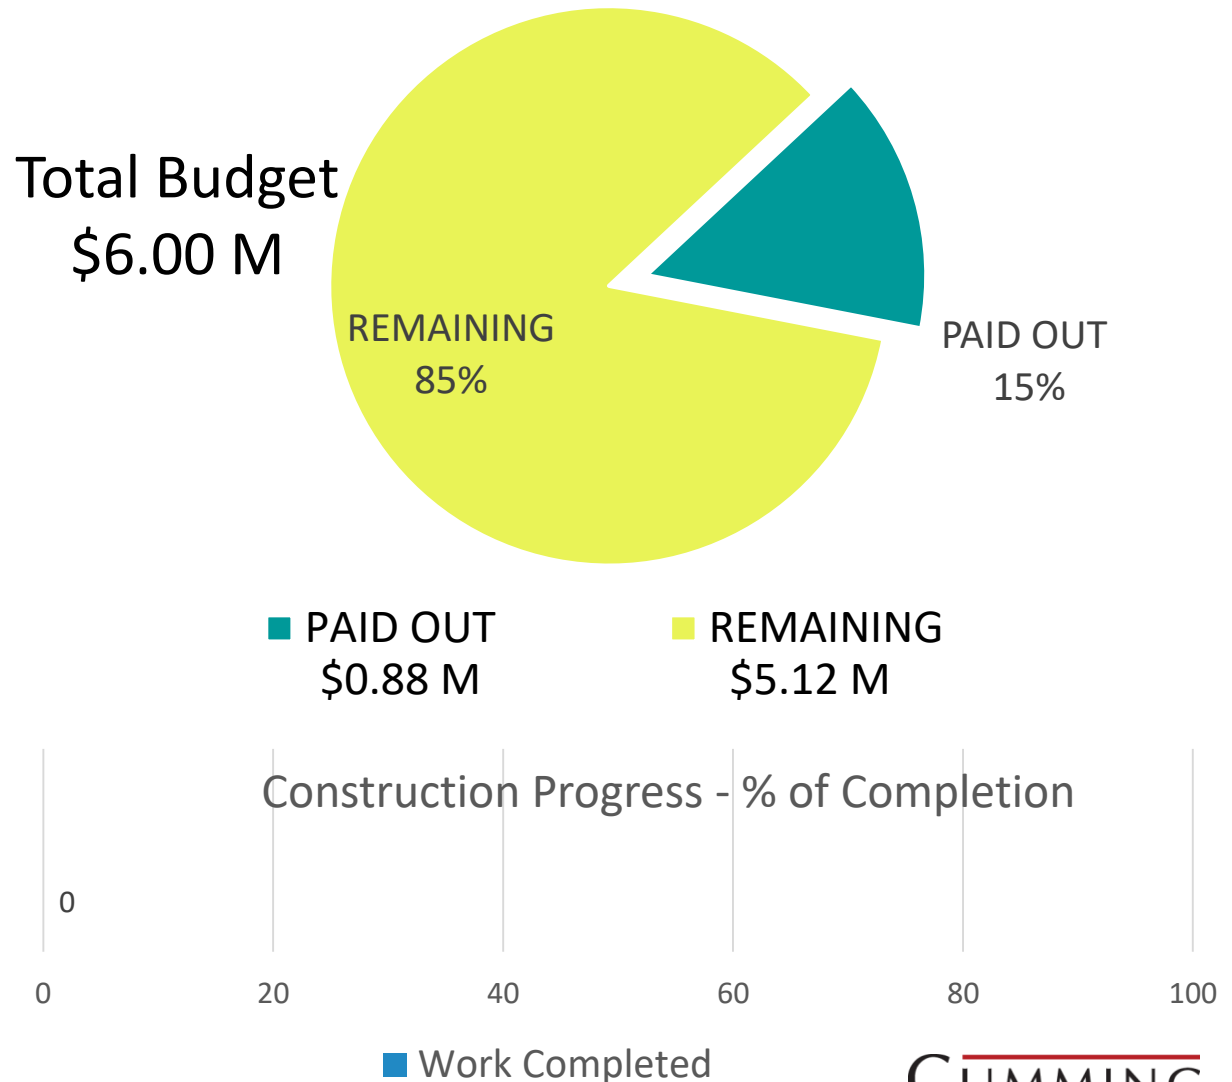


Project Status

Budget and Schedule


Newton MS 21st Century Projected Schedule 5/22/22 to 11/20/23

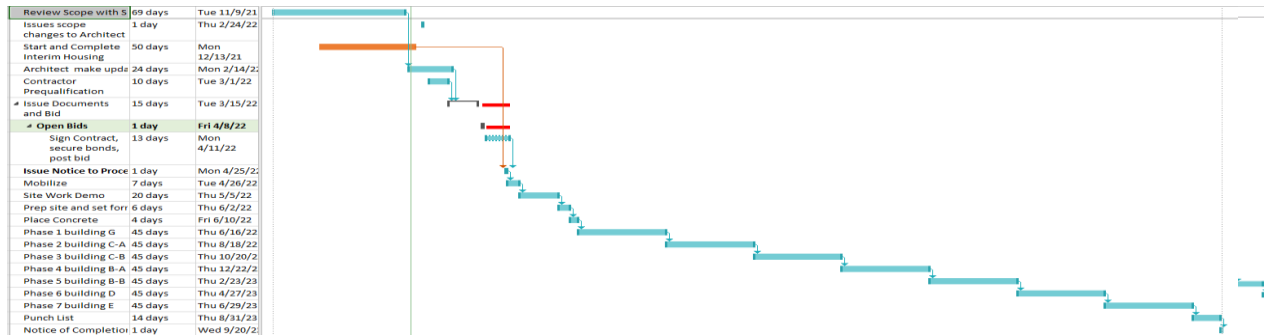


Sparks MS 21st Century Projected Schedule 5/22/22 to 3/2/23

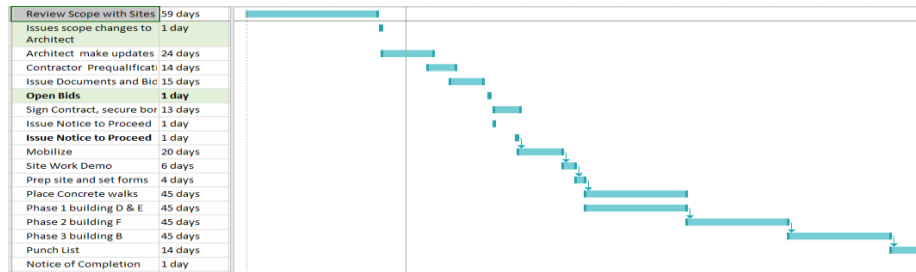

Grandview 21st Century Projected Schedule 5/22/22 to 8/5/23

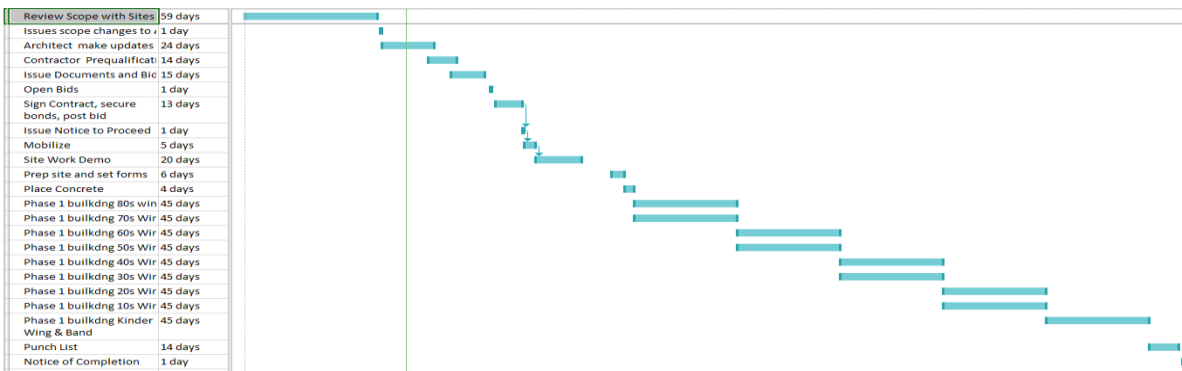



QUESTIONS + ANSWERS

CUMMING
Building Value Through Expertise
