

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
September 24, 2020

Business Services



Completed Projects

2020-2021

School Environment

Business Services: Completed Projects

Projects Completed as of September 24, 2020

Site	Item Description	Construct
Workman HS	Artificial Track and Field Phase I	Complete
District Office	Battery Back Up System	Complete
Amar CC	Bottle Filling Stations	Complete
Los Altos HS	Bottle Filling Stations	Complete
Mesa Robles K-8	Bottle Filling Stations (Attached to Shade Structure Close Out)	Complete
Sunset	Bottle Filling Stations	Complete
Wing Lane	Bottle Filling Stations (Attached to Shade Structure Close Out)	Complete
Willow AS	Concrete Replacement – Lunch Area	Complete
Willow AS	Conference (North) Room Renovation	Complete
District Office	Conference Room Remodel	Complete
Cedarlane	Covered Walkway	Complete
California	Exterior Painting	Complete
Los Molinos	Exterior Painting	Complete
Los Robles	Exterior Painting	Complete
Palm ES	Exterior Painting	Complete
Sparks ES	Exterior Painting	Complete
Sparks MS	Exterior Painting	Complete
Wing Lane	Exterior Painting	Complete
Workman HS	Exterior Painting	Complete
Cedarlane K-8	Fire Alarms	Complete
Newton	Fire Alarms	Complete
Sparks MS	Fire Alarms	Complete
Los Molinos	Floor Replacement - Interior Hallways	Complete

School Environment

Business Services: Completed Projects

Projects Completed as of September 24, 2020

Site	Item Description	Construct
Wilson HS	Floor Replacement - D9, D12 Carpets	Complete
La Puente HS	Front Office Flooring	Complete
La Puente HS	Front Office Painting	Complete
Los Molinos	Hallway Flooring and Painting	Complete
Cedarlane K-8	Head Start Shade Structure Installation	Complete
Los Altos ES	Interim Housing	Complete
Mesa Robles	Interim Housing & Permanent Portables	Complete
Lassalette	Kinder Reroof	Complete
Willow AS	Kitchen Remodel	Complete
Baldwin	MPR Lighting	Complete
Bixby	MPR Lighting	Complete
California	MPR Lighting	Complete
Grazide	MPR Lighting	Complete
Los Altos ES	MPR Lighting	Complete
Los Molinos	MPR Lighting	Complete
Nelson	MPR Lighting	Complete
Sparks ES	MPR Lighting	Complete
Sunset	MPR Lighting	Complete
Amar	New Furniture Replacement	Complete

School Environment

Business Services: Completed Projects

Projects Completed as of September 24, 2020

Site	Item Description	Construct
All Preschool	New Furniture Round 1 (Baldwin, California, Lassalette, Sparks ES, Sunset, Temple)	Complete
All Preschool	New Furniture Round 2 (Bixby, Cedarlane, Del Valle, Grandview, Valinda, Workman ES)	Complete
All Preschool	New Furniture Round 3 (Fairgrove, Kwis, Nelson, Palm, Wing Lane)	Complete
Workman ES	Office Entry Doors and Gates	Complete
Wilson HS	Photoshop Renovation	Complete
Workman HS	Pool Pump Repair	Complete
Los Altos HS	Re-Stripping of Tracks (Warranty Work)	Complete
Wilson HS	Re-Stripping of Tracks (Warranty Work)	Complete
Grandview K-8	Roof Replacement	Complete
Los Molinos	Room 6 – 21 st Century Remodel	Complete
Sunset	Shade Structure Demolition	Complete
Nelson	Synthetic Turf Installation	Complete
La Puente HS	Track Re-Surface	Complete
Nelson	21st Century Sample Classroom	Complete



Projects In Progress

2020-2021

School Environment

Business Services: Current Projects

Projects In Progress as of September 24, 2020

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
Workman HS	Artificial Track and Field Phase II	Complete	In Progress			10/31/2020	Submitted to DSA. CEQA Initial Study Complete
Baldwin	Bottle Filling Stations	Complete	In Progress			12/1/2020	
Bixby	Bottle Filling Stations	Complete	In Progress			12/1/2020	
California	Bottle Filling Stations	Complete	In Progress			12/1/2020	
Cedarlane K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	12/1/2020	
Del Valle	Bottle Filling Stations	Complete	In Progress			12/1/2020	
Dibble AS	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
District Office	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Fairgrove K-8	Bottle Filling Stations	Complete	Complete	Complete	In Progress	11/1/2020	
Grandview K-8	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Grazide	Bottle Filling Stations	Complete	In Progress			12/1/2020	
Hudson AS	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Kwis ES	Bottle Filling Stations	Complete	Complete	In Progress		11/1/2020	
La Puente HS	Bottle Filling Stations	Complete	Complete	In Progress		11/1/2020	
Lassalette K-8	Bottle Filling Stations	Complete	Complete	In Progress		11/1/2020	
Los Robles	Bottle Filling Stations	Complete	In Progress			12/1/2020	
Mesa Robles K-8	Bottle Filling Stations	In Progress	In Progress	Complete	In Progress	11/1/2020	
Nelson	Bottle Filling Stations	Complete	In Progress			12/1/2020	
Newton	Bottle Filling Stations	In Progress	In Progress			12/1/2020	

School Environment

Business Services: Current Projects

Projects In Progress as of September 24, 2020

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
Orange Grove	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Palm Canyon	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Palm ES	Bottle Filling Stations	Complete	In Progress			12/1/2020	
Sierra Vista	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Sparks ES	Bottle Filling Stations	Complete	Complete	In Progress		11/1/2020	
Sparks MS	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Stimson LC	Bottle Filling Stations	Complete	In Progress			12/1/2020	
Temple	Bottle Filling Stations	Complete	In Progress			12/1/2020	
Valinda	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Valley HS	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Wedgeworth	Bottle Filling Stations	Complete	Complete	In Progress		11/1/2020	
Willow AS	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Wilson HS	Bottle Filling Stations	Complete	Complete	In Progress		12/1/2020	
Wing Lane	Bottle Filling Stations	Complete	In Progress	In Progress		12/1/2020	
Workman ES	Bottle Filling Stations	Complete	Complete	In Progress		11/1/2020	
Workman HS	Bottle Filling Stations	In Progress	In Progress			12/1/2020	
Willow AS	Conference (South) Room Renovation	Complete	N/A	Complete	In Progress	12/12/2020	In Progress

School Environment

Business Services: Current Projects

Projects In Progress as of September 24, 2020

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
Grazide	Exterior Painting	N/A	N/A			11/1/2020	
District Office	Fire Alarm	Complete	N/A	In Progress		12/1/2020	
Willow AS	Fire Alarm	Complete	Complete	Complete		12/1/2020	Bid award 9/26/19
Dibble AS	Fire Alarms	Complete	N/A	Complete		12/1/2020	Bid award 9/26/19
Grandview K-8	Fire Alarms	Complete	Complete	Complete	In Progress	12/1/2020	In Progress
La Puente HS	Fire Alarms	Complete	Complete	Complete	In Progress	12/1/2020	Bid award 9/26/19
Los Altos ES	Fire Alarms	Complete	Complete	Complete	In Progress	12/1/2020	Bid award 9/26/19
Los Altos HS	Fire Alarms	In Progress				12/1/2020	
Mesa Robles K-8	Fire Alarms	Complete	Complete	Complete	In Progress	12/1/2020	In Progress
Nelson	Fire Alarms	Complete	Complete	Complete	In Progress	10/1/2020	Bid award 9/26/19
Wilson HS	Fire Alarms	Complete	Complete	Complete	In Progress	12/1/2020	In Progress
Workman ES	Fire Alarms	Complete	Complete	Complete	In Progress	12/1/2020	Bid award 9/26/19
Workman HS	Fire Alarms	Complete	Complete	In Progress		12/1/2020	Bid award 9/26/19
Lassalette K-8	Front Landscape	In Progress					On Hold
Sparks MS	Front Landscape	In Progress					On Hold
Workman ES	Front Landscape	In Progress					On Hold
Baldwin	Irrigation Replacement	In Progress				12/1/2020	
Bixby	Irrigation Replacement	In Progress				12/31/2020	
Cedarlane K-8	Irrigation Replacement	Complete	N/A	In Progress		12/1/2020	
Del Valle	Irrigation Replacement	Complete	Complete	In Progress		12/1/2020	
Fairgrove K-8	Irrigation Replacement	In Progress				12/31/2020	
Grazide	Irrigation Replacement	In Progress	N/A			12/1/2020	
Sierra Vista	Irrigation Replacement	Complete	Complete	In Progress		12/1/2020	

School Environment

Business Services: Current Projects

Projects In Progress as of September 24, 2020

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
Los Molinos	Kindergarten Portable Replacement	In Progress					On Hold
Del Valle	MPR Lighting	N/A	N/A	In Progress		12/1/2020	Part of Phase 4 lighting
Kwis ES	MPR Lighting	N/A	N/A	In Progress		12/1/2020	Part of Phase 4 lighting
Los Robles	MPR Lighting	N/A	N/A	In Progress		12/1/2020	Part of Phase 4 lighting
Palm ES	MPR Lighting	N/A	N/A	In Progress		12/1/2020	Part of Phase 4 lighting
Temple	MPR Lighting	N/A	N/A	In Progress		12/1/2020	Part of Phase 4 lighting
Wing Lane	MPR Lighting	N/A	N/A	In Progress		12/1/2020	Part of Phase 4 lighting
La Puente HS	Music Room Upgrades	N/A	N/A	In Progress			On Hold
Wilson HS	Music Room Upgrades	N/A	N/A	In Progress			On Hold
La Puente HS	New Kitchen	Complete	Complete	In Progress	In Progress	4/30/2021	In Progress
Del Valle	Office entry doors and gates	Complete	Complete				On Hold
Sparks ES	Office entry doors and gates	Complete	In Progress				On Hold
Temple	Office entry doors and gates	Complete	Complete				On Hold
Valinda	Office entry doors and gates	In Progress					On Hold
Grazide	Perimeter Wall Replacement	In Progress					On Hold
Wedgeworth	Permanent School	Complete	Complete			8/1/2021	CEQA Initial Study ready
District Office	Phase II HVAC Replacement	Complete	Complete	In Progress			On Hold

School Environment

Business Services: Current Projects

Projects In Progress as of September 24, 2020

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Target Date	Notes
Cedarlane	Interim Housing	In Progress				10/1/2020	DSA Backcheck
Newton	Interim Housing	Complete	In Progress			12/1/2020	
California	New Rubberized Playground with New Swings	N/A	N/A	In Progress			On Hold
District Office	Police Office Replacement & Restrooms	In Progress	N/A				On Hold
Los Altos ES	Portables	In Progress	Complete	In Progress			On Hold
Wedgeworth	Portables	In Progress					On Hold
Willow AS	Restroom Renovation	Complete	N/A	Complete	In Progress	10/30/2020	In Progress
Amar	Shade Structure - New	Complete	Complete	In Progress			On Hold
District Office	Solar	N/A	N/A	In Progress			Scheduled for 1/21
La Puente HS	Solar	N/A		In Progress			Scheduled for 1/21
Los Altos HS	Solar	N/A		In Progress			Scheduled for 1/21
Willow AS	Solar	N/A	N/A	In Progress			Scheduled for 1/21
Wilson HS	Solar	N/A		In Progress			Scheduled for 1/21
Workman HS	Solar	N/A		In Progress			Scheduled for 1/21
Willow AS	Two-Story Building Renovation	N/A	N/A	In Progress			On Hold
La Puente HS	New Pool	Complete	Complete	In Progress	In Progress	4/30/2021	In Progress

Nelson – C1 Construction (Before & After)



Nelson – 21st Century Classroom



Examples of Personal Protective Equipment (PPE)

- Elementary Schools (Grades TK-6)
 - K-8 Schools
 - Middle Schools
- High Schools (Grades 9-12)
 - Adult Education
 - District Office

Bixby Elementary (TK-5)



Front Counter



Office Counter

Lassalette (TK-8)



Front Counter




Kitchen Register Cart

Office Manager's
Desk



Orange Grove MS (6-8)



Front Counter



Kitchen Register



A/P Portable Desk

Workman High School (9-12)



2-Office Assistant Desk



Office Manager's Desk



Front Counter



Kitchen Register Cart

Hudson Adult Learning Center




Front Counter

Office Desk



District Office

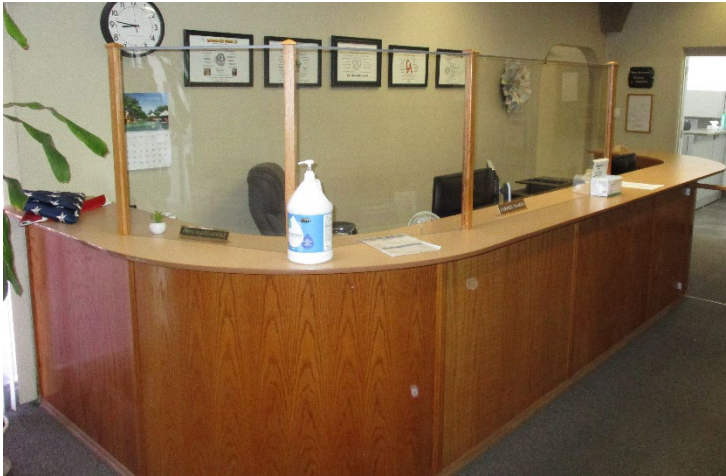

Reception Area



Fiscal Services



Human Resources



Next Report – October 22, 2020
