

# 21st Century Classroom Improvements

November 18, 2021 Board Update





INTERIM HOUSING								
SCHEMATIC DESIGN	DESIGN DEVELOPMENT	CONSTRUCTION	CONSTRUCTION	DSA APPROVAL	OCCUPANCY			
					****			
					****			
					100%			

21 <sup>ST</sup> CENTURY CLASSROOM								
SCHEMATIC DESIGN	DEVELOPMENT	CONSTRUCTION DOCUMENTS	DSA APPROVAL	CONSTRUCTION	COMPLETION			
					****			
					****			

100%

## **NOTES**

- Interim Housing Complete Close Out Phase
- Interior Phases 1 through 5 Complete
- Next steps:
- CLOSEOUT & DSA CERTIFICATION

Project Status
SUBSTANTIALLY
COMPLETE






#### **ALL PHASES SUBSTANTIALLY COMPLETE**



- 1. HVAC Grills
- 2. Conduit run



21st Century Classroom Improvements

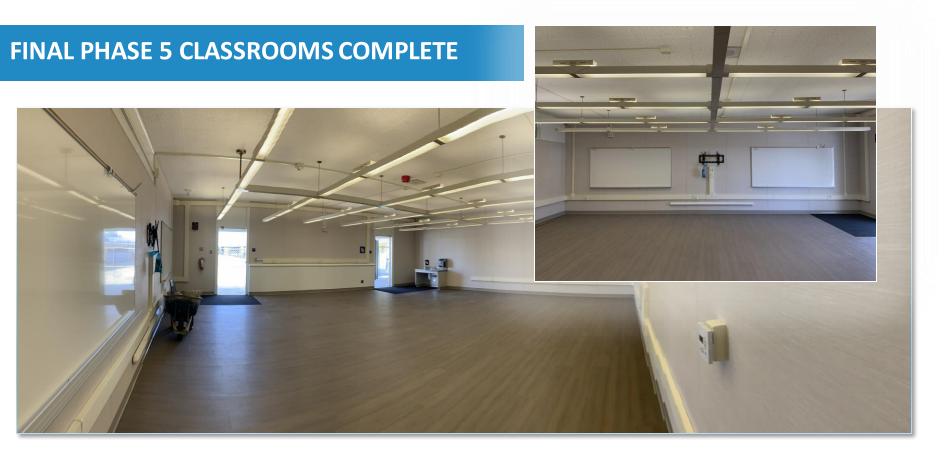

Project Status

SUBSTANTIALLY

COMPLETE





**Interior Improvements** 

#### **BAND ROOM COMPLETE**





Project Status
SUBSTANTIALLY
COMPLETE



# Grandview Academy, Newton, Sparks MS



# Newton Interim Housing AWAITING START

Interim Housing bid opened 7-15-21

Notice to Proceed Pending


**Board approval** 

Project Status
3 Schools Bid Ready

#### **NOTES**







#### 21st Century Classroom Projects APPROVED BY DSA

Newton Middle School 6-30-21

Grandview College Prep 6-30-21

Sparks Middle School 6-30-21


 Scope review meetings scheduled with site principals to gain stakeholder input per the

Board's guidance at the Special




**Board Meeting** 


## Newton Projected Schedule 2-23-22 to 5-30-23



Sparks MS Projected Schedule 2-23-22 to 1-23-23



## Grandview Projected Schedule 2-23-22 to 3-22-23







**QUESTIONS + ANSWERS** 

