



Update on FCPS Construction/Renovation Projects

November 2020



STEAM & Success Academies

- ▶ Architect: Ross Tarrant Architects
- ▶ General Contractor: D.W.Wilburn, Inc.
- ▶ GC Contract Sum: \$22,108,500.00
- ▶ Total Project Cost: \$26,990,125.53
- ▶ Change Orders to Date (12): \$477,336.66
- ▶ Scheduled Contract Completion Date: October 15, 2020
- ▶ % of Contract Completed: 99%
- ▶ Revised Completion Date per GC: September 9, 2020
(District began moving in)

STEAM & Success Academies


Front Façade



STEAM & Success Academies

► **Current Work Effort (November):**

- Interior back punch list items to complete December 5.
- Exterior back punch list items to complete December 5.

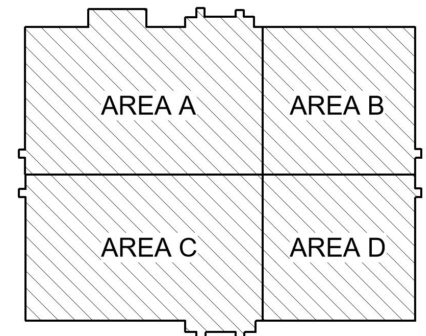

November 2020

STEAM & Success Academies

STEAM & Success -- Café




STEAM -- Commons Area



STEAM -- Multipurpose Space



STEAM – Stair & Commons Area

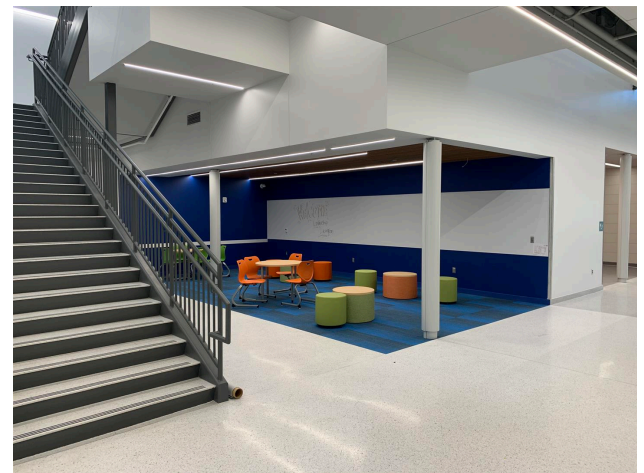

STEAM & Success Academies

Success -- Visitor Entrance



Success -- Classroom



Success – Commons Area



STEAM – Co-Lab

