




21st Century Classroom Improvements

June 22, 2023 Board Update



Sites In Progress & Completed

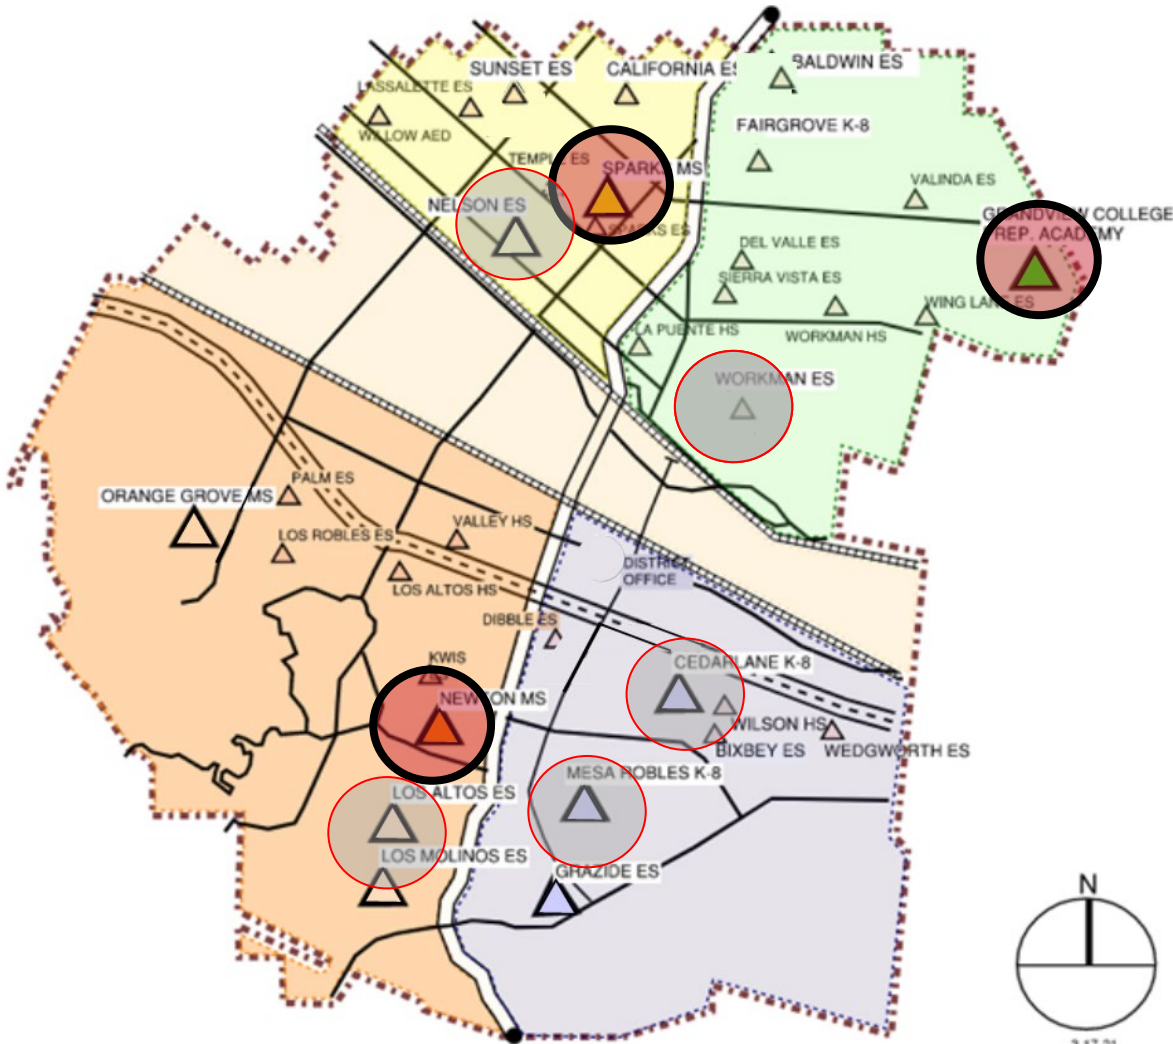

IN PROGRESS

Newton MS
Grandview K-8
Sparks MS

COMPLETED

Nelson ES
Los Altos ES
Workman ES
Mesa Robles K-8
Cedarlane K-8

Newton Middle School

Phases 1 & 2



Project Status

Construction

New Built-In Cabinets




CUMMING
Building Value Through Expertise

Newton Middle School

KPI Overview

NWMS 21 ST CENTURY CLASSROOM

Budget	Committed	Balance
\$ 4.70M	\$ 3.61M 76.8%	\$ 1.09M 23.2%

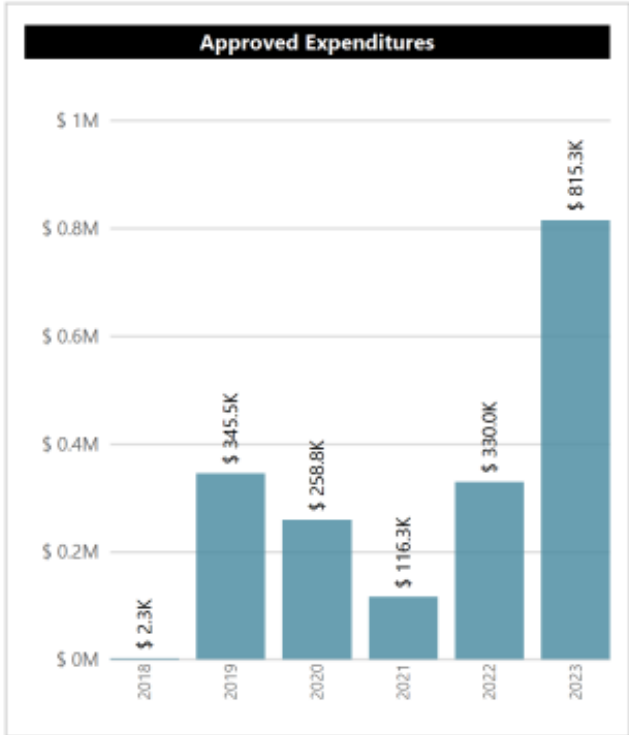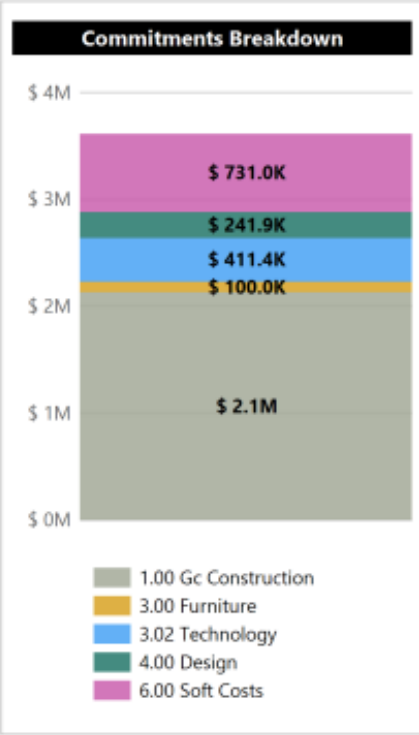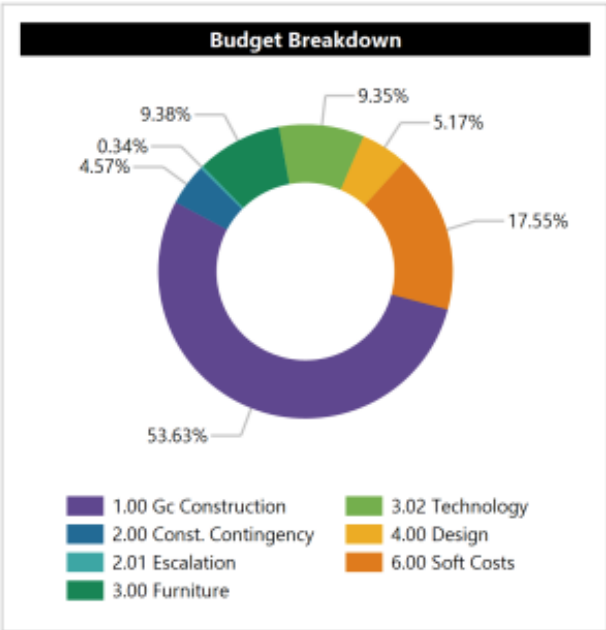

Modernization Plan

Classrooms: 19

Music Room: 1

Project Status

Budget

Grandview College Prep. Academy

Construction Improvements



Project Status




Construction

Grandview College Prep. Academy

KPI Overview

GVCPA 21ST CENTURY CLASSROOM

Budget	Committed	Balance
\$ 5.95M	\$ 4.31M 72.5%	\$ 1.64M 27.5%

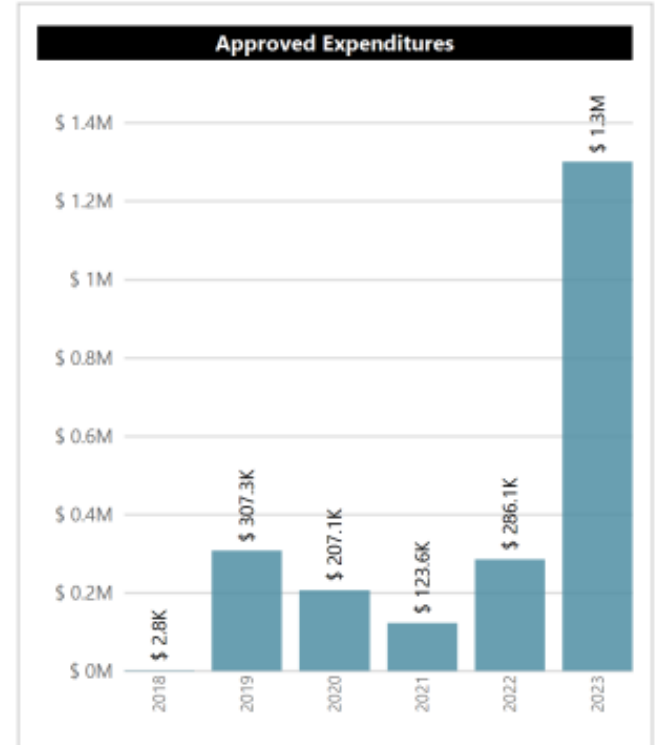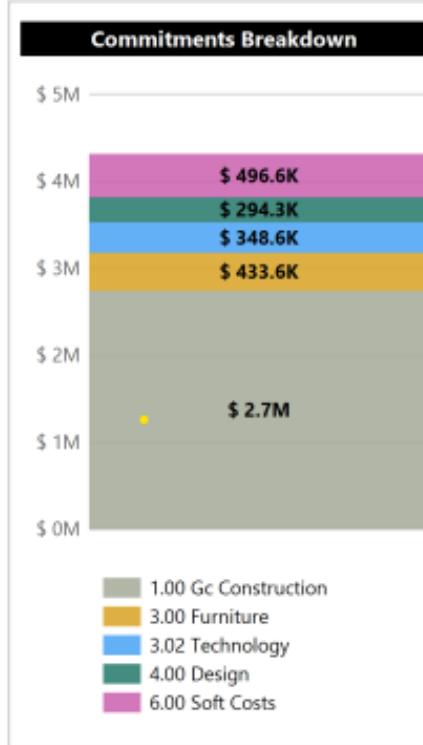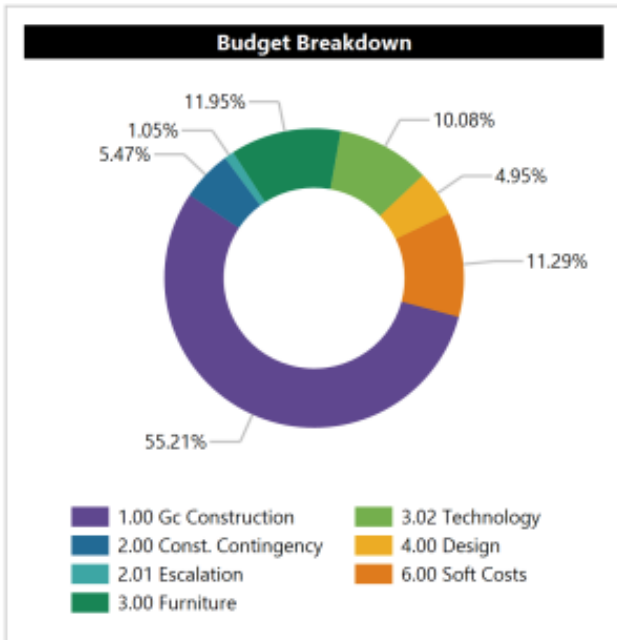

Project Status

Budget

Modernization Plan

Classrooms: 18

Music Room: 1

Kinder: 2


Sparks Middle School

Phase 1: 9-16

Complete

Phase 2: 17-20 Music/Band

In progress

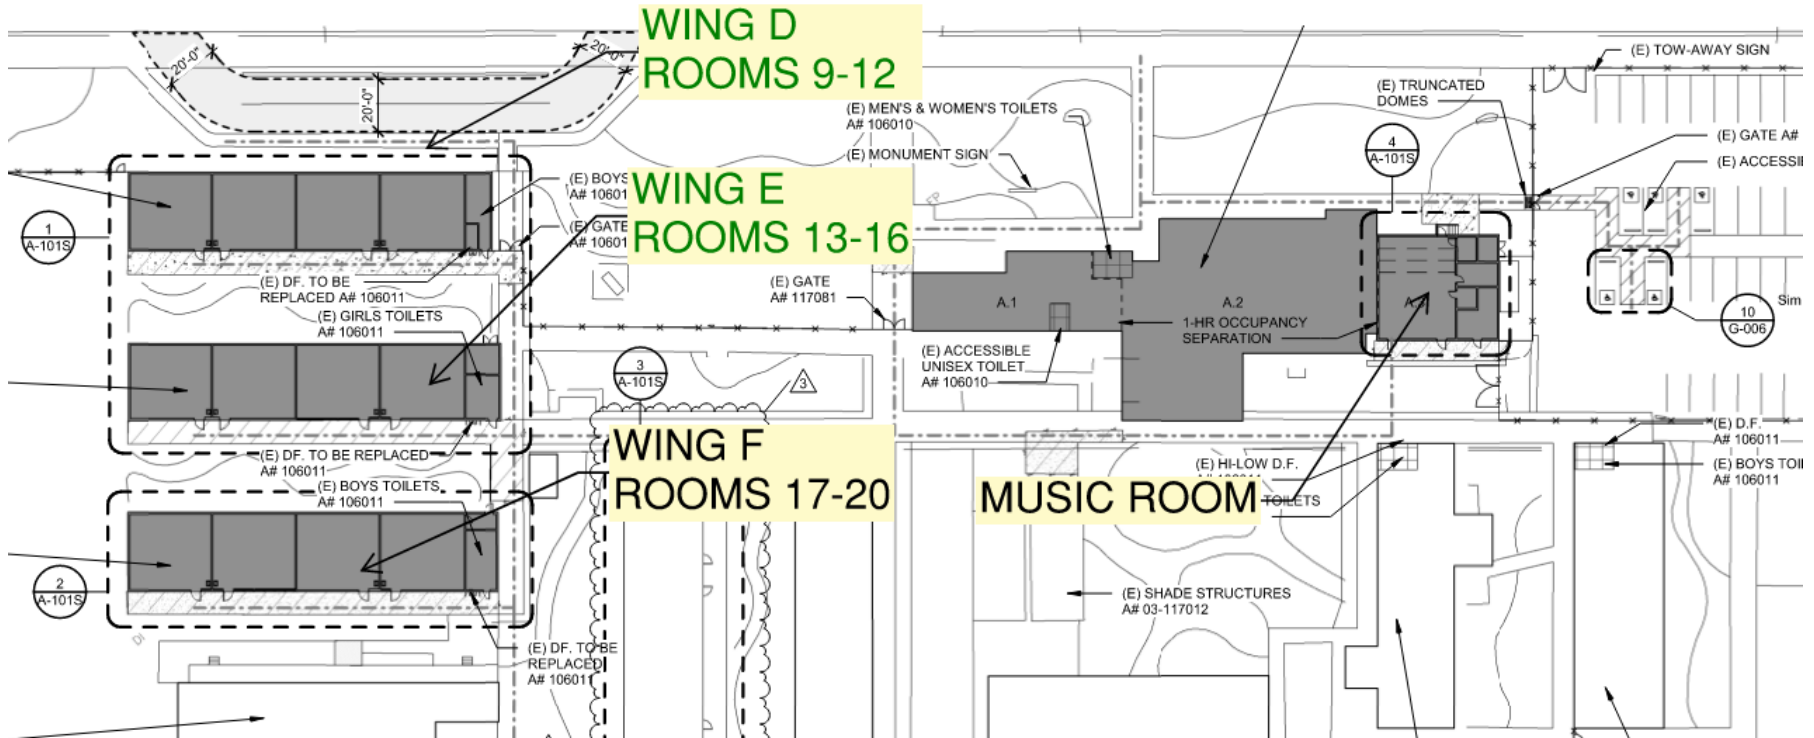

Site Plan & Status
Construction

Sparks Middle School






Project Status
Construction

Sparks Middle School

KPI Overview

SPKMS 21ST CENTURY CLASSROOM

Budget	Committed	Balance
\$ 3.58M	\$ 2.95M 82.4%	\$ 0.63M 17.6%

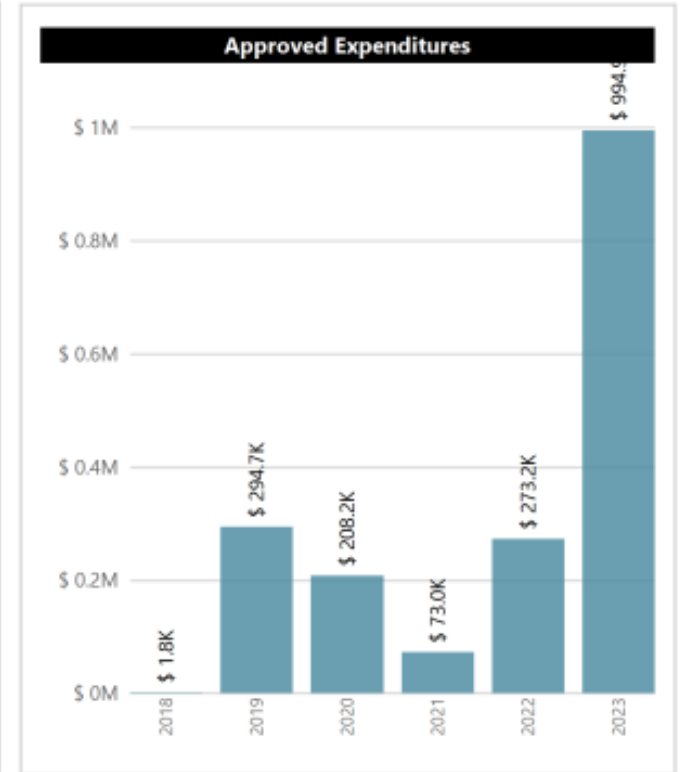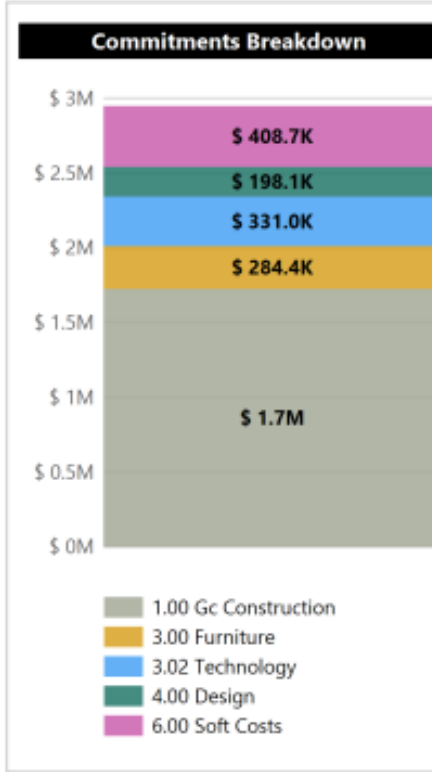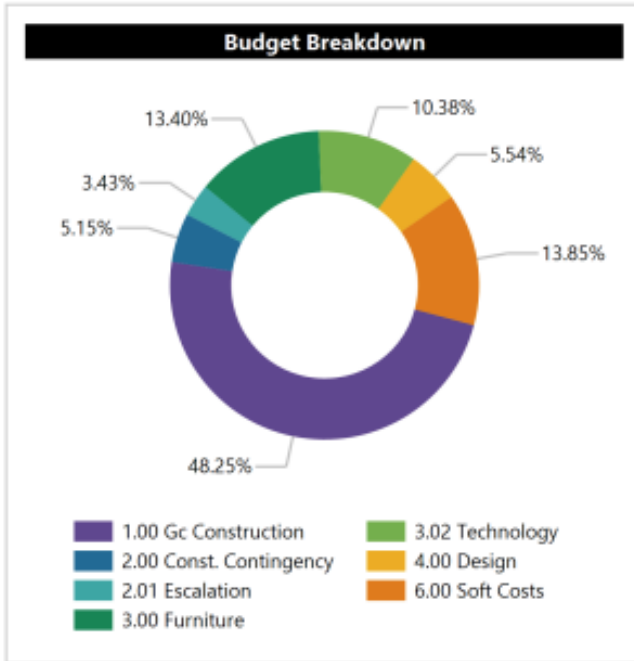

Modernization Plan

Classrooms: 12

Music Room: 1

Project Status

Budget




Scheduled Completion

Sparks MS: June 2023

Grandview: September 2023

Newton MS: October 2023



QUESTIONS + ANSWERS

CUMMING
Building Value Through Expertise
