# **TULSA PUBLIC SCHOOLS**

# Citizen Bond Oversight Committee September 12, 2023

Greg Shaw, Chairperson

#### TPS Staff:

Chris Hudgins, Exec. Dir. Bond Ellen Duecker, Bond Project Mgr. Maddie Carter, Admin. Asst.





# **TULSA PUBLIC SCHOOLS**

Citizen Bond Oversight Committee

**2021 Bond** 

**Progress Report** 

October 2, 2023

**Gregory Shaw, Chairperson** 







#### Today's Agenda

- Welcome & Introductions: Greg Shaw
- Meet Burroughs Principal, Dee Tisdale
- Approval of minutes
- Bond Projects Reporting: Staff
  - Bond status
  - Summer projects report
- Adjourn
- Tour Burroughs
- Next meeting: November 14, 2023 at Hale Senior High





Authorized: \$414MM

Received: \$192.5MM

Remaining: \$221.5MM

Next Bond Release: March, 2024

**Growth: Net evaluations** have increased!

2021 Bond Progress: Budget

46% funds received

6.5 years for project completion

MANAGING DEPARTME	NT PROJECT DESCRIPTION	AVAILABLE (UNSPENT) BUDGETS	Ī
CADEMICS	INSTRUCTIONAL LEARNING RESOURC	1,156,428.69	
	TEXTBOOKS & LEARNING MATERIALS	4,617,837.33	
	EXCEPTIONAL STUDENT/SPEC NEEDS	565,731.27	
	PROF LEARNING FOR TEACHERS	850,495.86	
	AUDITORIUM IMPROVEMENTS	709,664.62	
	LANGUAGE LEARNING RESOURCES	148,410.67	
	SCHOOL PROJECT FUNDS	3,141,773.88	
	POSTSECONDARY CAREER EDUCATION	585,194.09	
	EARLY CHILDHOOD EXPANSION	1,374,658.40	
	PROGRAM EXPANSIONS	704,549.94	
	SCOREBOARDS/SOUNDSYS REPLACMNT	5,319.36	
	WELLNESS AND PE	5,499,198.89	
	FINE ARTS	122,486.66	
	LIBRARY DIGITAL/PRINT RESOURCE	691,607.88	_
ECHNOLOGY	SECURITY CENTRAL OFFICE NEEDS	1,357,978.96	
	MASS COMMUNICATION AUDIO/VISUA	107,250.58	
	COMPUTERS/IWB & PERIPHERALS	1,451,006.51	
	ACCESS DOORS	1,203.25	
	CAMERAS/RADIOS/DISPATCH	677,361.68	
	ALARMS	1,786,564.07	
	BOND MANAGEMENT FEES	3,143.36	
	PHONE/INTERNET NEEDS	9,537.99	
	SOFTWARE/APPLICATION SUBSCRIPTION	542,527.98	
ACILITIES	HVAC	209,514.68	
	SECURE ENTRIES & FENCING	1,928,498.55	
	ACCESSIBILITY	496,040.19	
	PAVING	0.00	
	ROOFING	1,096,458.58	
	DINING/KITCHEN IMPROVEMENTS	0.00	
	FURNITURE	975,535.44	
	INTERIOR RENOVATIONS	2,245,343.96	
	PLANNED-UNBID/ARCHITECTS/CONTINGENCY	1,285,160.54	
	PROFESSIONAL SVC/BOND MNMT/ISSUANCE FEES	160,162.87	_
RANSPORTATION	SCHOOL BUSES / ROUTE MAIN	3,214,551.61	

# 2021 Bond: Current Available Funds 9/8/23



Summer Projects Report

Nonstop (almost)
9 week challenge!





#### 2023 Summer Bond & Construction Work

#### School Full Building-wide Interior Renovations:

- Burroughs Elementary
- Bell Elementary

#### **Kitchen and Dining Remodels:** (Impacted by equipment delays)

- Memorial
- Eliot Elementary
- and renovation schools, Burroughs, Bell
- Plus Rogers outdoor covered dining space

#### **Enhanced Secured School Entries Installed:**

- Central Middle/High
- East Central Senior High
- Hale Senior High
- Memorial Senior High
- Memorial Middle School
- Webster Middle/High
- Alcott (North Star & Parent Resource Center)

**新女器** 

- Tulsa MET
- Phoenix Rising
- Legacy lower and upper





## 2023 Summer Bond & Construction (Cont.)

#### **Library Remodels and Refreshes:**

- Central
- Webster
- Burroughs
- Carver (refresh)
- Lewis & Clark (refresh)
- Eugene Field (refresh)

#### **Science Lab Improvements:**

Hale Senior High: electrical upgrades, flooring, painting, furniture

#### **Various Other Construction Projects:**

- East Central Middle: cafeteria expansion and locker and auditorium seat replacement
- Grissom Montessori: sink installation in 10 classrooms
- Eisenhower: roofing
- Webster, Memorial and Central: Entry rebuild







### 2023 Summer Bond & Construction (Cont.)

#### Fine Arts:

 Auditorium Improvements continue district wide including stage and house lighting and sound improvements at multiple schools.

#### **College & Career:**

- Expanded into a 2nd career construction classroom at Hale
- Webster Aquaponics/hydroponics lab construction underway

#### **Athletics:**

- Rogers visitors stands complete. Concession under construction
- Scoreboards East Central and LaFortune
- Time Clocks: McLain, BTW, Eastside, Lafortune

#### **Academics Adoptions and Purchases:**

- Secondary ELA, English language arts curriculum
- Secondary World Languages, other than English, curriculum
- Secondary ELD, English language development curriculum
- Elementary and secondary math and literacy intervention resources
- Secondary digital instructional resources







# 2023 Summer Bond & Construction (Cont.)

#### **Playground Installations**

- Cooper Elementary 2
- Skelly Primary
- Carnegie Elementary
- Eugene Field Elementary 2
- Salk pre-k play area

#### Parking Lot Resurfacing:

 Central, East Central Sr. High, Thoreau, Disney, Zarrow, Lindbergh, ESC, Greeley Legacy

#### **Fence Replacements:**

Improves safety as well as enhances appearance!

 Bell, Cooper, Grissom, Peary, Sequoyah, Patrick Henry, Carnegie, Eliot, Mitchell, Whitman, Unity.

#### In addition to bond funded projects: Federally Funded HVAC Work

 Hale Senior High School: Full HVAC System Replacement done in tandem with other bond work throughout.


## **Schedule & Collaboration Critical!**

7 days a week!

Phases!




Carver August 9th



Burroughs August 9th

# **Schedule & Collaboration Critical!** August 1st: Hale Sr.High... Working together to be ready for staff and students.

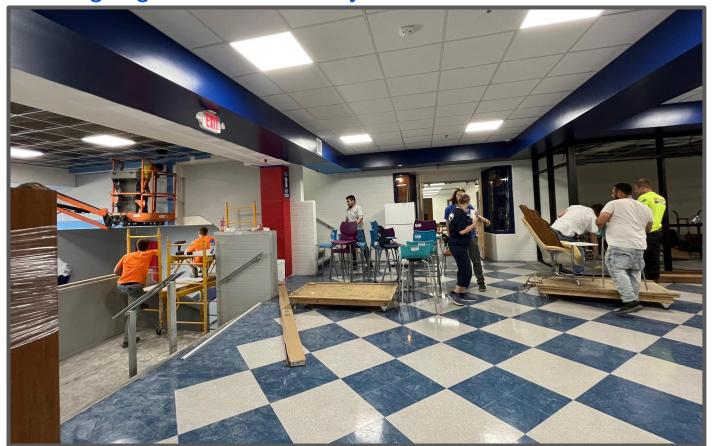

Working alongside school staff:

- → HVAC installers
- → Movers
- → Glaziers
- → Painters
- → Plumbers
- → Electricians
- → Flooring installers
- → Cleaners



Renovations:
Burroughs Elementary
Historic School
Revitalized!

Built in 1925

Project cost approx. \$3.5MM



Renovation:
Burroughs Elementary
Historic School
Revitalized!

#### Unique challenges:

Floor & subfloor structural integrity, kitchen rebuild to code (grease traps and exhaust), extensive millwork replacement, creating accessible spaces throughout.



Before

Hallways

# Renovations: Burroughs Elementary Historic School Revitalized!



After




Renovations:
Burroughs Elementary
Historic School Revitalized!

Before

Classrooms... New furnishings along with interior upgrades welcome students!

After

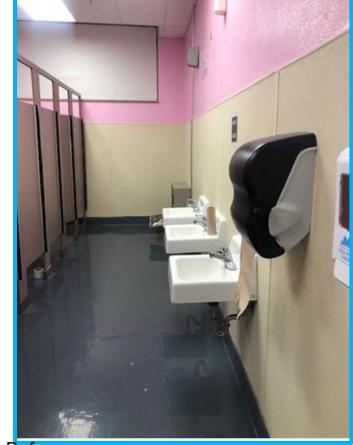

Before

Restrooms

After

# Renovations: Burroughs Elementary Historic School Revitalized!




### Renovation: Burroughs Elementary...Historic School Revitalized!



Renovation offers an opportunity to align spaces with program needs.

Library media center & computer lab **before** renovation.

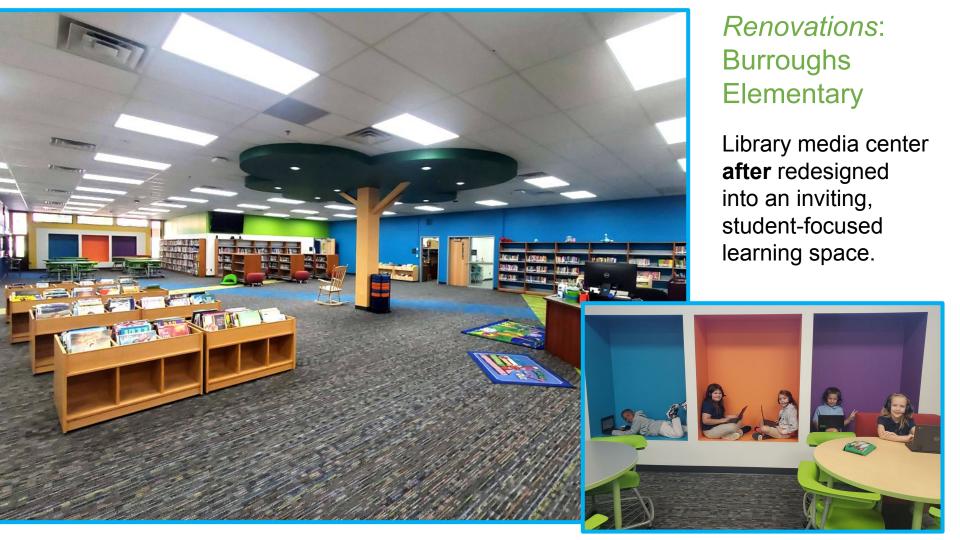



Renovations: Bell Elementary...

Newly renovated for young learners!

Built: 1952 Project cost \$5.5MM

Formerly a junior high, the renovation made the full transition to an elementary space for young learners. Early childhood classrooms were created in the 2015 bond. This renovation modernized the entire building.

ADA building modifications are an important focus in all construction projects. Bell is an example where they accounted for approximately 20% of construction costs.



Renovations: Bell Elementary... Newly renovated for ALL young learners!

#### ADA modifications included:

Entry/exit ramps
Widening narrow doorways
Rebuilding restrooms from ground up to meet code.



Before

Classrooms: new flooring, paint and millwork welcome students.


# Renovations: Bell Elementary... Newly renovated for young learners!





# Renovations: Bell Elementary... Newly renovated for young learners!



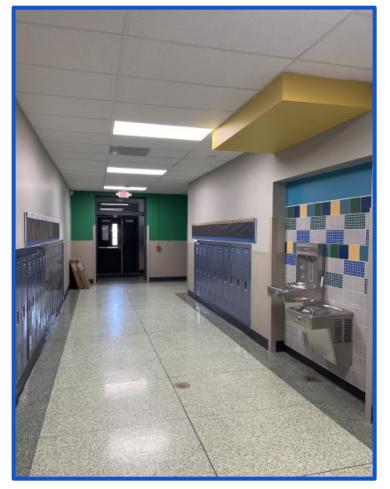

Hallways are brighter and more inviting!



Renovations: Bell Elementary...
Newly renovated for young
learners!

Before

Cafeteria



Renovations: Bell Elementary... Newly renovated for young learners!




Bell auditorium: New stage lights, electrical upgrades, paint and curtains. Sound system in progress. *More about auditoriums later...* 



Kitchen Dining Renovations: Included new cooking and refrigeration equipment and serving lines.

- Eliot
- Burroughs
- Bell
- Memorial Senior

Major and minor issues caused delays but on track for completion.

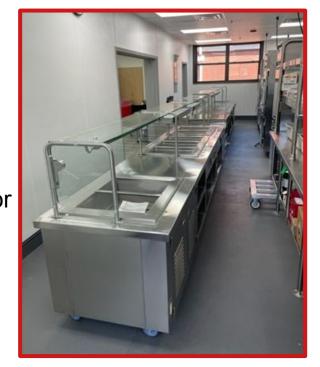





# Kitchen Dining Renovations:

### Rogers:

Canopy over outdoor dining area:

- Create inviting space for students almost year round
- Increases seating capacity
- Allows for 2 lunch periods

Nearly complete Target 10/1

### Safety and Security: Enhanced Secured School Entries

Installed at 10 Schools this summer

Designs are customized for each site

Work typically involves a full office redesign in addition to door installation

- Central Middle/High
- East Central Senior High
- Hale Senior High
- Memorial Senior High
- Memorial Middle School
- Webster Middle/High
- Alcott (North Star/Parent Resource Center)
- Tulsa MET
- Phoenix Rising
- Legacy lower and upper



# Safety and Security: Enhanced Secured School Entries Weapons Detection Systems for Secondary Schools

District team conducted research last spring and summer.

Purchased 34 portable systems that can be deployed in multiple locations around the school and the district where needed.

- 2 per high schools (main building and fieldhouse/stadium)
- 3 per grade 6-12 middle & high schools
- 1 for middle schools and alternative sites

Trainings were conducted for each school team prior to school starting.

Currently in post implementation evaluation phase

- Set-up at all our high school varsity football games
- Set-up at visitor entrances of each site
- Schools are evaluating frequency of use for continuous or intermittent monitoring at student entrances

### Safety and Security: Enhanced Secured School Entries

Door access control systems: additional doors installed district-wide.

- Spring, 2023: Site visits to identify & map needs for additional door access controls.
- Playground and parking lot secondary entrances/exits.

HOOVER

SPRINGDALE

LEWIS AND CLARK

OWEN

PEARY

- Costs per door range from approx. \$3500 to \$4200 per door.
- Supply chain issues are impacting installation

DISNEY

CARNEGIE

KENDALI WHITTIER

CLINTON WEST

Phase 1	Phase 2	Phase 3	Phase 4
BELL	DOLORES HUERTA	EMERSON	MAYO
ELIOT	EISENHOWER	EUGENE FIELD	MCKINLEY
MCCLURE	MONROE	FELICITAS MENDEZ	ROBERTSON
ANDERSON	MITCHELL	GLA	SALK
CELIA CLINTON	KEY	HAMILTON	SKELLY UPPER
BURROUGHS	JOHN HOPE FRANKLIN	HAWTHORNE	SKELLY LOWER
COOPER	GRISSOM	LANIER	UNITY
	WALT WHITMAN	LINDBERGH	WAYMAN TISDALE
PATRICK HENRY	SEQUOYAH	MACARTHUR	
COUNCIL OAK	MARSHALL		


Green indicates complete
All others are in the process of being quoted.

### Secondary School Entrances

Along with enhanced secure modifications, the bond plans included updating secondary school facades to welcome students and families.

Senior Highs: East Central, Memorial, McLain, Hale Middles: Thoreau, Memorial, Hale, East Central, Carver



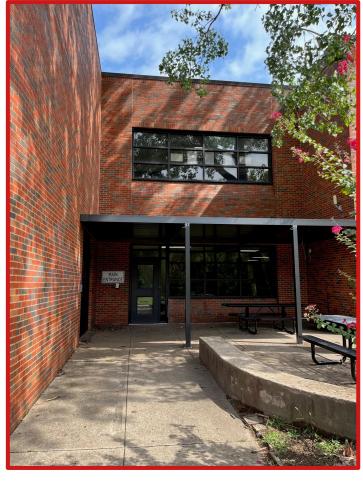

Central Middle High New Entrance

Memorial Senior High Entry (under construction)



# Webster Middle High Historic Entry..nearly complete



# Library Renovations and Refreshes

- Central
- Webster
- Burroughs
- Carver (refresh)
- Lewis & Clark (refresh)
- Eugene Field (refresh)

Central Middle & High...School spirit reflected in design



# Library Renovations and Refreshes

Webster Middle High



Honoring historic designs while creating: modern, flexible, personalized learning spaces.

## Library Renovations and Refreshes



Kendall-Whittier graphic ceiling border finishes off last summer's remodel.

Carver, Eugene Field and Kendall Whittier



## Playground Installations

- Cooper Elementary 2
- Skelly Primary
- Carnegie Elementary (Special needs unit)
- Eugene Field Elementary2
- Salk pre-k play area

This completes all new playground installations!

Additional funds remain to upgrade/refresh existing playgrounds. (replace wood chips with accessible surface!)



Athletics:

Rogers Visitor Stands and Concessions/Restrooms

Visitors stands open for first game!

Concession stand and restrooms in progress.



#### Athletics:

New Time Clocks & Scoreboards

#### Scoreboards:

- Eastside
- Lafortune


#### Time clocks:

- McLain
- BTW
- Eastside
- Lafortune



Fine Arts: Auditorium Improvements district-wide...lighting, sound, curtains, electrical upgrades as needed.

Investing wisely to extend systems life with IP addressing for remote control and timed system shutdown.







Locking cage over catwalk ladder.

# Fine Arts: Auditorium Improvements district-wide...

Improvements include <u>safety</u> upgrades to catwalks, railings and rigging.



Railing along edge of orchestra pit. It never had one!

Fine Arts:
Auditorium
Improvements
district-wide

Progress to date

25 auditoriums in secondary and formerly secondary schools.

Included in FCI, facilities condition assessment


		Sound System	Stage Lights	Electrical Upgrades	Curtains (& rigging)
	BTW	<b>V</b>	95%	<b>V</b>	!
	Central	<b>V</b>	contracted	contracted	!
e:	E. Central Sr.	<b>V</b>	<b>V</b>	<b>V</b>	!
	Edison	<b>V</b>	In progress	In progress	N/A
У	Hale Sr.	contracted	<b>V</b>	<b>V</b>	<b>~</b>
	McLain	<b>V</b>	<b>V</b>	<b>V</b>	<b>V</b>
	Memorial Sr.	<b>V</b>	In progress	In progress	
	Rogers	<b>V</b>	<b>V</b>	<b>V</b>	90%
	Webster	contracted	In progress	In progress	70%

	School	Sound System	Stage Lights	Electrical	Curtains		
Fine Arts: Auditorium	Carver	RFP	P.O. issued	Awaiting quote	In contract		
Improvements	E. Central Middle	RFP	P.O. issued	Awaiting quote	In contract		
district-wide	Hale Middle	RFP	P.O. issued	Awaiting quote	In contract		
	Memorial Middle	RFP	P.O. issued	Awaiting quote	In contract		
	Monroe	•	<b>~</b>	<b>v</b>	<b>~</b>		
	Thoreau	2015 bond	P.O. issued	Awaiting quote	In contract		
	Bell	Under contract	90%	<b>v</b>	•		
	Lewis & Clark	•	•	<b>v</b>	•		
	Wayman Tisdale	RFP					
	Skelly	<b>~</b>					
	Anderson				<b>v</b>		
Additional sites will be added to charts as work is scheduled.							

East Central Middle School: Auditorium improvements included new seats, carpet and paint. Curtains, sound and stage lighting are in progress.

In addition, East Central received new lockers and a cafeteria expansion



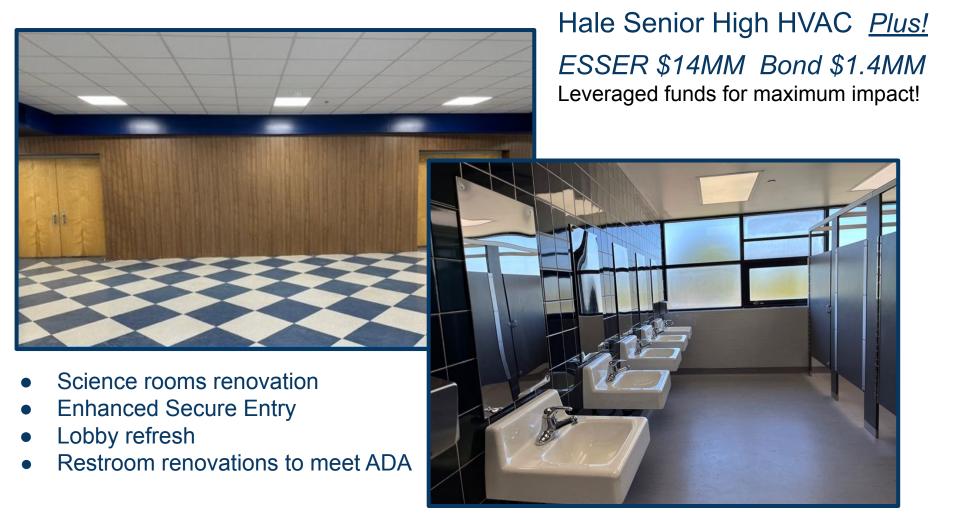

## Webster Middle Senior High Construction On Schedule to complete for 2024



Hydro and Aquaponics Labs



**Band Room Addition** 

## Fence Replacements: Improve safety and school image





Phase 1	Phase 2	Phase 3 Summer '23	
Rogers	Springdale	• Bell	
Hawthorne	Salk	<ul> <li>Carnegie</li> </ul>	
Burroughs	Hoover	• Cooper	
Disney	Celia Clinton	• Eliot	
Clinton West	Kerr	• Grissom	
Marshall	Lewis & Clark	<ul> <li>Mitchell</li> </ul>	
	Tulsa MET	• Peary	
	Lindbergh	<ul> <li>Sequoyah</li> </ul>	
	McKinley	• Unity	
	Robertson	<ul><li>Whitman</li></ul>	
		Patrick Henry	

# **Transportation Bond...Progress Finally!**



#### Received:

- 8 CNG SPED Buses with air conditioning!
- 10 half- ton pickup service vehicles
- 9 Police vehicles.

#### Awaiting:

- 5 months away from receipt of
   15 nine-passenger vans
- 4 months away from delivery on 10 Type A buses for senior highs and programs!



Please don't hesitate to contact Chris or Ellen if you have any questions or concerns before then.

Chris Hudgins hudgich@tulsaschools.org

Ellen Duecker dueckel@tulsaschools.org 918-746-6520



Next Committee Meeting: November 14th @ Hale Sr. High

