



Kerrville

Independent School District

Bond 2018

2018 Bond Program Update

6.17.19



Project Calendar Expectations



Our Goal: All projects completed on time, under budget, with highest quality

Safety Items

- Package 1 and Package 3 - Vestibules completed (August 2019)

Roofs, HVAC, MEP, et al.

- Package 2 completed (December 2020)

New Construction - HPMS

- March 25 Schematic Design Board Approval
- May 20 Design Development Phase 100% complete
- Break Ground (September 2019)
- 18+1 Months Construction w/ Final Completion (May 2021)





Summer 2019 Progress

Package 1: Safety

PBK Architects

**5/20 Door locks
expenditure approved by
Board. (August 9th
substantial completion)**

**5/20 Safety cameras
expenditure approved by
Board (August 9th
substantial completion)**


Package 3: Secured Vestibules

Huckabee, Inc. Architects

6/4 Work began

**8/2 Substantial
completion**

Starkey ES

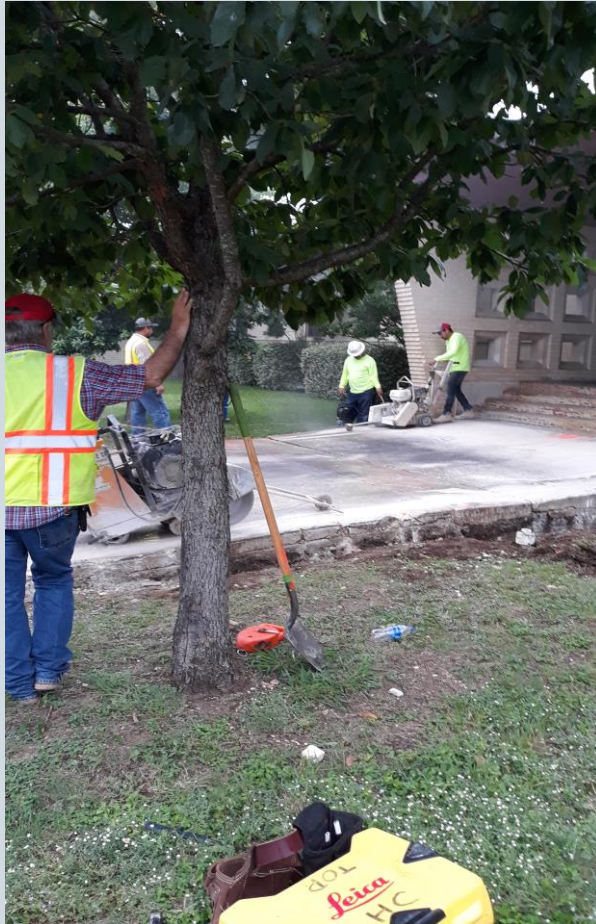


Starkey ES



Daniels Elementary and BTW 6th Grade School



Hal Peterson Middle School – Next Steps

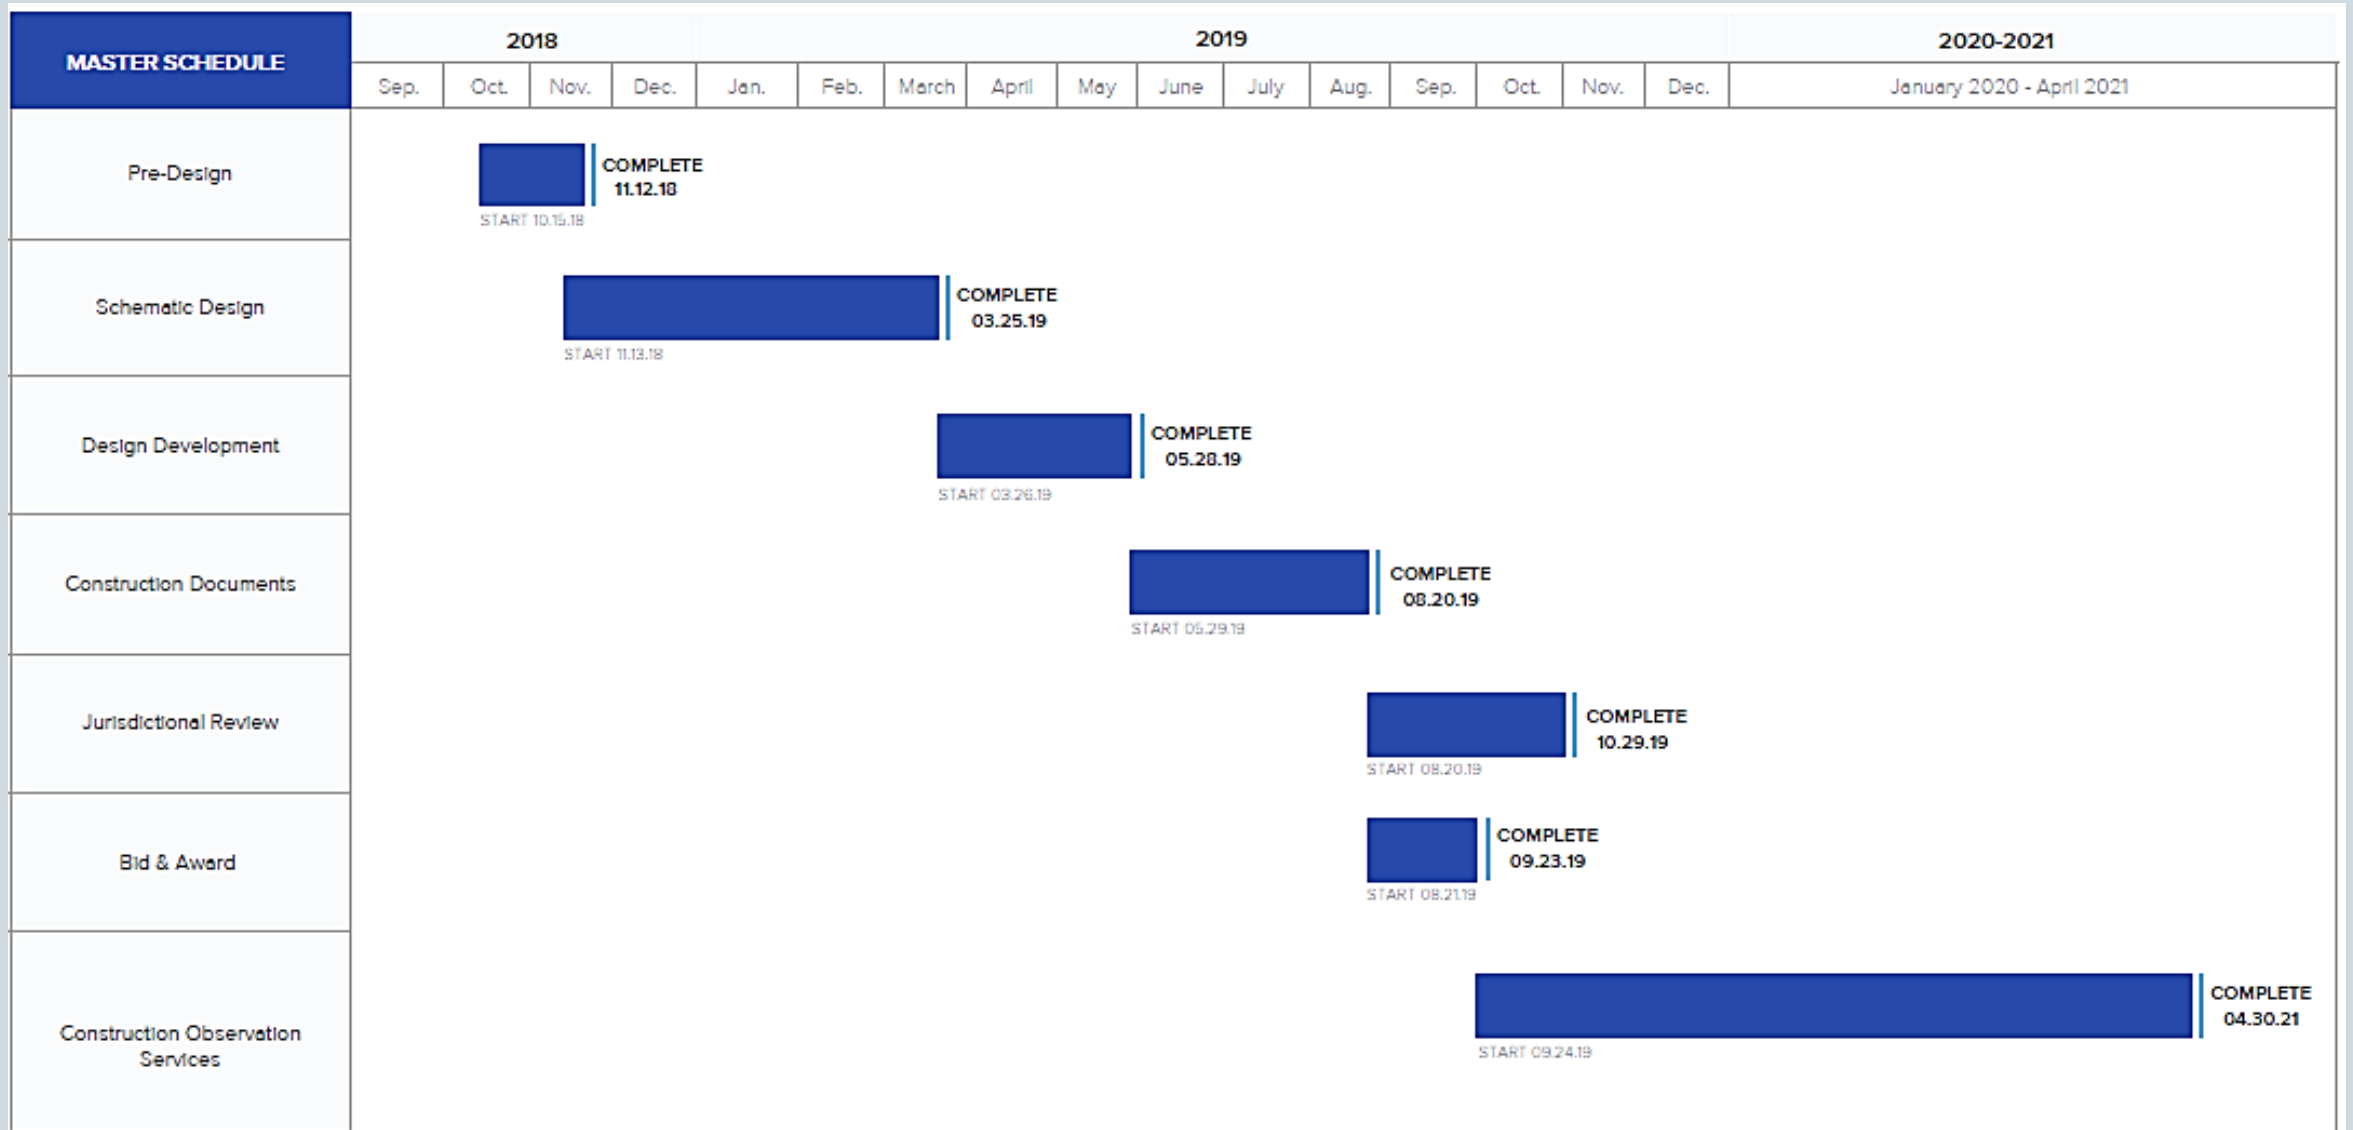

Hal Peterson Middle School – Next Steps

- May 14th Annexation 1st Reading Approved by City Council
- May 28th Annexation 2nd and Final Reading Approved by City Council
- June 4th Meeting to Review Cost Estimate with Architect and CM&R
- June 6th City Planning & Zoning Approved Preliminary and Final Plat (3175 Loop 534)
- June 18th Local Sub Contractor Outreach Event 2pm @ Tivy HS
- July 19th Huckabee-Inc. to Provide Construction Documents to Bartlett Cocke
- August 20th Bid Opening
- September 16th GMP for Board Approval



EXTERIOR IMAGES



KERRVILLE INDEPENDENT SCHOOL DISTRICT

DRAFT COPY ONLY
NOT FOR REGULATORY APPROVAL, PERMITTING, OR CONSTRUCTION.



KERRVILLE INDEPENDENT SCHOOL DISTRICT


DRAFT COPY ONLY
NOT FOR REGULATORY APPROVAL, PERMITTING, OR CONSTRUCTION.




KERRVILLE INDEPENDENT SCHOOL DISTRICT

DRAFT COPY ONLY
NOT FOR REGULATORY APPROVAL, PERMITTING, OR CONSTRUCTION.

INTERIOR IMAGES

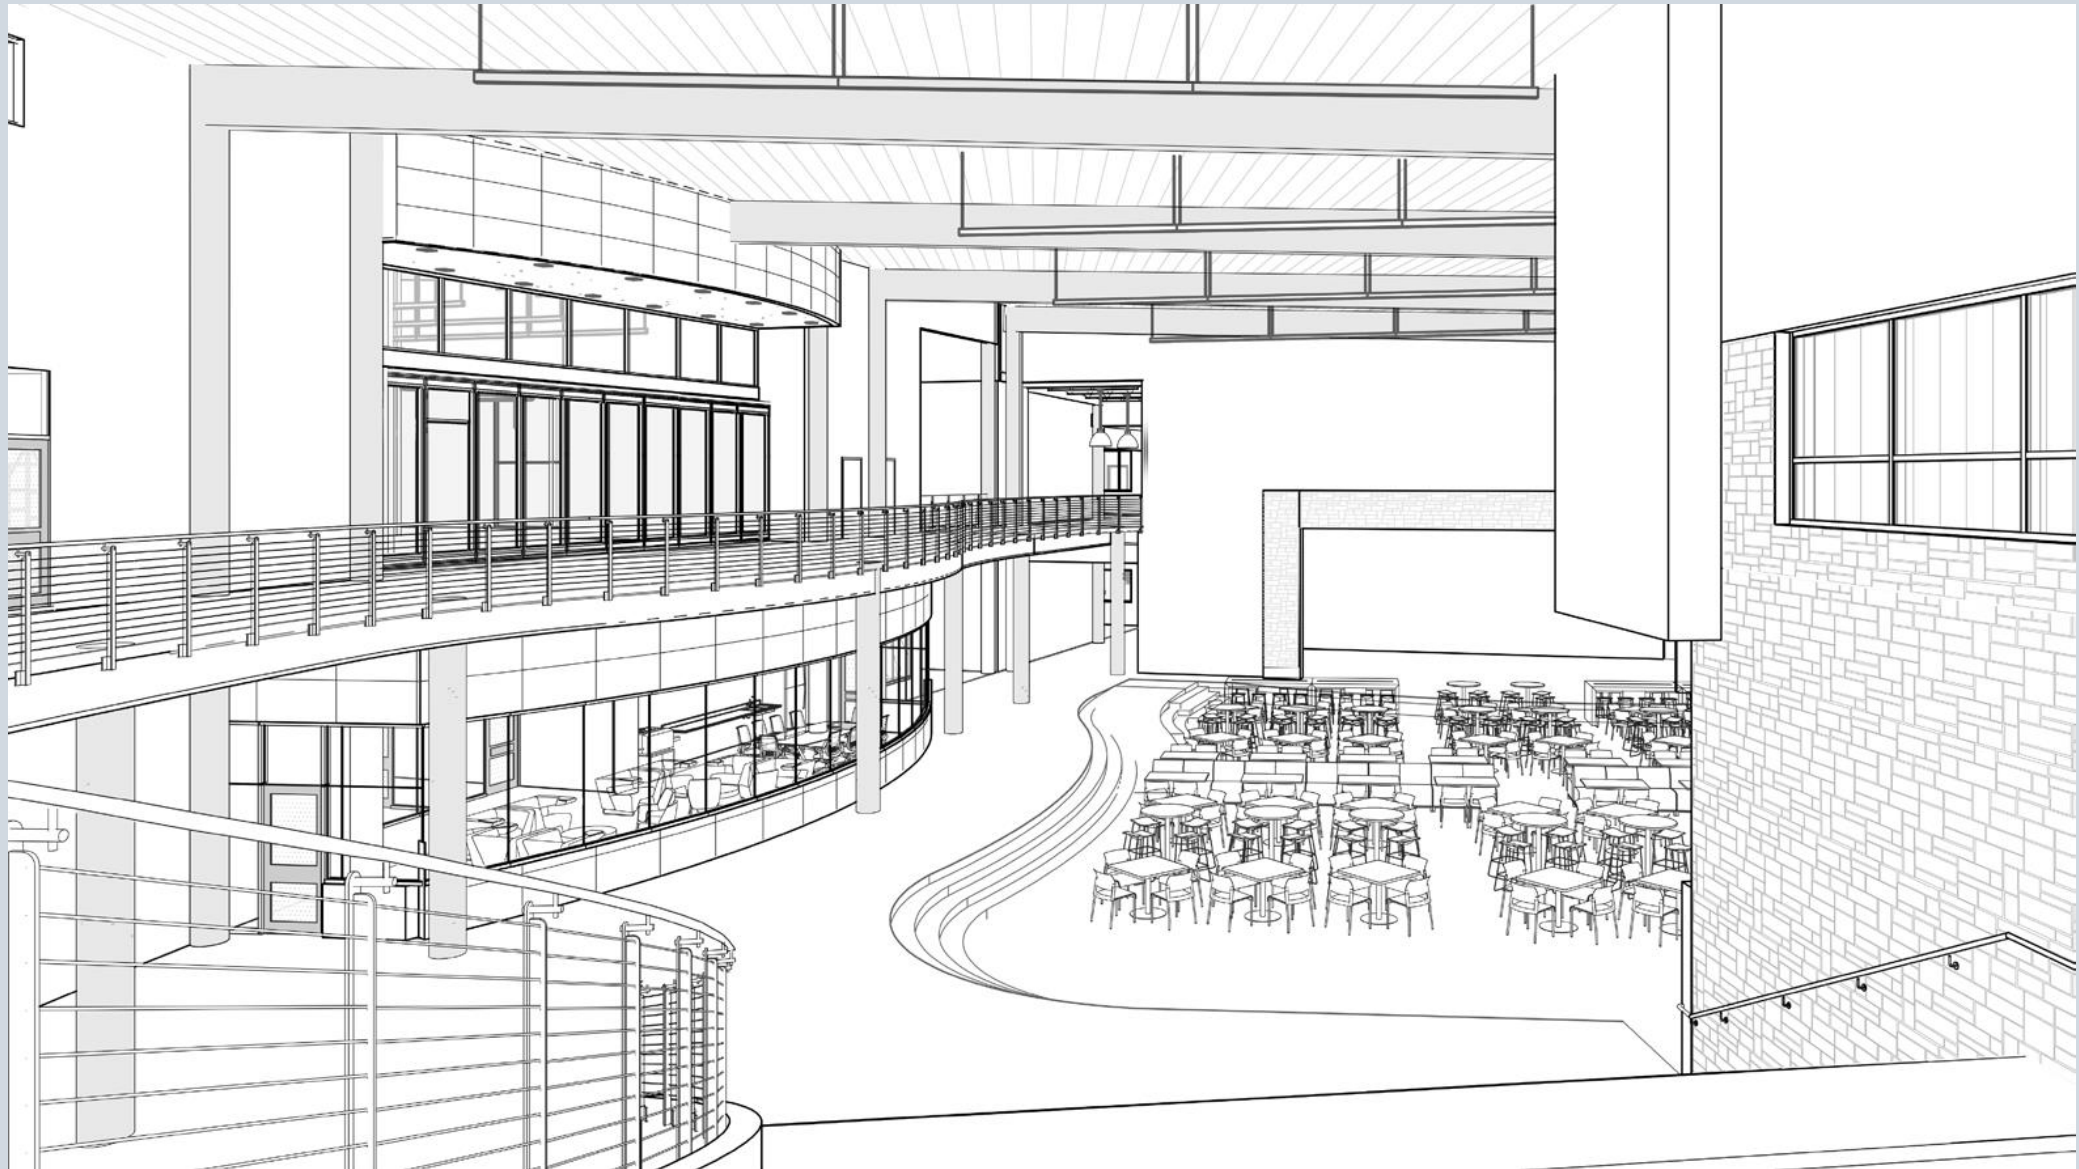



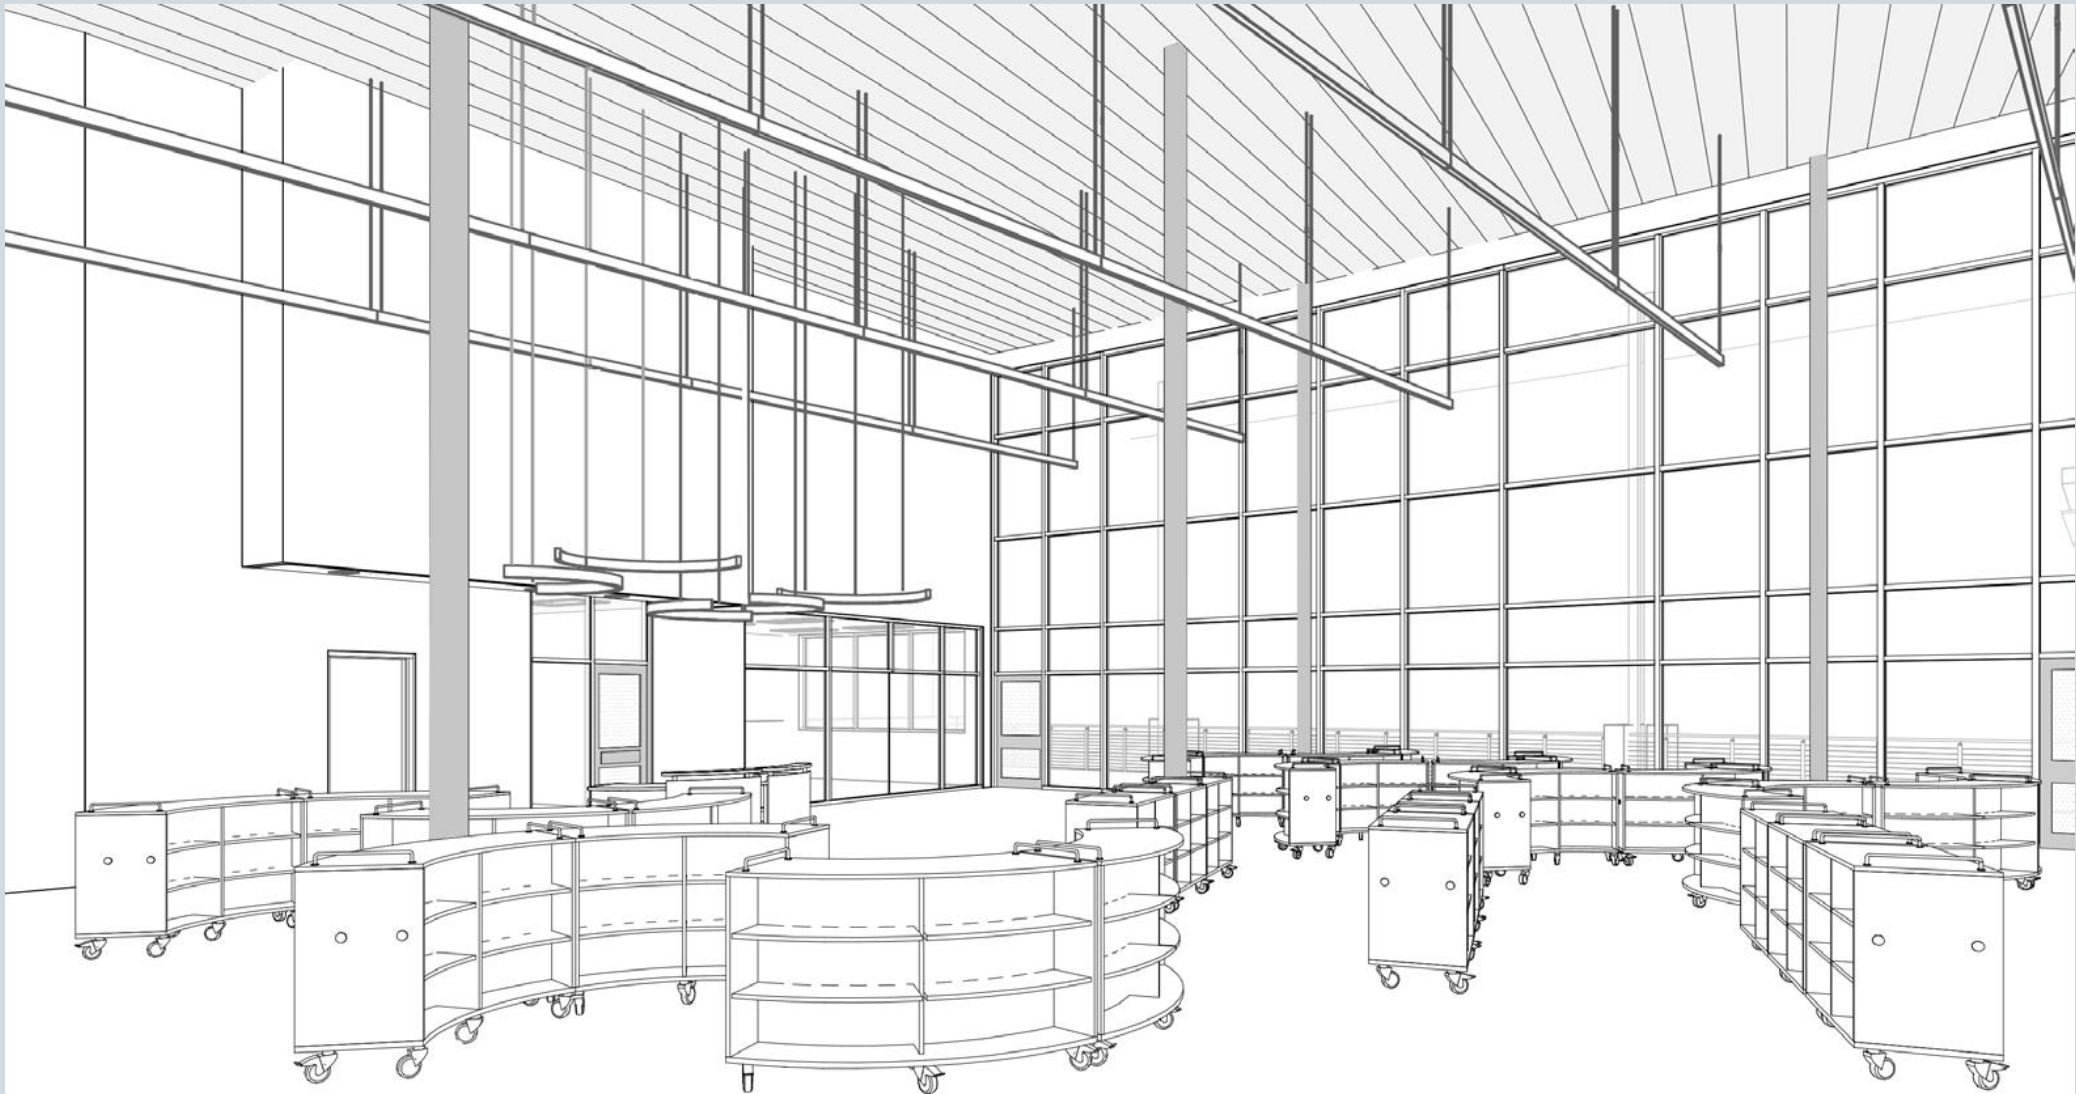





KERRVILLE INDEPENDENT SCHOOL DISTRICT

DRAFT COPY ONLY
NOT FOR REGULATORY APPROVAL, PERMITTING, OR CONSTRUCTION.

More Information To Come

