




Project Highlights

June 18, 2020

2020

Projects

2020 Bond Projects

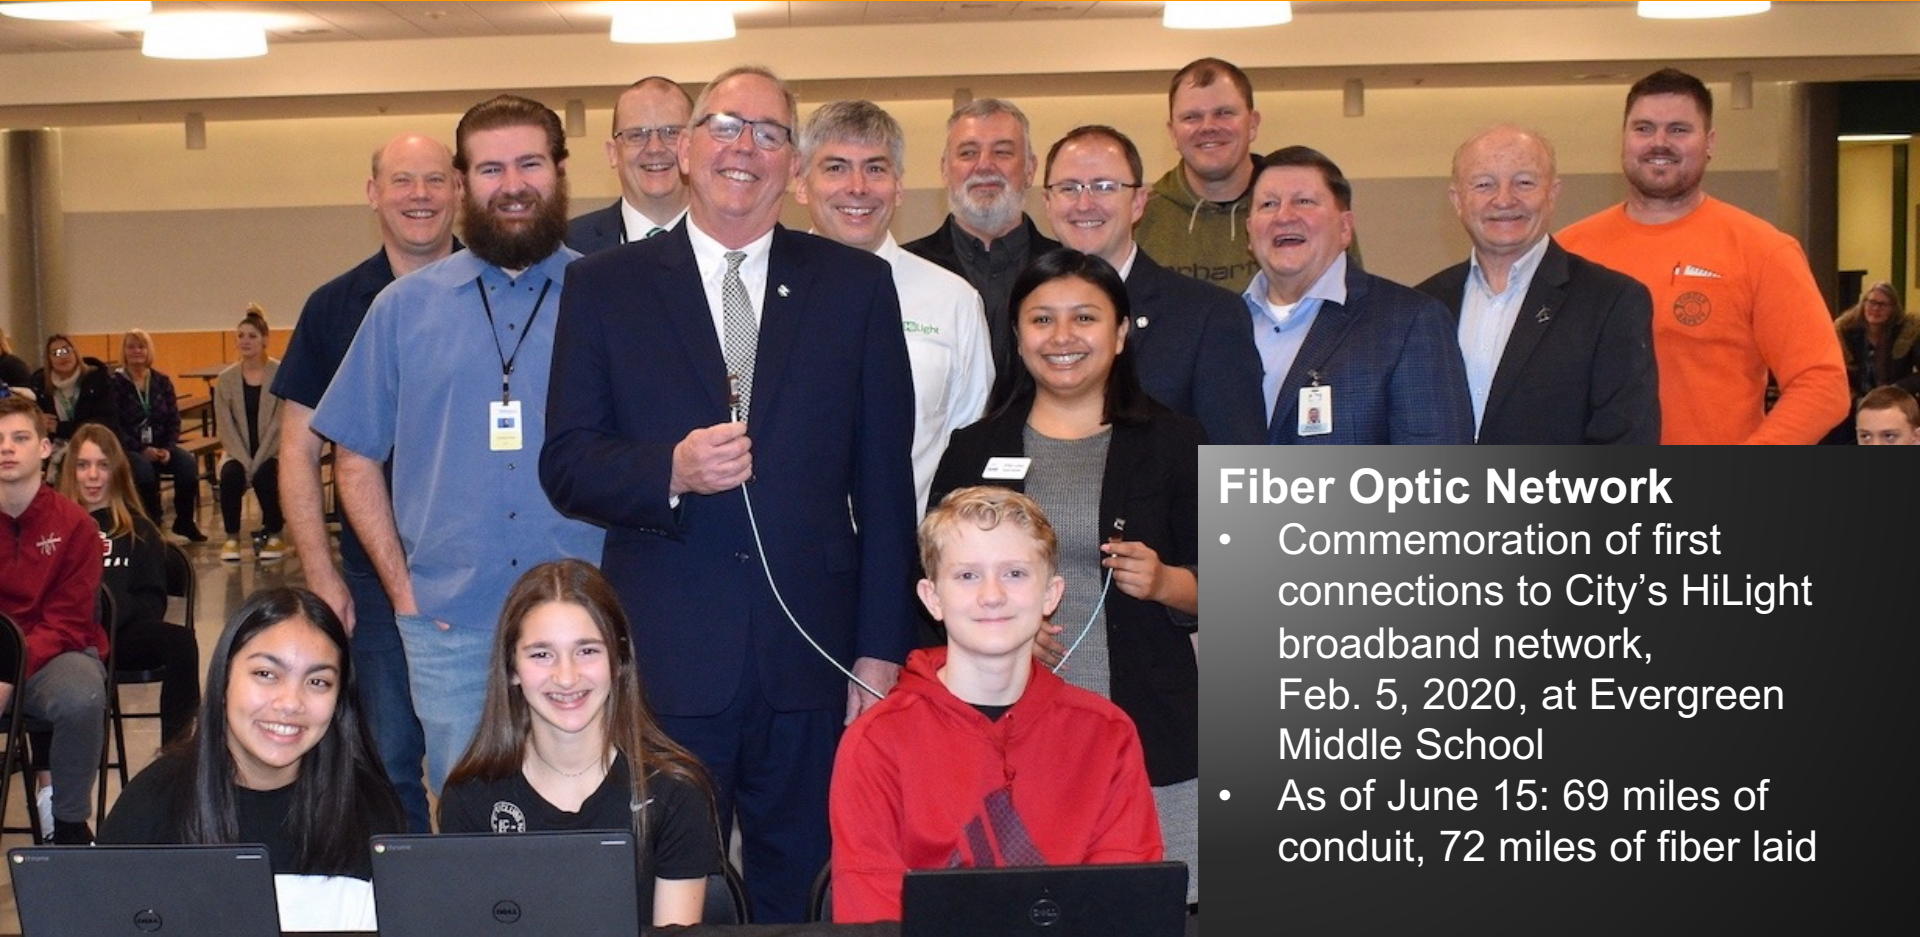

Fiber Optic Network

- Commemoration of first connections to City's HiLight broadband network, Feb. 5, 2020, at Evergreen Middle School
- As of June 15: 69 miles of conduit, 72 miles of fiber laid

2020 Bond Projects



Brookwood Elementary

- Replacement school
- Completion August 2020
- Watch [video update](#)

as of June 16, 2020



2020 Bond Projects



Butternut Creek Elementary

- Domestic water pipe replacement
- Completion August 2020

as of June 16, 2020

2020 Bond Projects



Eastwood Elementary

- New gym: grand opening, Feb. 4, 2020
- Security upgrades: June 2020
- Roofing: summer



2020 Bond Projects

W.L. Henry Elementary

- April-Dec. 2020: New gymnasium
- May-Aug. 2020:
 - Parent/bus dropoff improvements
 - Water line upgrades
 - Roofing upgrades

as of June 15, 2020




2020 Bond Projects



Indian Hills Elementary

- HVAC upgrades – add air conditioning
- Seismic upgrades
- Add ADA-accessible restroom
- 3-classroom modular building
- Completion August 2020

as of June 16, 2020

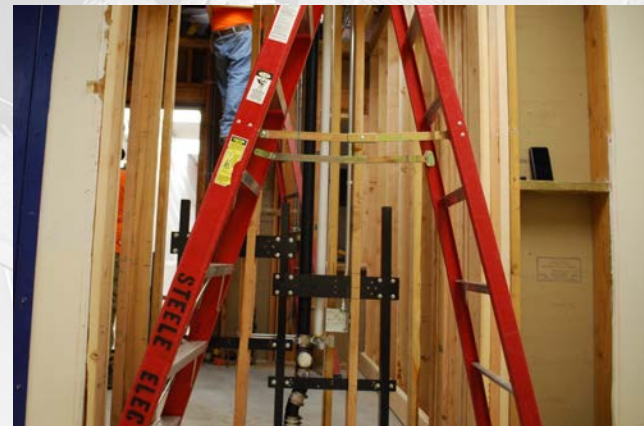

2020 Bond Projects



Minter Bridge Elementary

- 2-classroom modular building: May – Aug. 2020
- New gym: May 2020 – Jan. 2021
- Summer 2020:

Seismic upgrades
Roofing upgrades
Add heating to existing HVAC

as of June 15, 2020

2020 Bond Projects



Mooberry Elementary

- New gym: grand opening March 9, 2020
- New playground: completed March 30, 2020




2020 Bond Projects

North Plains Elementary

- New gym: roofing and exterior panels being installed
- Parent/bus dropoff: started June 2020
- Both projects complete by August 2020
- Watch [video update](#)

as of June 9-15, 2020

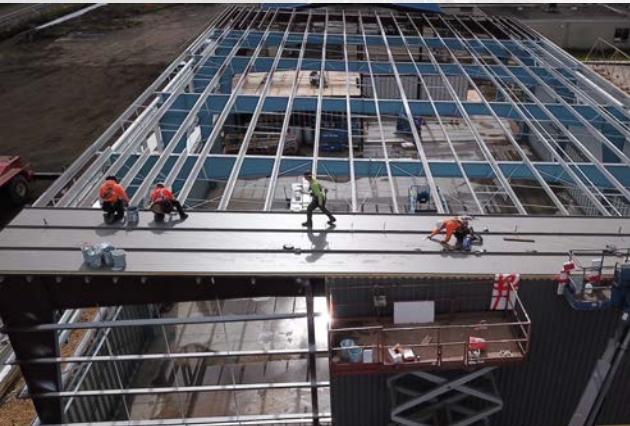

2020 Bond Projects

New Elementary School #28 in North Plains

- Concrete being poured into forms, trenching for utilities
- Complete by August 2021

as of June 8 and 15, 2020



2020 Bond Projects



New Gymnasiums

- Ladd Acres Elementary
Oct. 2020-Aug. 2021
- McKinney Elementary
Oct. 2020-Aug. 2021



2020 Bond Projects



Brown Middle School

- May-Aug. 2020
- Phase 2 of renovations including office switch-out, entry vestibule, roofing, and HVAC

as of June 9-16, 2020




2020 Bond Projects



Evergreen Middle School

- New 18,000 sq. ft. wing with media center and six classrooms
- Completed in April 2020
- Watch [virtual tour](#)

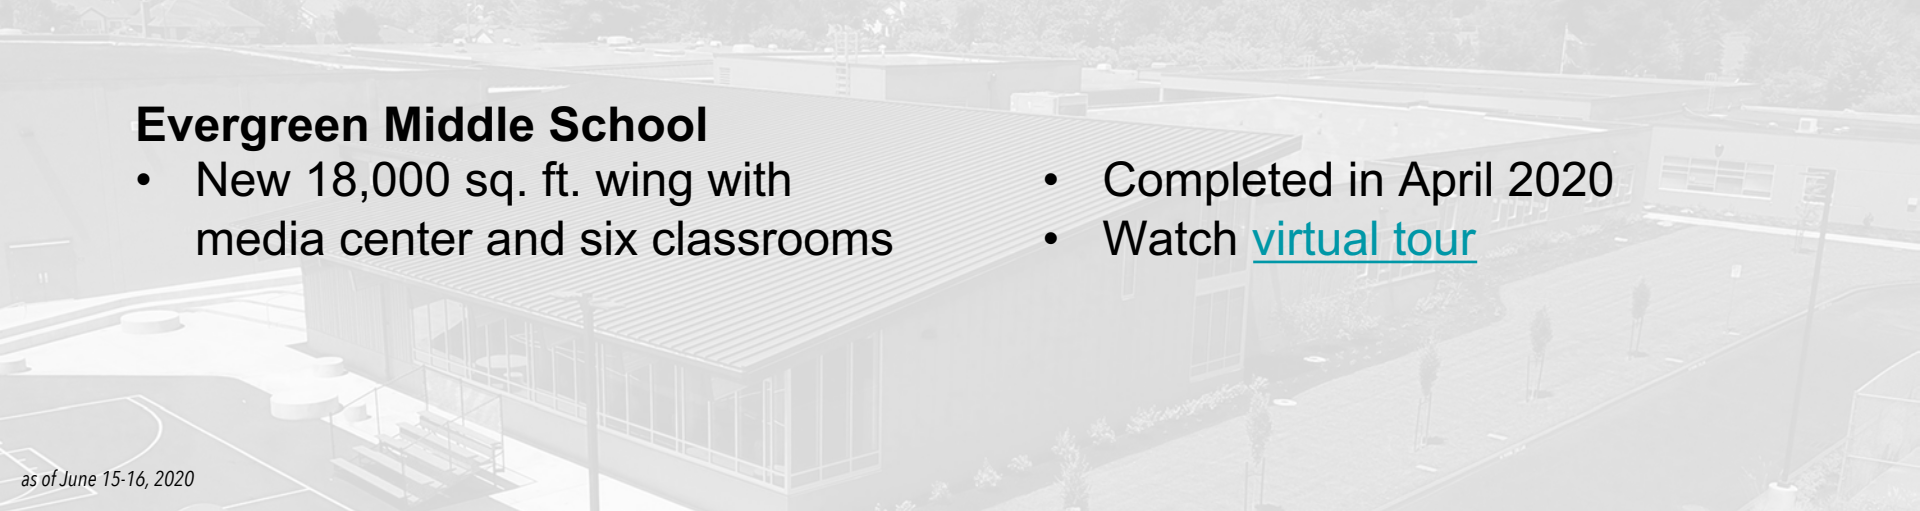

as of June 15-16, 2020



2020 Bond Projects



Glencoe High School

- New addition and front entry wing
- Cafeteria/commons expansion
- Improvement to north/student parking lot
- 2nd-floor renovations
- Half-street improvement to Glencoe Road with traffic signal
- Construction trades CTE space
- New weight and team rooms (completed)
- Watch [video update](#)

as of June 16, 2020



2020 Bond Projects



Hillsboro High School

- Auto tech expansion
 - Commons renovations
 - Parking lot improvements (portables removed)
- Completed:
Fire access road; seismic and HVAC renovations, including academic buildings and front office

as of June 15, 2020



2020 Bond Projects



Transportation & Support Services Facility

- 47,000 sq. ft. building
- Parking for 100 school buses

aerial as of June 3, 2020; other photos June 15, 2020



2020 Bond Projects



Roofing

- Eastwood Elementary
- Imlay Elementary
- Century High School
- Liberty High School
- Miller/Hillsboro Big Picture (complete)



Learn more...

You can follow the progress of the Hillsboro School District 2017 Bond at:

www.Hillsboro-Bond.org

or contact:

Adam Stewart, Capital Projects Officer,
stewart@hsd.k12.or.us or 503-844-1340

Jane Siguenza, Bond Marketing Specialist,
siguenzj@hsd.k12.or.us or 503-844-1761

