



WAUNAKEE COMMUNITY SCHOOL DISTRICT DESIGN AND CONSTRUCTION UPDATE

WORKING TOGETHER for a STRONG FUTURE



Vol. 10 | MAY 2024

HERITAGE ELEMENTARY CONSTRUCTION

Work at the new Heritage Elementary School site is really picking up. Curbs, concrete sidewalks, and the asphalt paving has begun! Metal panels are being installed on the east and west sides of the buildings, as well as in the courtyard. The roof metal work will be installed after the panels are completed.

The inside of the building is progressing well, too. The flooring work is finished in the early childhood/kindergarten, first grade, and second grade areas. Painting and wall coverings on the first floor are about 80% completed. Acoustic and specialty ceilings are being installed after the painting. Elevators are in place. The mechanical, electrical, and plumbing work on the first floor is nearly complete.

The drywall work on the second floor of the building is almost completed. The mechanical, electrical, plumbing, and fire protection teams are completing their tasks and have started the finish work in the third and fourth grade classrooms. The painters are also working on the second floor, completing ceiling and wall painting. Network cabling, access control systems, security systems, and clocks are all being installed throughout the building.

DID YOU KNOW?

Over 2,100 gallons of paint and 26 different paint colors will be used over the course of the project. That is enough to fill a 12' circular swimming pool!

UPCOMING MILESTONES



Wednesday, May 29
Neighborhood Town Hall



Friday, June 7
Last Day for Students in old building



Monday, June 17
Public School Surplus Sale



Tuesday, September 3
First Day of School



Sunday, October 6
Ribbon Cutting at new Heritage Elementary School



Carpeting - Early Childhood/Kindergarten Wing

For questions about the facilities design/construction process:

www.waunakee.k12.wi.us/community/fall-2022-referendum

wcsd_fall2022@waunakee.k12.wi.us

608.849.2000 - ext. 8491



VOGEL
BROS. BUILDING CO.



WAUNAKEE COMMUNITY SCHOOL DISTRICT DESIGN AND CONSTRUCTION UPDATE



Heritage Last Look



Heritage Elementary



Heritage Last Look

HERITAGE LAST LOOK

Thank you to everyone who attended the Community Last Look Open House events at Heritage Elementary School. The Waunakee Community School District held a series of Community Last Look Open House events at Heritage Elementary in April 2024, including one on April 15 specifically for retired staff, and another on April 22 for students, staff, families, and community members.



Heritage Last Look



Engineering Class Tour




Heritage Last Look

LOCAL PARTNER SPOTLIGHT

Hooper is a well-respected Mechanical and Electric Power Contractor that has been serving customers like Waunakee Community School District for more than 110 years. Hooper's Mechanical areas of expertise include fabrication and installation of complex plumbing, HVAC, building automation, fire protection, and process piping systems.

Hooper's core values include Safety, Respectful Collaboration, Outstanding Craftsmanship, and Community Engagement. Living and working under these guiding principles is what makes Hooper a preferred partner for the Waunakee Community School District construction projects and the community as a whole.

Hooper's Mechanical Division has been a significant partner in helping the district meet the needs of students and the community. Current projects include the collaborative project delivery of the plumbing for the new Heritage Elementary, new Middle School, and Waunakee High School remodeling.

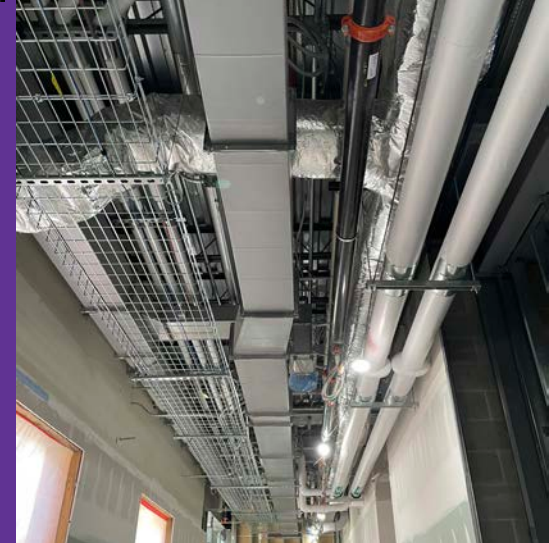

For questions about the facilities design/construction process:

www.waunakee.k12.wi.us/community/fall-2022-referendum

wcsd_fall2022@waunakee.k12.wi.us

608.849.2000 - ext. 8491

